



Job Name: 26-2080 - The Cumberland Job Location: Bowling Green, KY Contractor: J & J Concrete & Excavating, LLC					Plant: 100 6/22/2026 6:25:17 PM		Tech: Jared - A PC: E. Bradley				
Structure ID: B1 SS-MH											
P2 MH048RS48			MH RISER T/G								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 24" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE Custom Ht T/n - 22" 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0285 7) MH Step ML-10-TDS-NCR - 10"						0 lb 1550 lb 3353 lb 2804 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb 0 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS AT 0 DEGREES 5. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY ICAST			
Rim: 531.9' Rim to Invert: 8.46' Slack: 2.52" Sump: 2" Step Position: 0°						Structure Total: 9420 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

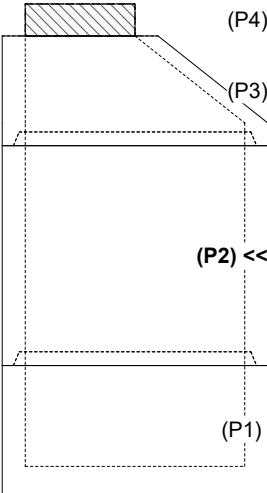


(P4)
(P3)
(P2) <<
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

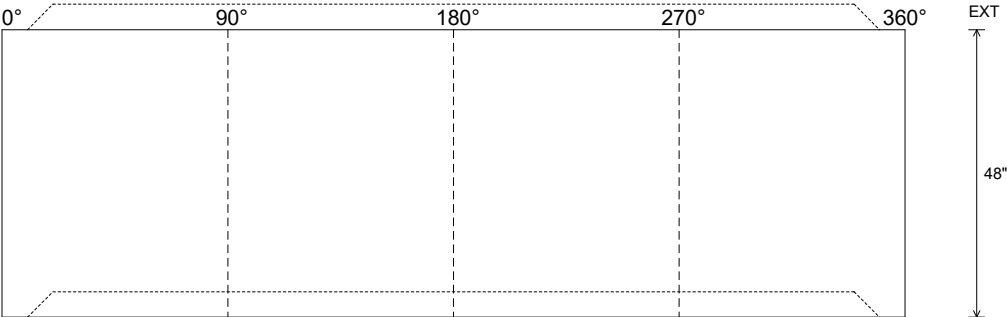

(P2)

48"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
----------------------------------	------------------------------------	--	--	--
