



Job Name: 26-2080 - The Cumberland Job Location: Bowling Green, KY Contractor: J & J Concrete & Excavating, LLC					Plant: 100 6/22/2026 6:23:33 PM		Tech: Jared - A PC: E. Bradley				
Structure ID: B2 SS-MH											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 24" P1) 48" - MH BASE Custom Ht T/n - 45" 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) A-Lok - 0285 8) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 1677 lb 4379 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 0 lb 3 lb 0 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY ICAST				
Structure Total: 9820 lb											
Rim: 533.35' Rim to Invert: 8.82' Slack: 1.84" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	524.53'	0°	0"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	1.125"	0"	
Invert 2	524.63'	90°	45.5"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	2.375"	0"	
Invert 3	526.43'	270°	136.625"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	23.875"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

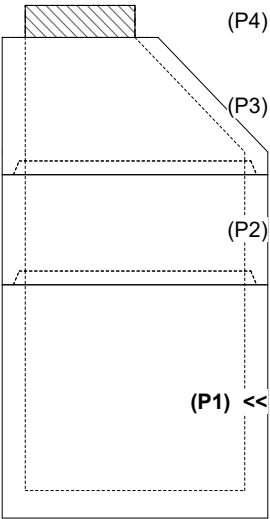

UPSIDE-DOWN VIEW (int. dimenions)

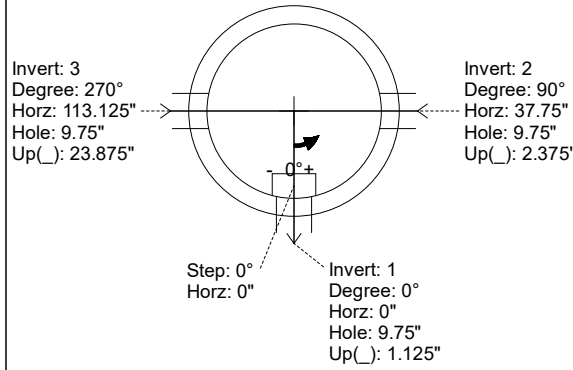

INSIDE WALL DIMENSIONS

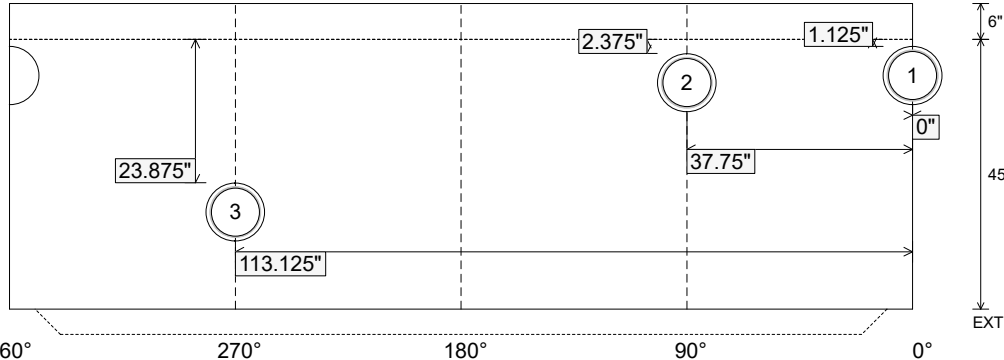

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 45" Height (Ext): 51"	Weight (Net): 4379 lb Volume (Net): 1.12cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2080 - The Cumberland Job Location: Bowling Green, KY Contractor: J & J Concrete & Excavating, LLC					Plant: 100 6/22/2026 6:23:33 PM		Tech: Jared - A PC: E. Bradley						
Structure ID: B2 SS-MH													
P1 MH048BAVF		MH BASE Custom Ht T/n											
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 24" P1) 48" - MH BASE Custom Ht T/n - 45" 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) A-Lok - 0285 8) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 1677 lb 4379 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 0 lb 3 lb 0 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY ICAST					Structure Total: 9820 lb	
Rim: 533.35' Rim to Invert: 8.82' Slack: 1.84' Sump: 2' Step Position: 0°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	524.53'	0°	0"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	1.125"	0"			
Invert 2	524.63'	90°	45.5"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	2.375"	0"			
Invert 3	526.43'	270°	136.625"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	23.875"	0"			
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													

(P4)

(P3)

(P2)

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

Invert: 2
Degree: 90°
Horz: 37.75"
Hole: 9.75"
Up(): 2.375"

Invert: 3
Degree: 270°
Horz: 113.125"
Hole: 9.75"
Up(): 23.875"

Step: 0°
Horz: 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 9.75"
Up(): 1.125"

UPSIDE-DOWN VIEW (int. dimensions)

INVERT CHANNEL
DRAWING

INSIDE WALL DIMENSIONS

23.875"

113.125"

23.875"

37.75"

1.125"

2.375"

360°

270°

180°

90°

0°

6"

45"

EXT

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 45"
Height (Ext): 51"

Weight (Net): 4379 lb
Volume (Net): 1.12cu.yd
