



Job Name: 26-2080 - The Cumberland Job Location: Bowling Green, KY Contractor: J & J Concrete & Excavating, LLC					Plant: 100 6/22/2026 6:23:25 PM		Tech: Jared - A PC: E. Bradley				
Structure ID: C2 ST-CI											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 40" 1) CASTING - HOE 525 SET (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 30 3) MH Step ML-10-TDS-NCR - 10"						0 lb 1300 lb 3493 lb 442 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 5235 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS AT 63 DEGREES 5. HOE 525 FRAME, FLAT GRATE, & CURB HOOD SUPPLIED BY ICAST			
Rim: 531.24' Rim to Invert: 4.8' Slack: 1.5" Sump: 1.9" Step Position: 63°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (°)	Offset	
Invert 1	526.44'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"	
Invert 2	526.44'	197°	99.75"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

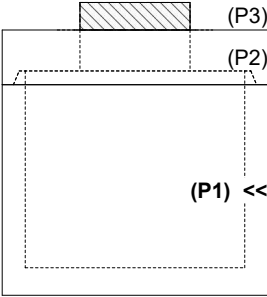


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

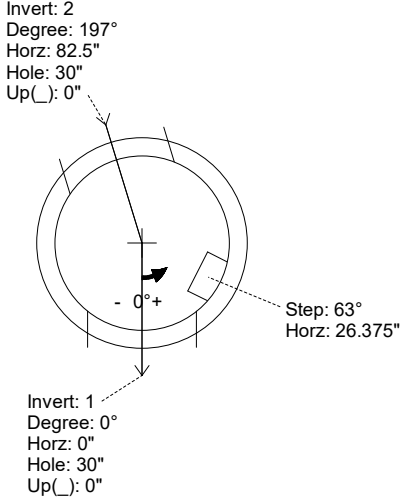

INSIDE WALL DIMENSIONS

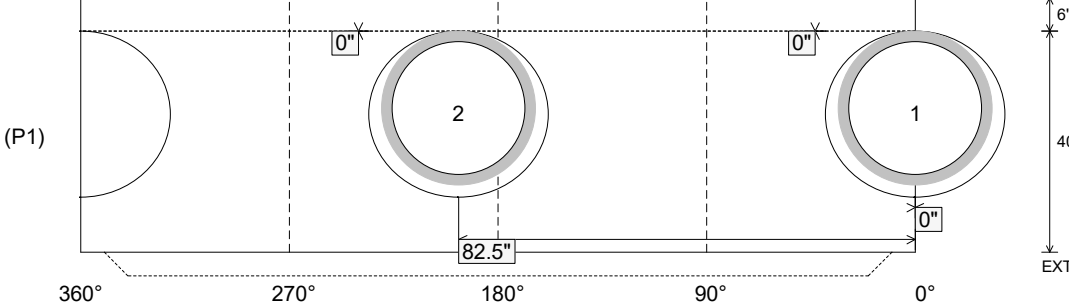

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 40" Height (Ext): 46"	Weight (Net): 3493 lb Volume (Net): 0.89cu.yd
----------------------------------	---------------------------------	--	--	--
