


Job Name: 26-2080 - The Cumberland
Job Location: Bowling Green, KY
Contractor: J & J Concrete & Excavating, LLC

Plant: 100

6/22/2026 6:26:02 PM

Tech: Jared - A

PC: E. Bradley



Structure ID: C4 ST-CI

P2 MH048LD12-24X36RECT



MH FLAT TOP w/24"x36" Hole F/G

- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12"
P1) 48" - MH BASE T/n - 42"
1) CASTING - HOE 525 SET (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 30
3) MH Step ML-10-TDS-NCR - 10"

0 lb
1300 lb
3632 lb
442 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 5374 lb

Structure Notes:

1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #4 BAR @ 10" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE 525 FRAME, FLAT GRATE, & CURB HOOD SUPPLIED BY ICAST
5. LIFTERS: 4 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
6. TOP SURFACE TO RECEIVE FLOATED FINISH

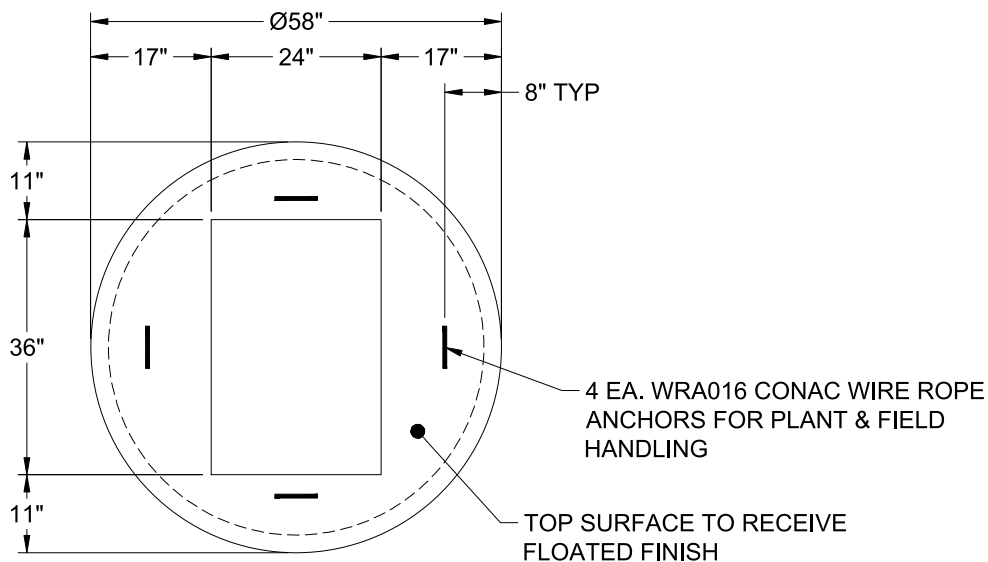

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1300 lb
Volume (Net): 0.46cu.yd
