

Job Name: 26-2080 - The Cumberland
Job Location: Bowling Green, KY
Contractor: J & J Concrete & Excavating, LLC

Plant: 100

6/22/2026 6:26:02 PM

Tech: Jared - A

PC: E. Bradley



Structure ID: C6 ST-MH

P2 MH048LD07ECC

MH FLAT TOP w/ 24" ECC Hole F/F



- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/F - 7"
P1) 48" - MH BASE Custom Ht F/n - 23"
1) CASTING - HOE MC-375 F/C Storm
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
1) DOGHOUSE INVRTD - 24"x23"
1) Hole - 20
2) MH Step ML-10-TDS-NCR - 10"

0 lb
1286 lb
2570 lb
271 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 4127 lb

Structure Notes:

1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #4 BAR @ 10" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE MC-375 FRAME & COVER "STORM" SUPPLIED BY ICAST
5. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
6. TOP SURFACE TO RECEIVE FLOATED FINISH

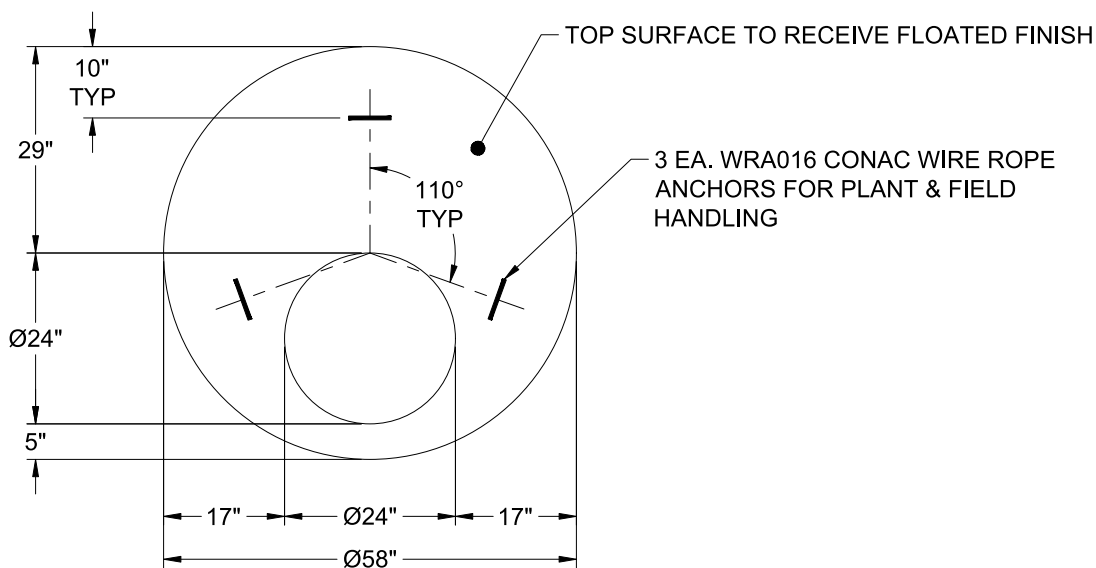

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 5"

Height (Ext): 7"

Weight (Net): 1286 lb
Volume (Net): 0.33cu.yd
