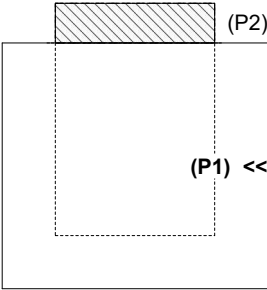

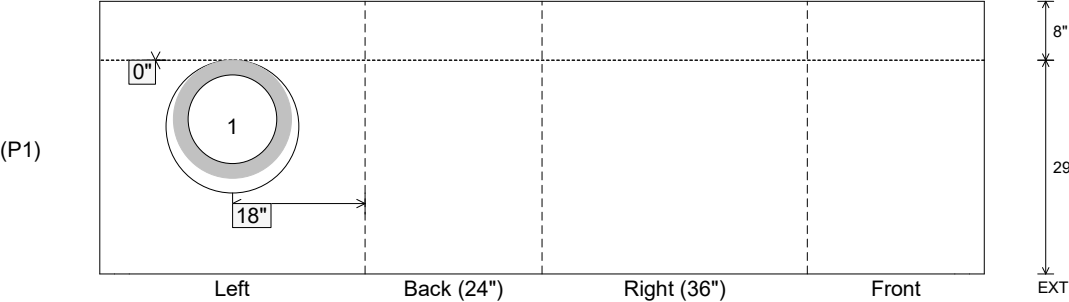


Job Name: 26-2104 - Jeffersonville High School Parking Lot Job Location: Jeffersonville, IN Contractor: Mac Construction & Excavating, Inc.					Plant: 100 6/27/2026 7:12:44 PM		Tech: Jared - A PC: T. Lewis				
Structure ID: 15 ST-CI											
P1 BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht F/n									
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 29" 1) CASTING - HOE 525 SET (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18					0 lb 4185 lb 442 lb 0 lb 0 lb ----- Structure Total: 4627 lb		<u>Structure Notes:</u> 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. STORM INVERT BY OTHERS 5. HOE 525 FRAME, GRATE, & CURB HOOD SUPPLIED BY OTHERS				
Rim: 482'		Rim to Invert: 2.88'		Slack: 1.56"		Sump: 2"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	479.12'	270°	26"	12" RCP B WALL	16"	Hole 18	18"	18"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 29" Height (Ext): 37"		Weight (Net): 4185 lb Volume (Net): 1.07cu.yd		
