

Job Name: 26-2104 - Jeffersonville High School Parking Lot

Job Location: Jeffersonville, IN

Contractor: Mac Construction & Excavating, Inc.

Plant: 100

6/27/2026 7:12:45 PM

Tech: Jared - A

PC: T. Lewis



Structure ID: 17 ST-CI

P1 BX2436-08BVF

BOX BASE 8inW, 8inF, Variable Ht F/n

P2) 24" x 36" - CASTING HEIGHT - 6"

P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 29"

1) 24" x 36" - Conseal CS-102 1.00"

1) Hole - 18

0 lb

4185 lb

0 lb

0 lb

0 lb

Structure Total: 4185 lb

Structure Notes:

1. PER ASTM C-913 SPECIFICATIONS

2. CONCRETE: 4,000 PSI AT 28 DAYS

3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)

4. STORM INVERT BY OTHERS

5. HOE 525 FRAME, GRATE, & CURB HOOD SUPPLIED BY OTHERS

Rim: 482.49'

Rim to Invert: 2.87'


Slack: 1.44"

Sump: 2"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	479.62'	270°	26"	12" RCP B WALL	16"	Hole 18	18"	18"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

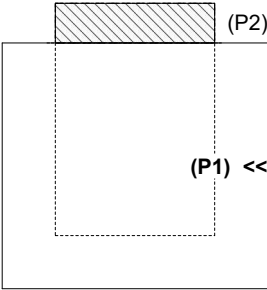

UPSIDE-DOWN VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

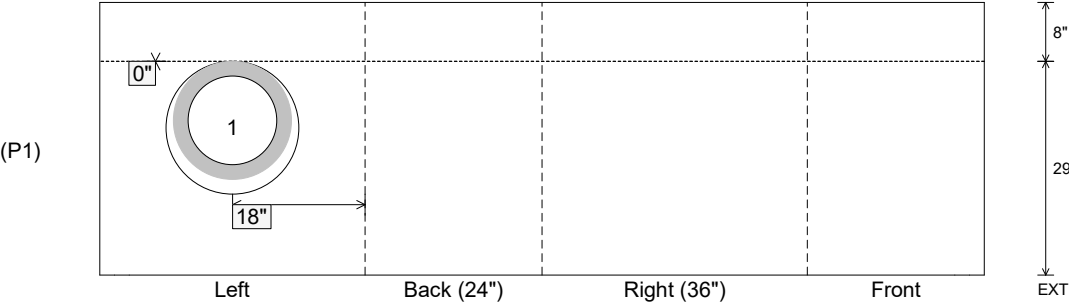

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 29"

Height (Ext): 37"

Weight (Net): 4185 lb

Volume (Net): 1.07cu.yd
