

Job Name: 26-2104 - Jeffersonville High School Parking Lot Job Location: Jeffersonville, IN Contractor: Mac Construction & Excavating, Inc.	Plant: 100	Tech:	Jared - A	
	6/27/2026 7:13:18 PM	PC:	T. Lewis	
Structure ID: 23 ST-CI				
P2 MH048LD07-24X36RECT		MH FLAT TOP w/24"x36" Hole F/F		



P3) 24" x 36" - CASTING HEIGHT - 6"
 P2) 48" - MH FLAT TOP w/24"x36" Hole F/F - 7"
 P1) 48" - MH BASE Custom Ht F/n - 21"
 1) 48" - Conseal CS-102 1.00"
 1) 24" x 36" - Conseal CS-102 1.00"
 2) Hole - 18

0 lb
 1044 lb
 2509 lb
 0 lb
 0 lb
 0 lb

 3553 lb

Structure Total:

- Structure Notes:
- PER ASTM C-478 SPECIFICATIONS
 - CONCRETE: 4,000 PSI AT 28 DAYS
 - REINFORCEMENT: #4 BAR @ 10" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
 - HOE 525 FRAME, GRATE, & CURB HOOD SUPPLIED BY OTHERS
 - LIFTERS: 4 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
 - TOP SURFACE TO RECEIVE FLOATED FINISH

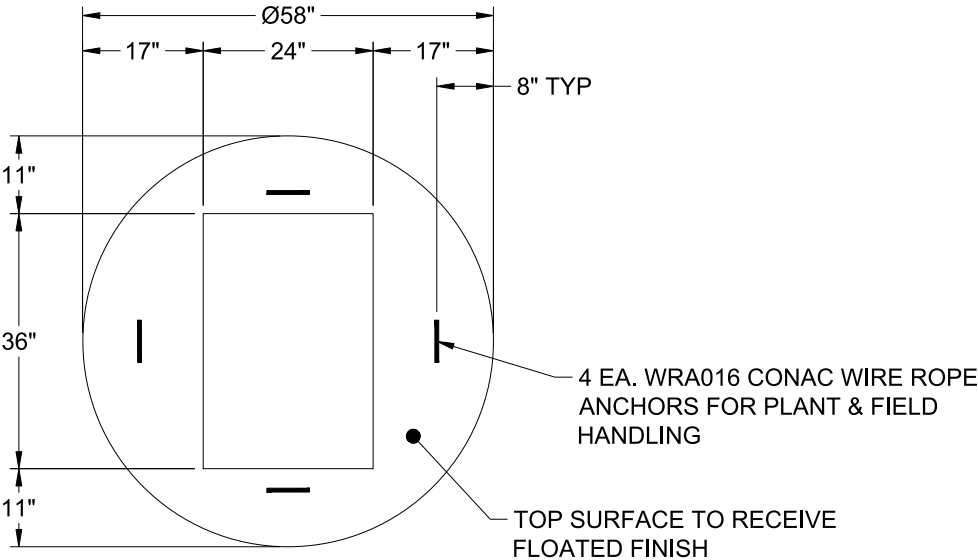

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 5"	Height (Ext): 7"	Weight (Net): 1044 lb Volume (Net): 0.27cu.yd
----------------------------------	--------------------------------	--------------------	------------------	--
