
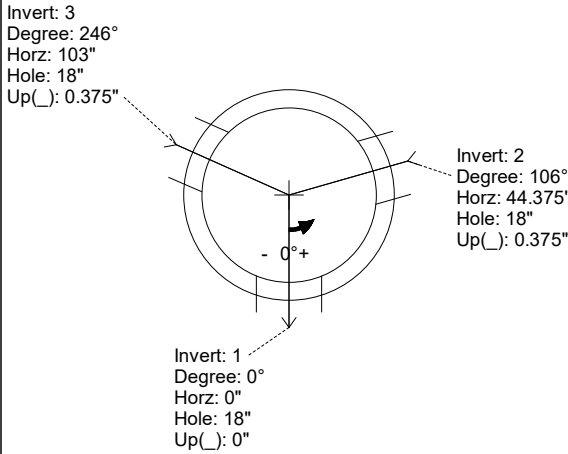
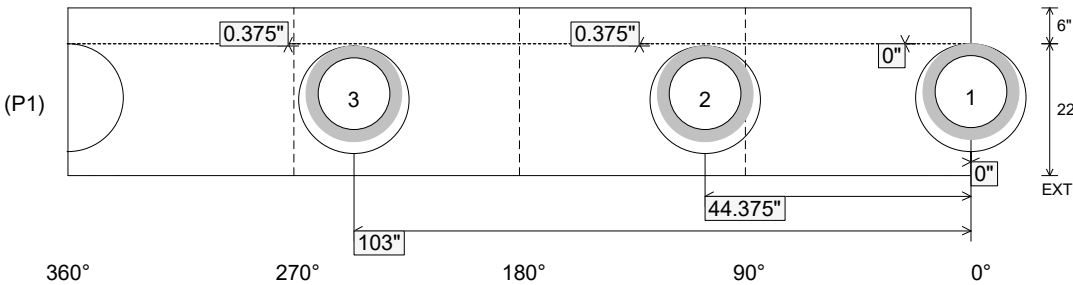


Job Name: 26-2104 - Jeffersonville High School Parking Lot Job Location: Jeffersonville, IN Contractor: Mac Construction & Excavating, Inc.					Plant: 100 6/27/2026 7:12:36 PM		Tech: Jared - A PC: T. Lewis				
Structure ID: 7 ST-CI											
P1 MH048BAVF		MH BASE Custom Ht F/n									
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 22" 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 3) Hole - 18"					0 lb 1044 lb 2475 lb 0 lb 0 lb 0 lb Structure Total: 3519 lb		<u>Structure Notes:</u> 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STORM INVERT BY OTHERS 5. NO STEPS 6. HOE 525 FRAME, GRATE, & CURB HOOD SUPPLIED BY OTHERS				
Rim: 483.85' Rim to Invert: 2.83' Slack: 0.96" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	481.02'	0°	0"	12" RCP B WALL	16"	Hole 18	18"	18.451"	0"	0"	
Invert 2	481.05'	106°	53.625"	12" RCP B WALL	16"	Hole 18	18"	18.451", 11.466"	0.375"	0"	
Invert 3	481.05'	246°	124.5"	12" RCP B WALL	16"	Hole 18	18"	18.451"	0.375"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions) INSIDE WALL DIMENSIONS											
  											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 22" Height (Ext): 28"		Weight (Net): 2475 lb Volume (Net): 0.63cu.yd		
