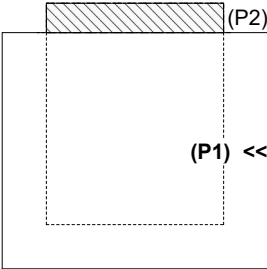

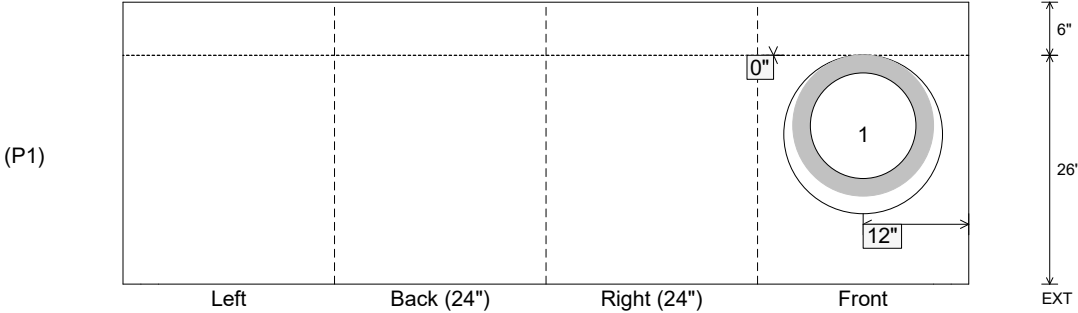


Job Name: 26-2104 - Jeffersonville High School Parking Lot Job Location: Jeffersonville, IN Contractor: Mac Construction & Excavating, Inc.					Plant: 100 6/27/2026 7:12:39 PM		Tech: Jared - A PC: T. Lewis				
Structure ID: 8 ST-CB											
P1 BX24240606VF		BOX BASE 6inW, 6inF, Variable Ht F/n									
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 6inW, 6inF, Variable Ht F/n - 26" 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 18					0 lb 2095 lb 0 lb 0 lb ----- 2095 lb Structure Total:		<u>Structure Notes:</u> 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. STORM INVERT BY OTHERS 5. HOE-326-BH FRAME & BEEHIVE GRATE SUPPLIED BY OTHERS				
Rim: 483.63' Rim to Invert: 2.47' Slack: 1.64" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	481.16'	0°	18"	12" RCP B WALL	16"	Hole 18	18"	18"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 6"		Height (Int): 26" Height (Ext): 32"		Weight (Net): 2095 lb Volume (Net): 0.54cu.yd		
