

Job Name: 26-2104 - Jeffersonville High School Parking Lot

Job Location: Jeffersonville, IN

Contractor: Mac Construction & Excavating, Inc.

Plant: 100

6/27/2026 7:12:36 PM

Tech: Jared - A

PC: T. Lewis



Structure ID: 9 ST-CB

P1 BX2424-06BA24

BOX BASE 6inW, 6inF F/n

P2) 24" x 24" - CASTING HEIGHT - 4"

P1) 24" x 24" - BOX BASE 6inW, 6inF F/n - 24"

1) 24" x 24" - Conseal CS-102 1.00"

1) Hole - 18

0 lb

1974 lb

0 lb

0 lb

1974 lb

Structure Total:

Structure Notes:

1. PER ASTM C-913 SPECIFICATIONS

2. CONCRETE: 4,000 PSI AT 28 DAYS

3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)

4. STORM INVERT BY OTHERS

5. HOE-326-BH FRAME & BEEHIVE GRATE SUPPLIED BY OTHERS

Rim: 483.37'

Rim to Invert: 2.21'


Slack: 0.52"

Sump: 2"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	481.16'	180°	18"	12" RCP B WALL	16"	Hole 18	18"	18"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

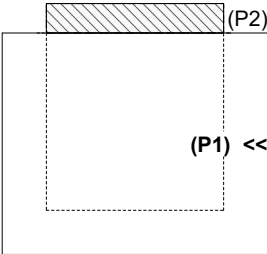

UPSIDE-DOWN VIEW (int. dimensions)

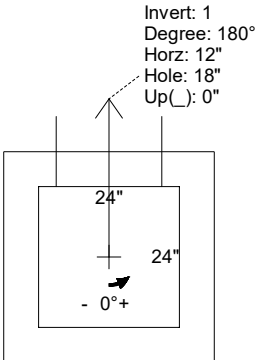

INSIDE WALL DIMENSIONS

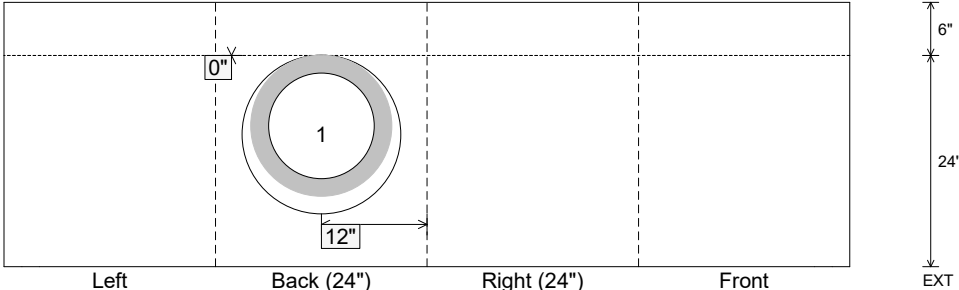

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 6"

Floor Height: 6"

Height (Int): 24"

Height (Ext): 30"

Weight (Net): 1974 lb

Volume (Net): 0.5cu.yd
