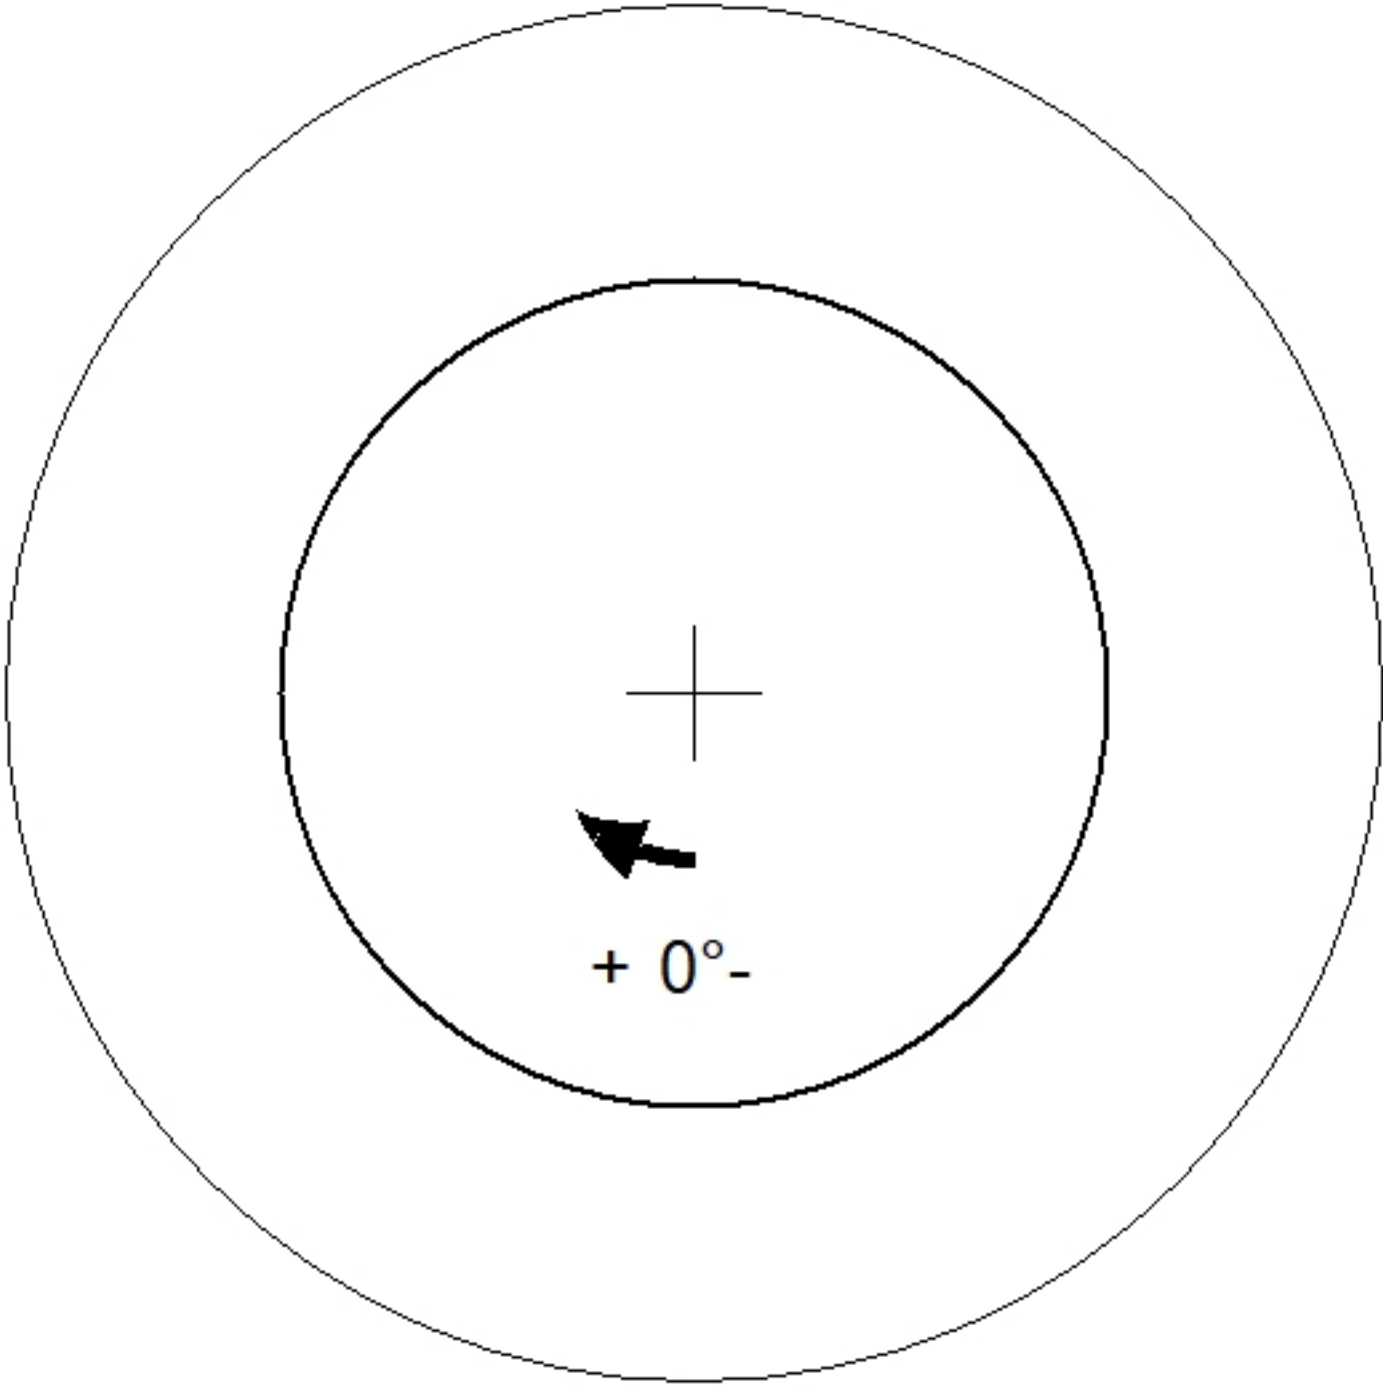


Job Name: 26-2117 - The Preserve at Priest Lake Job Location: Nashville, TN Contractor: Bear Construction LLC		Plant: 100 8/27/2026 2:56:49 PM	Tech: J. Horsley PC: T. Ryan	
Structure ID: 4 SS-MH				
P4 GR3CDARED		GRADE RING w/ConBlock-CDA Red F/F		
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3" P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 36" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 60" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 10) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 2251 lb 4192 lb 2911 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 16 lb 0 lb ----- 11262 lb Structure Total:	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING BY ICAST (JBS 1150 F/C) . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
24" - GRADE RING w/ConBlock-CDA Red F/F - 3" - (P4)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 3"	Weight (Net): 202 lb Volume (Net): 0.05cu.yd
