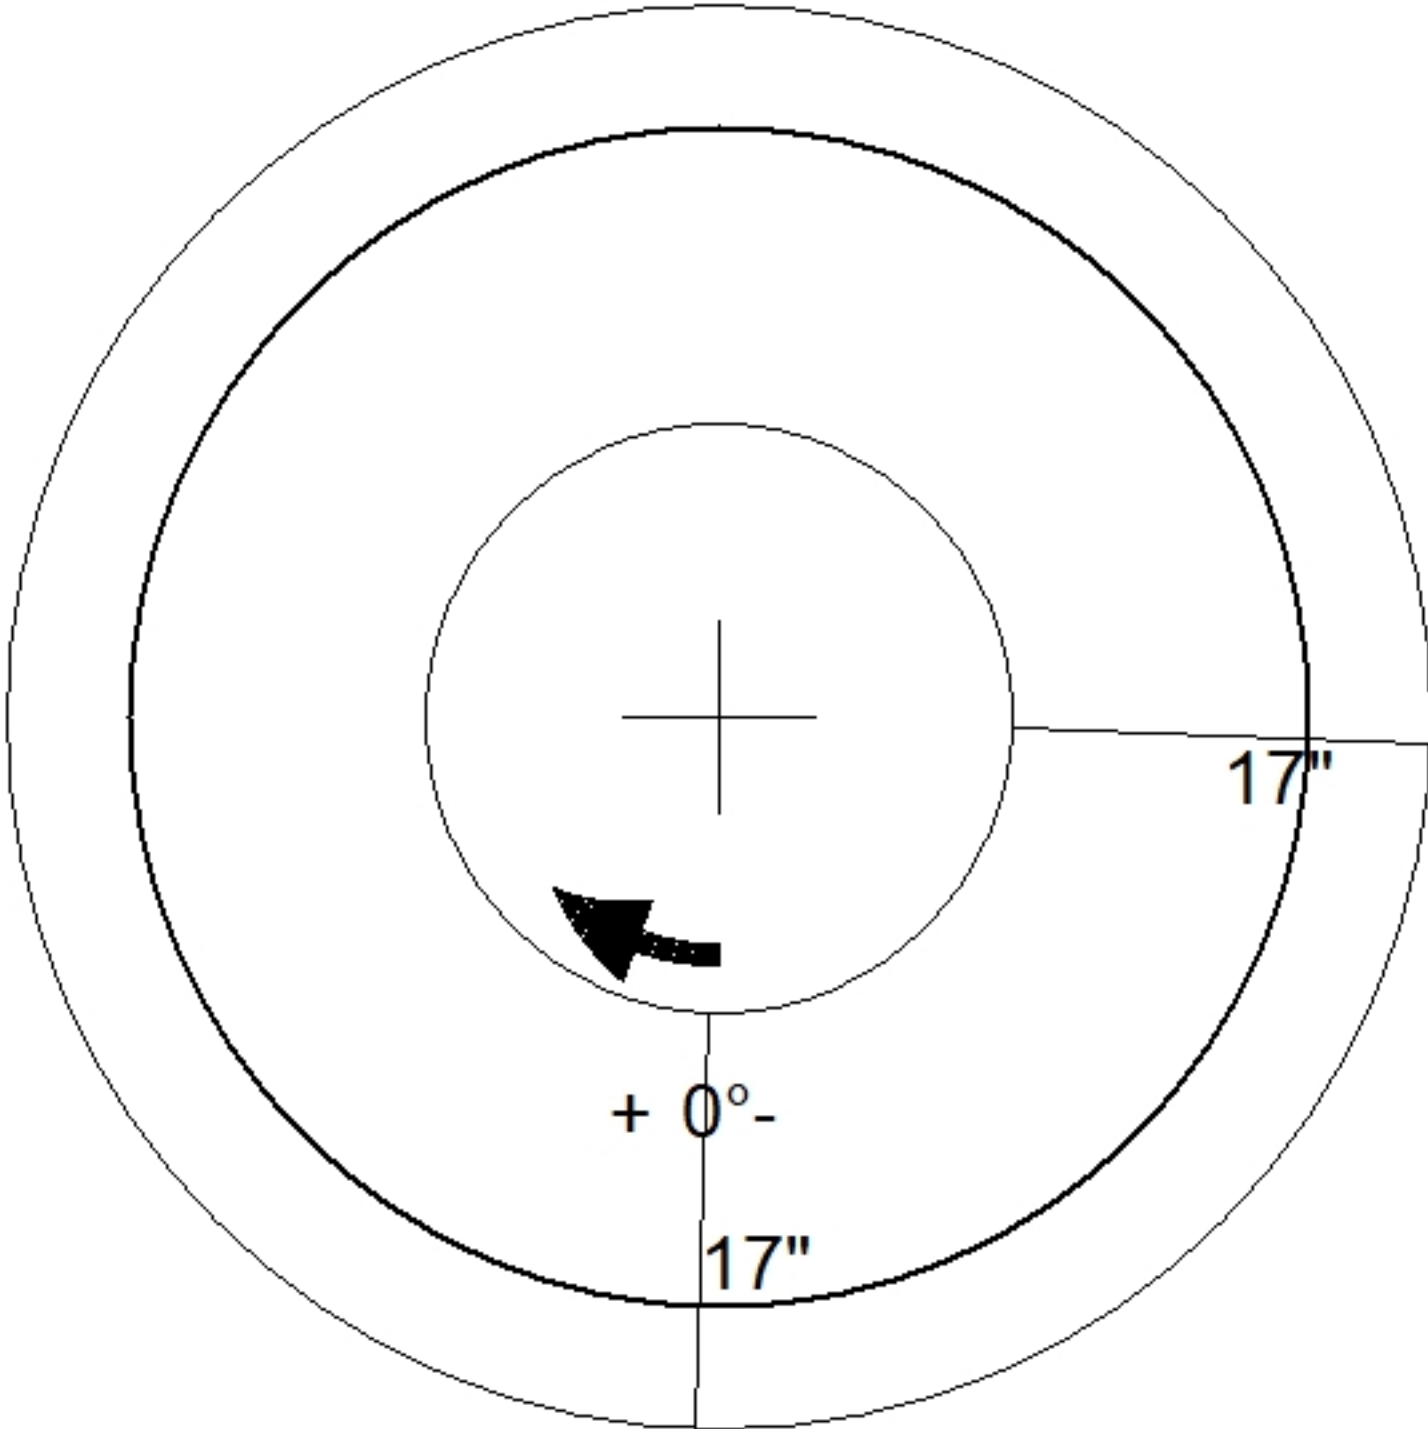
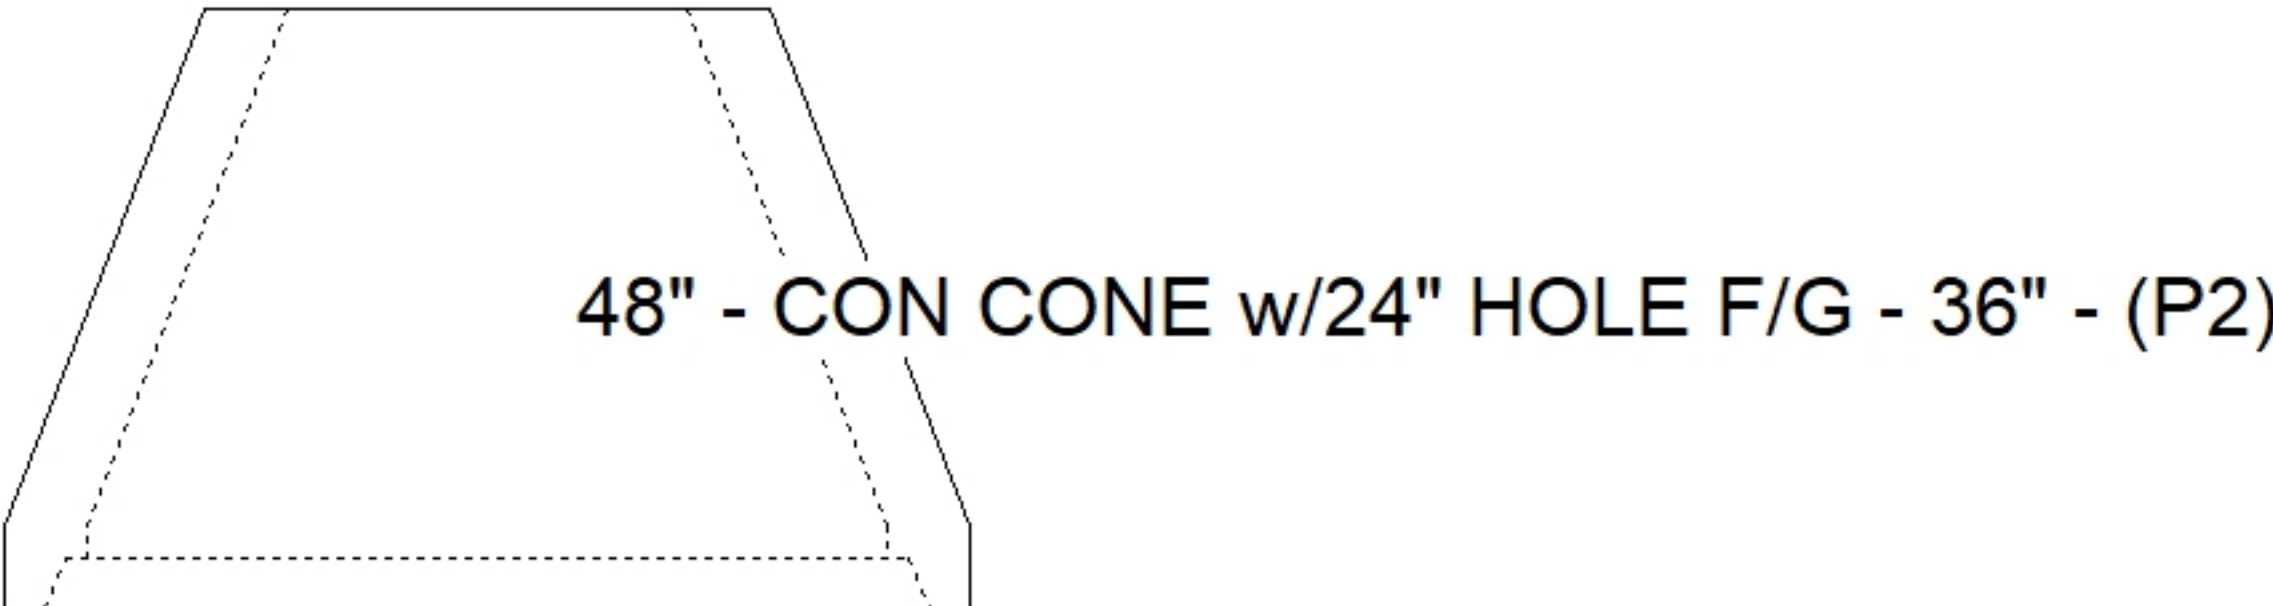


Job Name: 26-2117 - The Preserve at Priest Lake Job Location: Nashville, TN Contractor: Bear Construction LLC		Plant: 100 8/27/2026 1:35:08 PM	Tech: J. Horsley PC: T. Ryan		
Structure ID: MH1 ST-MH					
P2 MH048CCN36 CON CONE w/24" HOLE F/G					
P3) 24" - CASTING HEIGHT - 7" P2) 48" - CON CONE w/24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 42" 1) 48" - STORM INVERT CHANNEL - 1/4 HEIGHT 1) CASTING - JBS 1150 F/C STORM 1) 48" - Conseal CS-102 1.00" 3) Hole - 26 3) MH Step ML-10-TDS-NCR - 10"		0 lb 2252 lb 3565 lb 1075 lb 250 lb 0 lb 0 lb 0 lb Structure Total: 7142 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (JBS 1150 F/C) - REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
					
					
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2252 lb Volume (Net): 0.57cu.yd	
