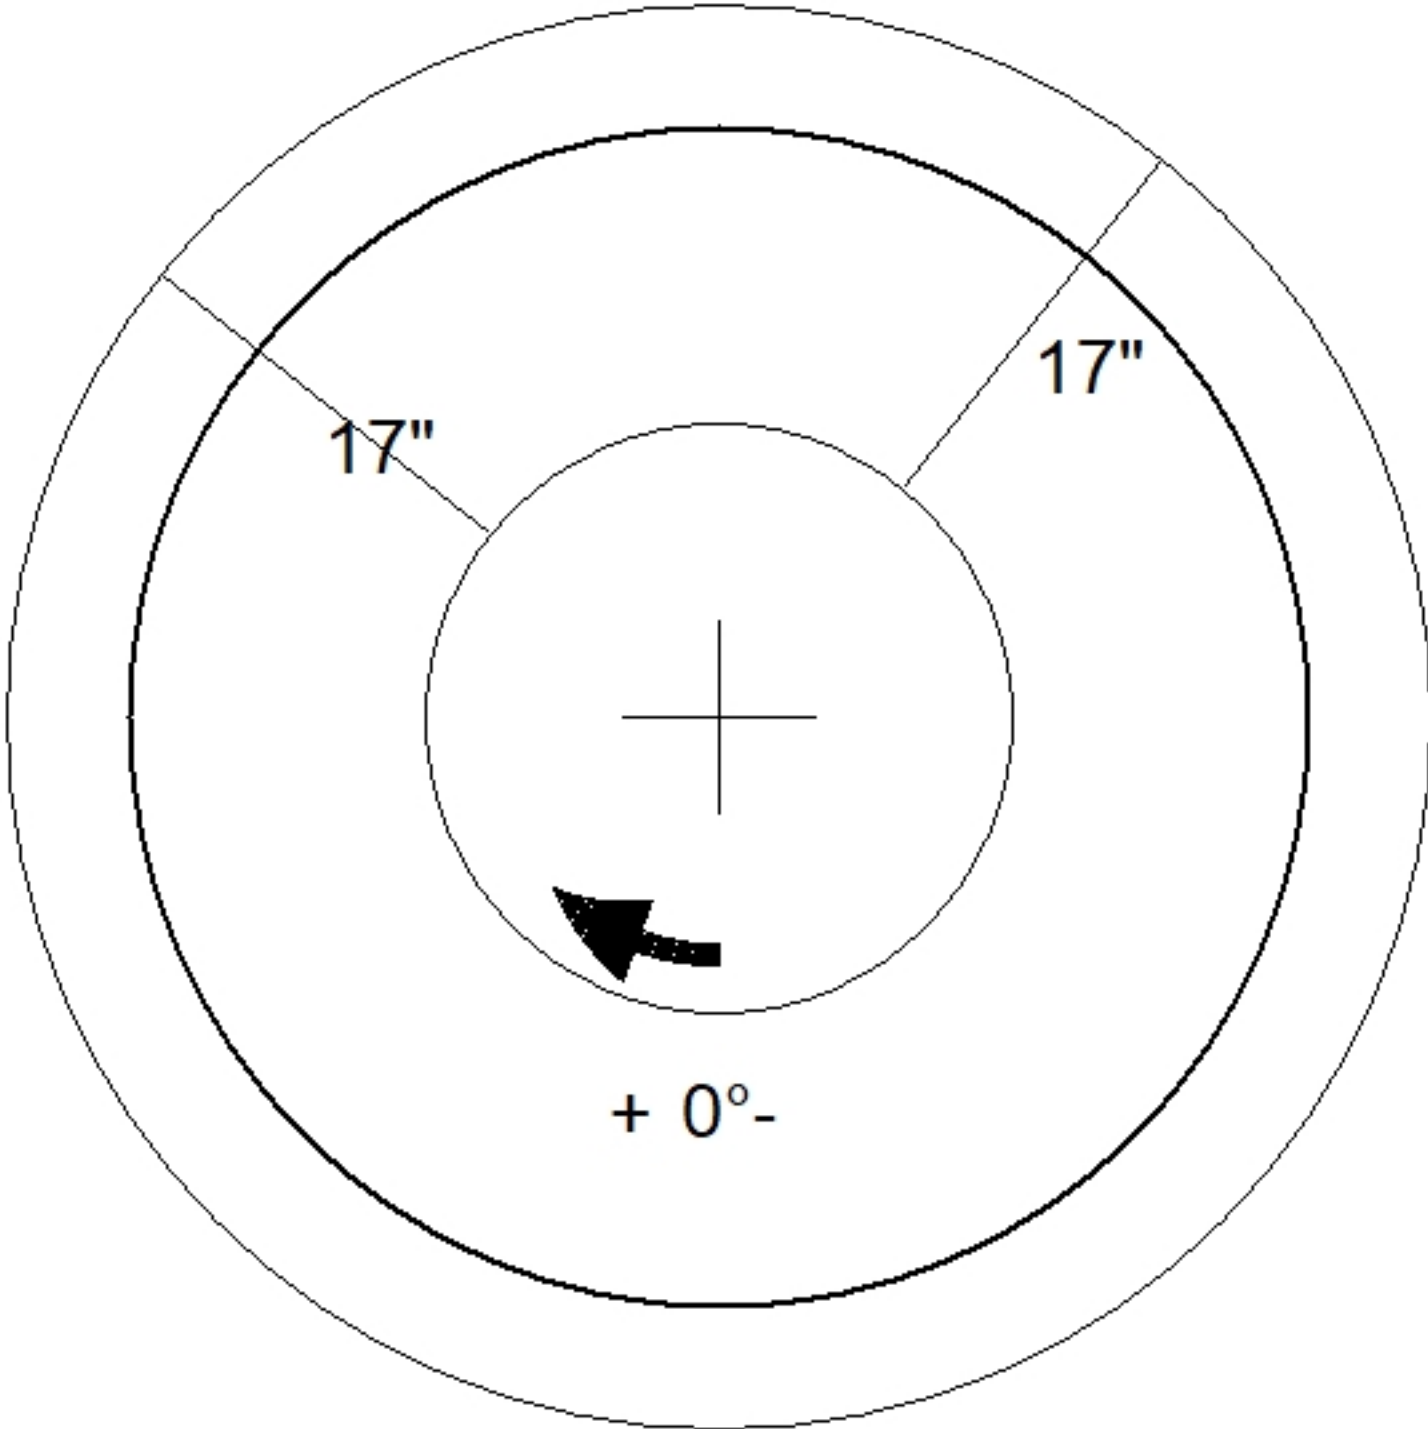
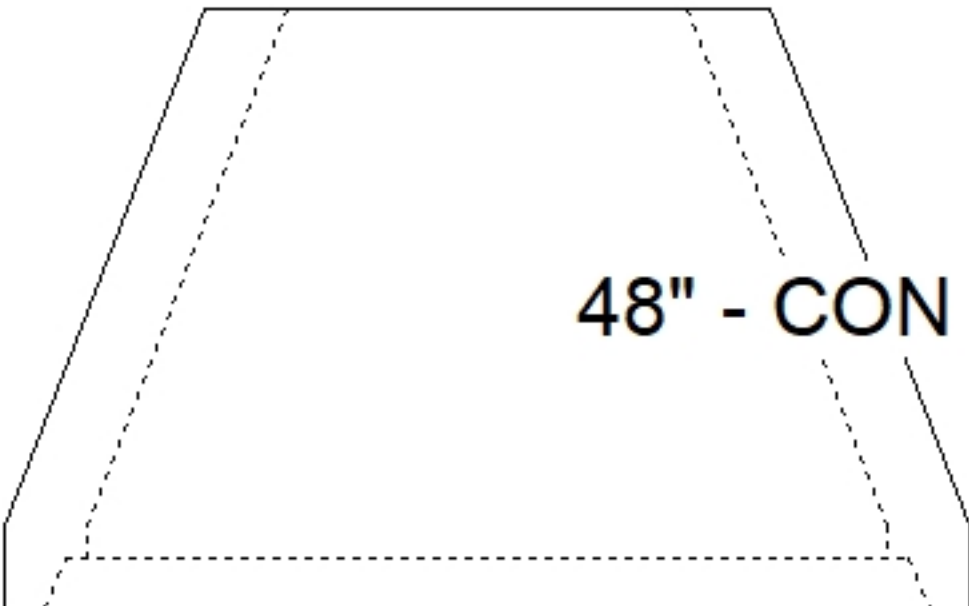


Job Name: 26-2117 - The Preserve at Priest Lake Job Location: Nashville, TN Contractor: Bear Construction LLC		Plant: 100 8/27/2026 1:22:33 PM	Tech: J. Horsley PC: T. Ryan	
Structure ID: MH3 ST-MH				
P2 MH048CCN36		CON CONE w/24" HOLE F/G		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - CON CONE w/24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 48" 1) 48" - STORM INVERT CHANNEL - 1/4 HEIGHT 1) CASTING - JBS 1150 F/C STORM 1) 48" - Conseal CS-102 1.00" 2) Hole - 26 4) MH Step ML-10-TDS-NCR - 10"		0 lb 2252 lb 4217 lb 1075 lb 250 lb 0 lb 0 lb 0 lb ----- 7794 lb Structure Total:	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (JBS 1312F/C) . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2252 lb Volume (Net): 0.57cu.yd
