




Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:37 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: 21 ST-DCB											
P1 MH048BAVF		MH BASE Custom Ht									
P3) 18" x 36" - CASTING HEIGHT - 5.5" P2) 48" - MH FLAT TOP w/18"x36" Hole - 12" P1) 48" - MH BASE Custom Ht - 41" 1) 48" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 16						0 lb 2008 lb 3973 lb 0 lb 0 lb 0 lb ----- Structure Total: 5981 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE 580 F/G) . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER (As .12). - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1069.88' Rim to Invert: 4.88' Slack: 0.06" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	1065'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.3"	0"	
Invert 2	1065'	202°	102.241"	12" HDPE	14.5"	Hole 16	16"	16.312"	-1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

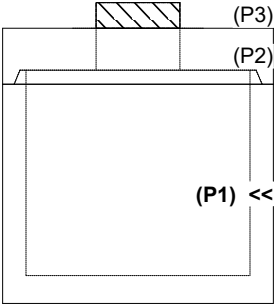


RIGHT-SIDE UP VIEW (int. dimensions)

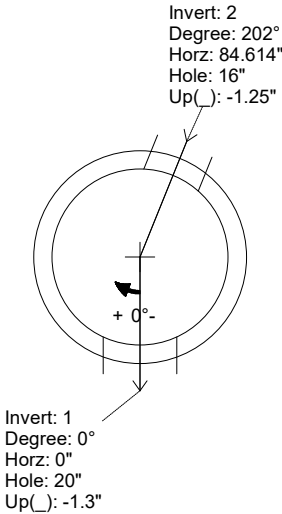

UPSIDE-DOWN VIEW (int. dimensions)

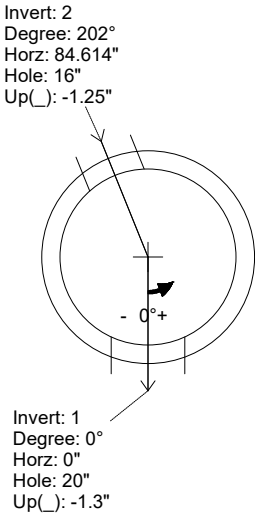

INSIDE WALL DIMENSIONS

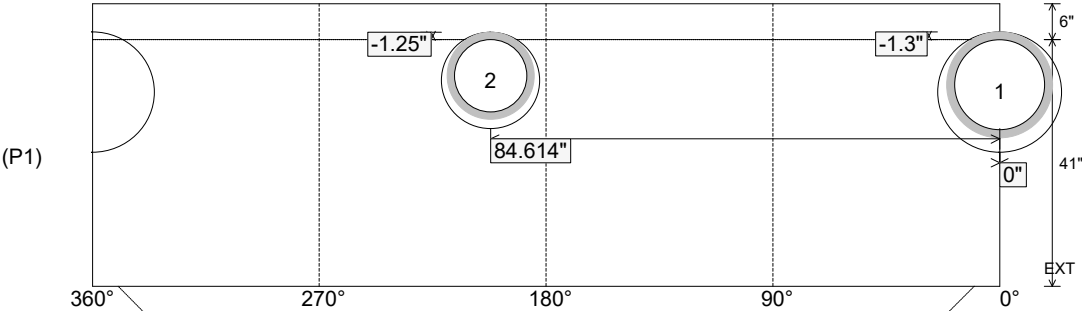

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 41" Height (Ext): 47"	Weight (Net): 3973 lb Volume (Net): 1.01cu.yd
----------------------------------	---------------------------------	--	--	--
