




Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:22 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: MH 1 SS-MH											
P1 MH048BA24		MH BASE									
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING - 4" P2) 48" - ECC CONE w/ 24" HOLE - 30" P1) 48" - MH BASE - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 4) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 2050 lb 2863 lb 1440 lb 0 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 6647 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE MC-420 F/C). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 1059.44' Rim to Invert: 5.21' Slack: 0.52' Sump: 3" Step Position: 190.5°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1054.23'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1"	0"	
Invert 2	1054.28'	103°	52.133"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.6"	0"	
Invert 3	1054.28'	278°	140.708"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.6"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

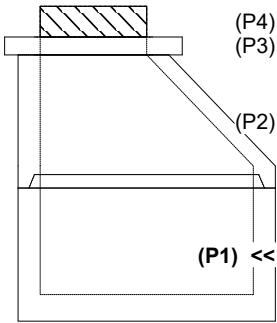


RIGHT-SIDE UP VIEW (int. dimensions)

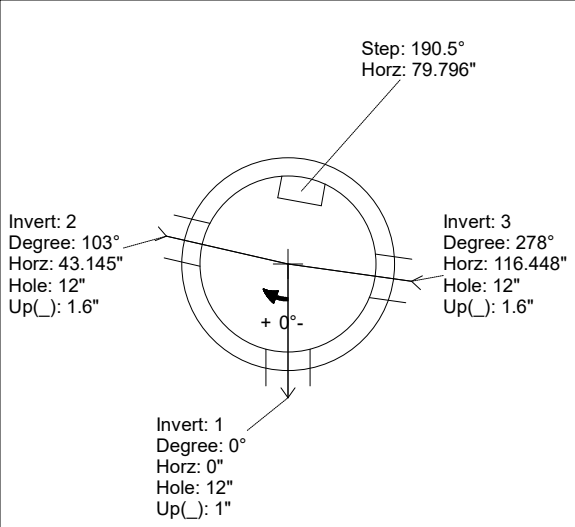

UPSIDE-DOWN VIEW (int. dimensions)

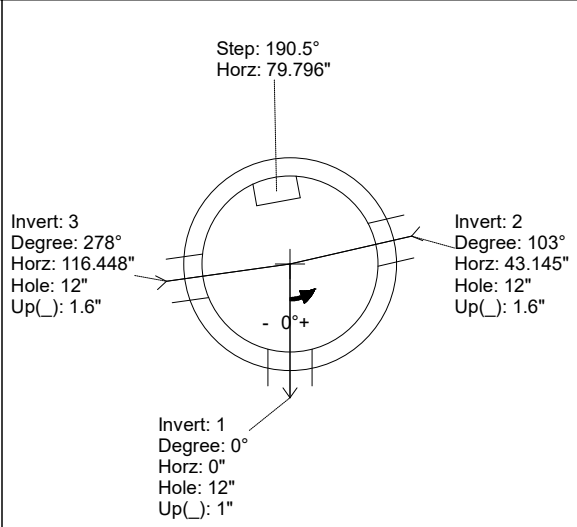

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2863 lb Volume (Net): 0.73cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:22 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: MH 1 SS-MH											
P1 MH048BA24		MH BASE									
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING - 4" P2) 48" - ECC CONE w/ 24" HOLE - 30" P1) 48" - MH BASE - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 4) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 2050 lb 2863 lb 1440 lb 0 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 6647 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE MC-420 F/C). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 1059.44' Rim to Invert: 5.21' Slack: 0.52" Sump: 3" Step Position: 190.5°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1054.23'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1"	0"	
Invert 2	1054.28'	103°	52.133"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.6"	0"	
Invert 3	1054.28'	278°	140.708"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.6"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2863 lb Volume (Net): 0.73cu.yd
----------------------------------	---------------------------------	--	--	--
