

Job Name: 26-2171 - Lake Malone Campground Multi Park West

Job Location: Lewisburg, KY

Contractor: Sensabaugh Design & Construction, LLC

Plant: 100

6/11/2026 3:16:10 PM

Tech: Jared - F

PC: M. Sullivan



Structure ID: SSMH-E1


P3 MH048CN36

ECC CONE w/ 24" HOLE F/G

P4) 24" - CASTING HEIGHT - 7"	0 lb	<u>Structure Notes:</u> . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C "SANITARY"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12)		
P3) 48" - ECC CONE w/ 24" HOLE F/G - 36"	3000 lb			
P2) 48" - MH RISER Custom Ht T/F - 70"	4637 lb			
P1) 48" - P.I.P. BY OTHERS - BTM SLAB F/n - 0"	0 lb			
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb			
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb			
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb			
1) CASTING - HOE MC-315 F/C Sanitary	258 lb			
2) 48" - Conseal CS-102 1.00" (Double)	0 lb			
1) 24" - Conseal CS-102 1.00" (Double)	0 lb			
2) DOGHOUSE - 12"x18"	0 lb			
1) PSX - 8QRS-S NYLO	6 lb			
1) PSX - 12-06 NYLO	8 lb			
9) MH Step ML-10-TDS-NCR - 10"	0 lb			

Structure Total: 9350 lb				
Rim: 567.82'	Rim to Invert: 8.87'	Slack: 1.44"	Sump: 8"	Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

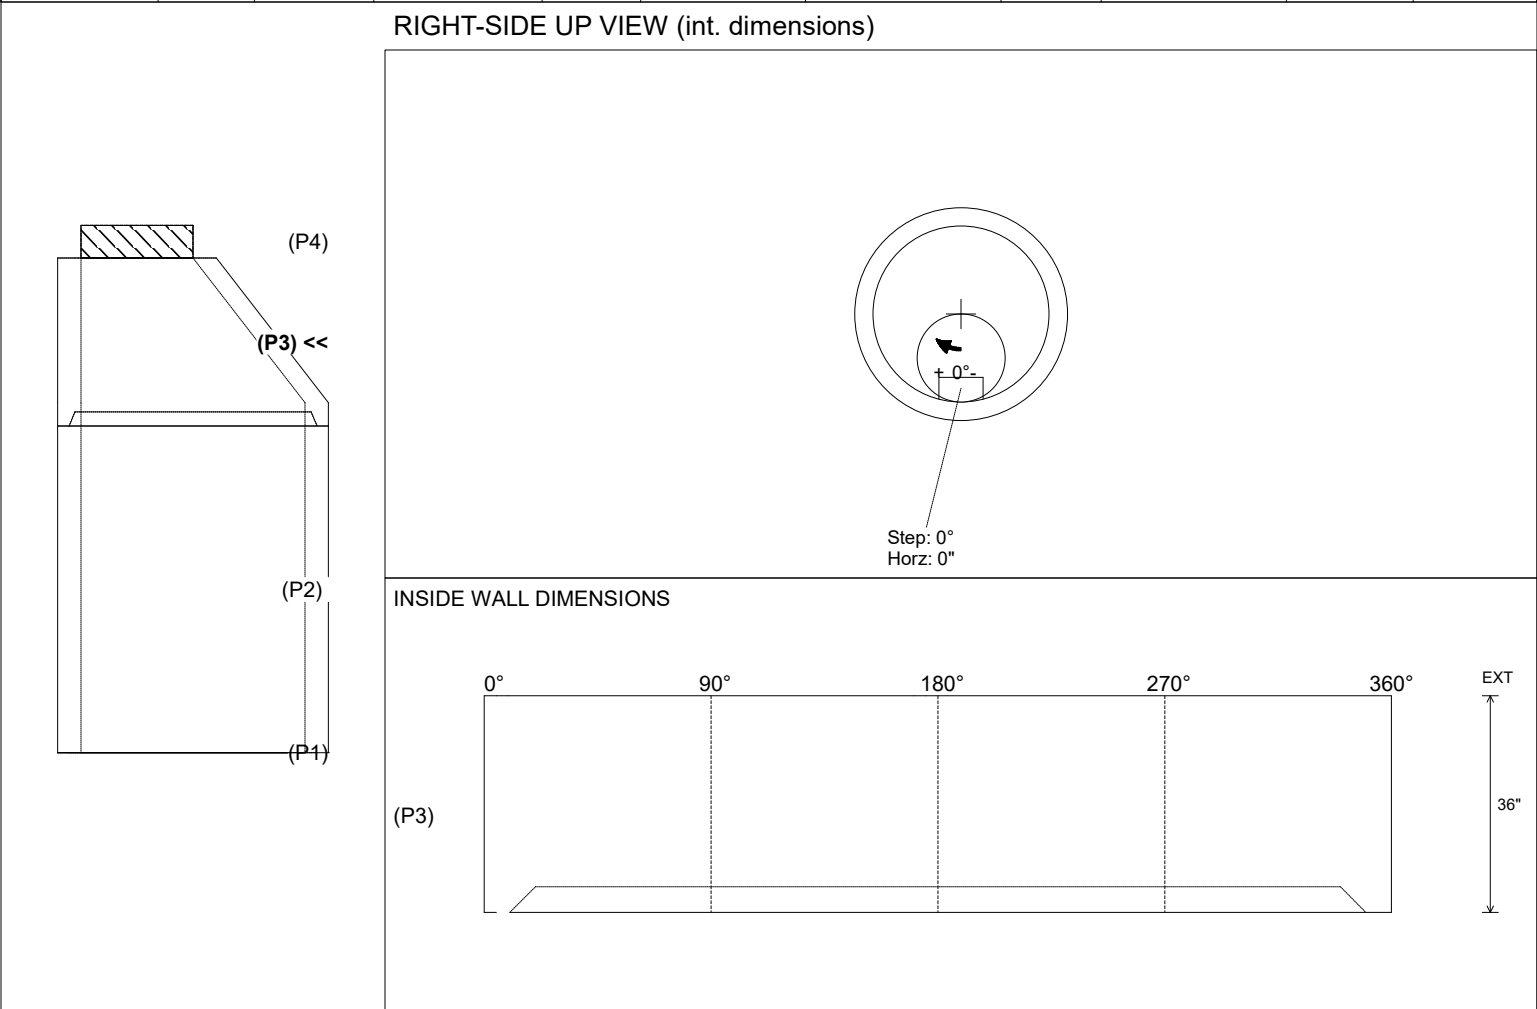

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 36" Height (Ext): 36"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd
----------------------------------	----------------------------------	--	--	---
