



Job Name: 26-2171 - Lake Malone Campground Multi Park West Job Location: Lewisburg, KY Contractor: Sensabaugh Design & Construction, LLC					Plant: 100 6/11/2026 3:15:24 PM		Tech: Jared - F PC: M. Sullivan			
Structure ID: SSMH-E2										
P1 MH048BA24			MH BASE T/n							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-06 NYLO 1) PSX - 8QRS-S NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 3000 lb 2515 lb 2890 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 16 lb 6 lb 0 lb ----- Structure Total: 10125 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C "SANITARY"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 568.38' Rim to Invert: 8.38' Slack: 0.56" Sump: 3" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	560'	0°	0"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0"	0"
Invert 2	560.1'	92°	46.625"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	1.25"	0"
Invert 3	560.1'	290°	146.75"	4" PVC SCH40	4.5"	PSX 8QRS-S NYLO	8"	8.038"	2.25"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

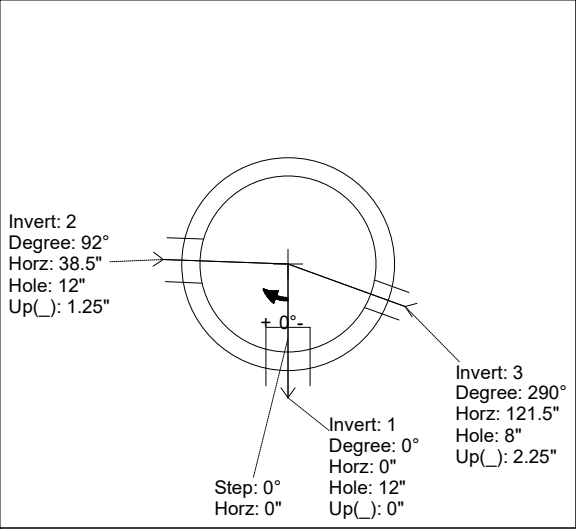

UPSIDE-DOWN VIEW (int. dimensions)

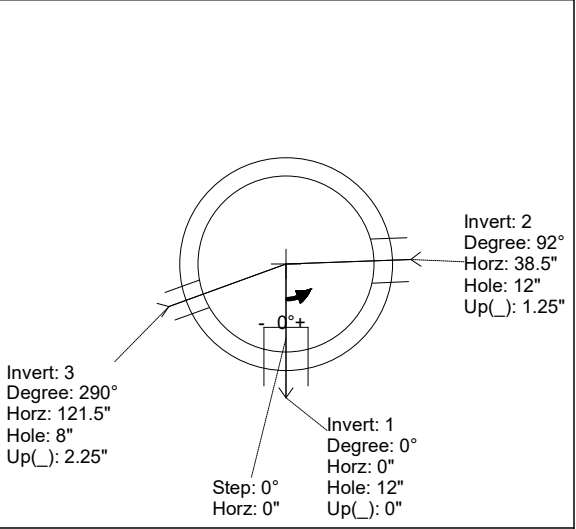


INSIDE WALL DIMENSIONS

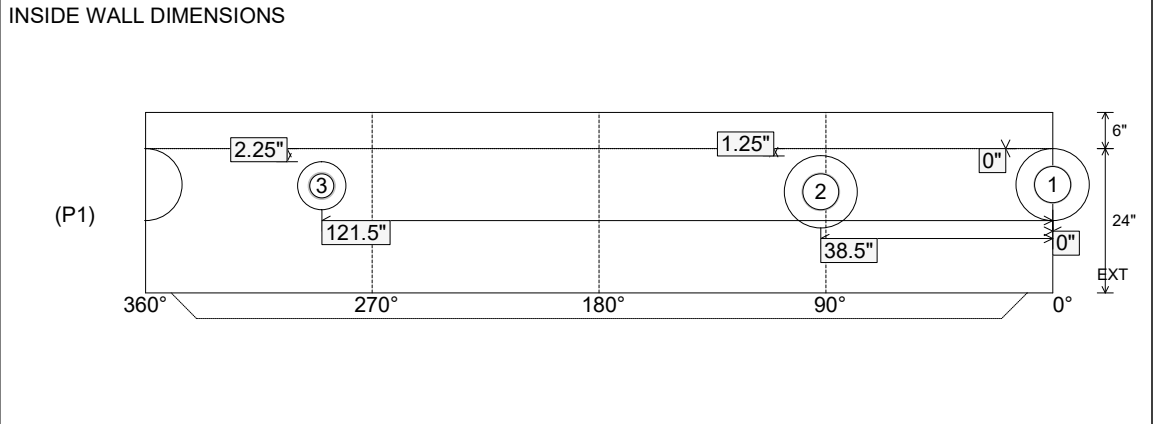


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2890 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2171 - Lake Malone Campground Multi Park West Job Location: Lewisburg, KY Contractor: Sensabaugh Design & Construction, LLC				Plant: 100 6/11/2026 3:15:24 PM		Tech: Jared - F PC: M. Sullivan				
Structure ID: SSMH-E2										
P1 MH048BA24		MH BASE T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-06 NYLO 1) PSX - 8QRS-S NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 3000 lb 2515 lb 2890 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 16 lb 6 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C "SANITARY"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Structure Total:					10125 lb					
Rim: 568.38'		Rim to Invert: 8.38'		Slack: 0.56"		Sump: 3"		Step Position: 0°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	560'	0°	0"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0"	0"
Invert 2	560.1'	92°	46.625"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	1.25"	0"
Invert 3	560.1'	290°	146.75"	4" PVC SCH40	4.5"	PSX 8QRS-S NYLO	8"	8.038"	2.25"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

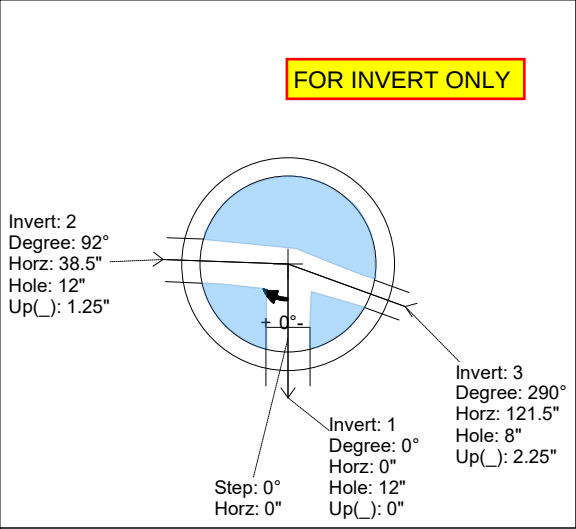

UPSIDE-DOWN VIEW (int. dimensions)

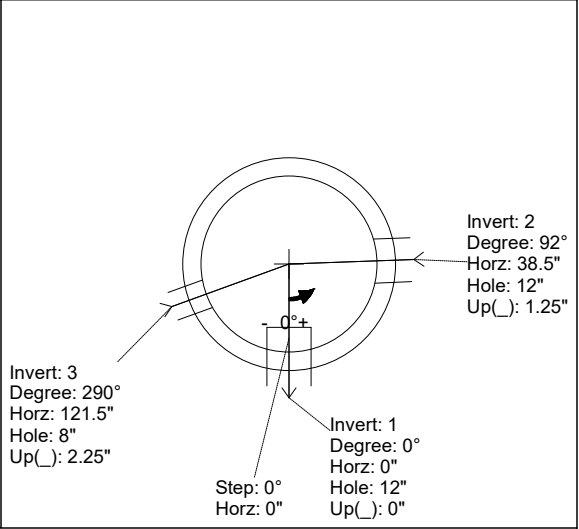

INSIDE WALL DIMENSIONS

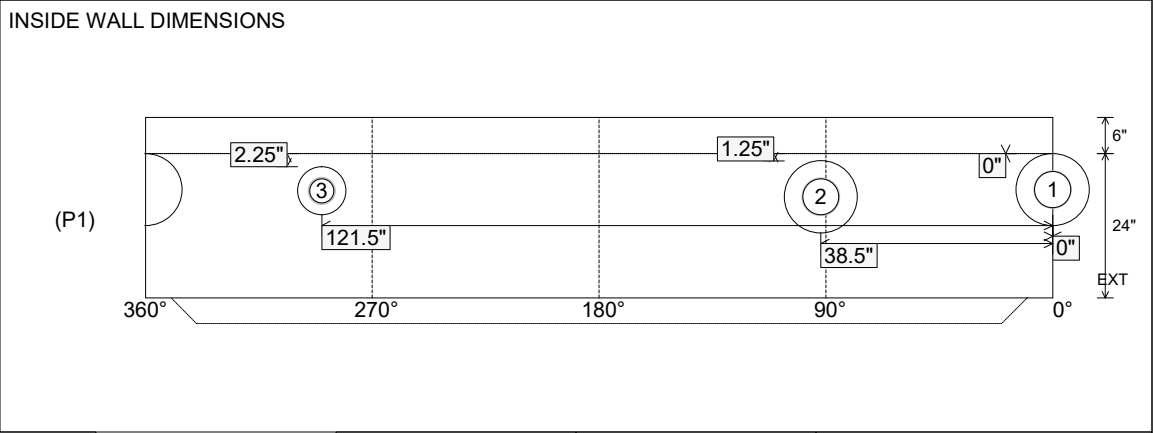

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2890 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--
