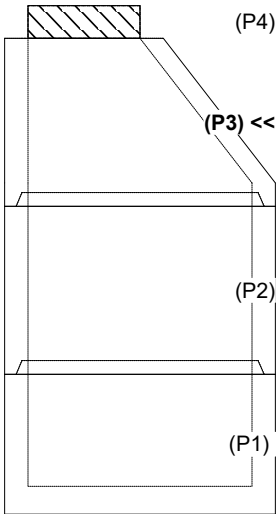




Job Name: 26-2171 - Lake Malone Campground Multi Park West Job Location: Lewisburg, KY Contractor: Sensabaugh Design & Construction, LLC					Plant: 100 6/11/2026 3:16:10 PM		Tech: Jared - F PC: M. Sullivan						
Structure ID: SSMH-E2													
P3		MH048CN36		ECC CONE w/ 24" HOLE F/G									
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-06 NYLO 1) PSX - 8QRS-S NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 3000 lb 2515 lb 2890 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 16 lb 6 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C "SANITARY"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					Structure Total: 10125 lb	
Rim: 568.38'		Rim to Invert: 8.38'		Slack: 0.56"		Sump: 3"		Step Position: 0°					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 3000 lb Volume (Net): 0.5cu.yd				
