


Job Name: 26-2197 - Miller Park Job Location: CPU Contractor: Campbellsville Water & Sewer				Plant: Beaver Dam, KY 5/4/2026 9:38:54 AM		Tech: J. Horsley PC: T. Ryan						
Structure ID: MH 1												
P1 MH048BA36				MH BASE T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 36" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 22M DD 4) MH Step ML-10-TDS-NCR - 10"						0 lb 3000 lb 3516 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 16 lb 0 lb ----- Structure Total: 8277 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. HOE MC-350 FRAME & COVER "SANITARY" SUPPLIED BY ICAST				
Rim: 6.5'		Rim to Invert: 6.5'		Slack: 1"		Sump: 2"		Step Position: 0°				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	0'	0°	0"	18" PVC SDR35	18.75"	PSX 22M DD	22"	22.854"	0"	0"		
Invert 2	0'	120°	60.75"	18" PVC SDR35	18.75"	PSX 22M DD	22"	22.854"	0"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

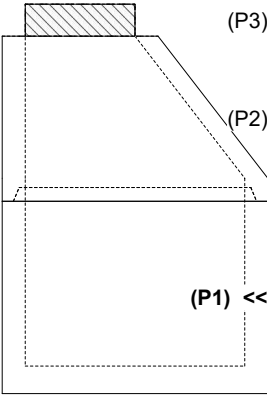


(P3)


(P2)

(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

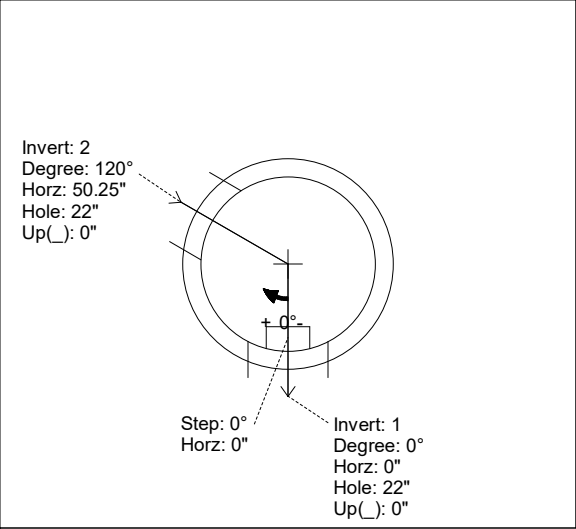

Upside-Down View (int. dimensions)

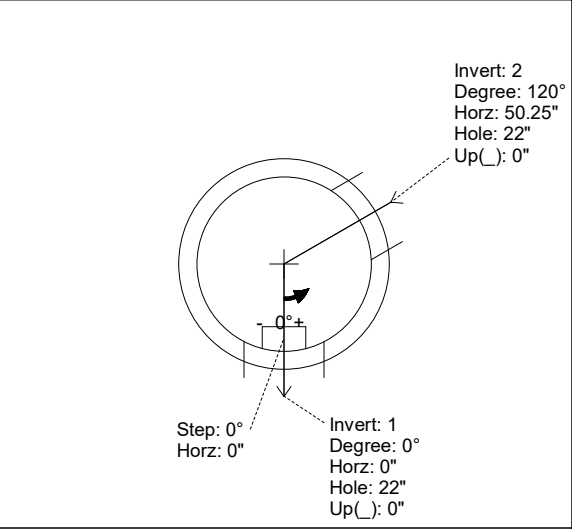


INSIDE WALL DIMENSIONS

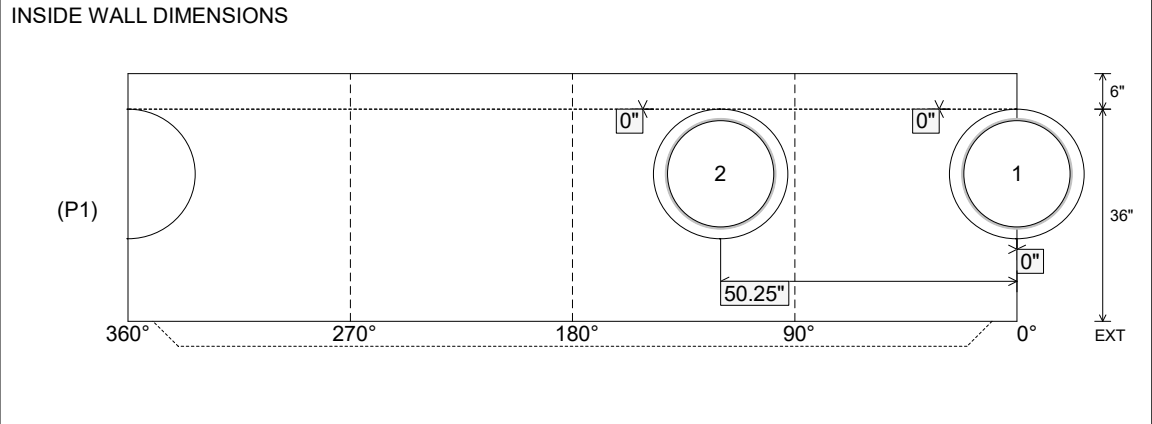

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3516 lb Volume (Net): 0.9cu.yd
----------------------------------	---------------------------------	--	--	---

Job Name: 26-2197 - Miller Park Job Location: CPU Contractor: Campbellsville Water & Sewer				Plant: Beaver Dam, KY 5/4/2026 9:38:54 AM		Tech: J. Horsley PC: T. Ryan						
Structure ID: MH 1												
P1 MH048BA36				MH BASE T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 36" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 22M DD 4) MH Step ML-10-TDS-NCR - 10"						0 lb 3000 lb 3516 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 16 lb 0 lb ----- Structure Total: 8277 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. HOE MC-350 FRAME & COVER "SANITARY" SUPPLIED BY ICAST				
Rim: 6.5'				Rim to Invert: 6.5'		Slack: 1"		Sump: 2"		Step Position: 0°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset		
Invert 1	0'	0°	0"	18" PVC SDR35	18.75"	PSX 22M DD	22"	22.854"	0"	0"		
Invert 2	0'	120°	60.75"	18" PVC SDR35	18.75"	PSX 22M DD	22"	22.854"	0"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

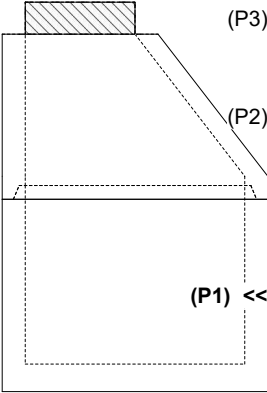


(P3)

(P2)

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

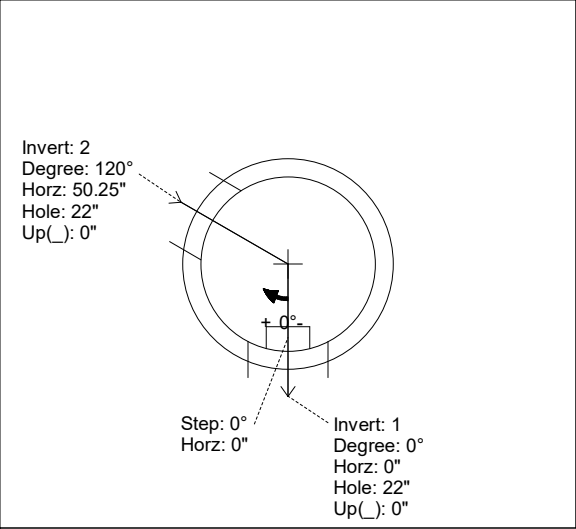


Invert: 2
Degree: 120°
Horz: 50.25"
Hole: 22"
Up(_): 0"

Step: 0°
Horz: 0"


Invert: 1
Degree: 0°
Horz: 0"
Hole: 22"
Up(_): 0"

UPSIDE-DOWN VIEW (int. dimenions)

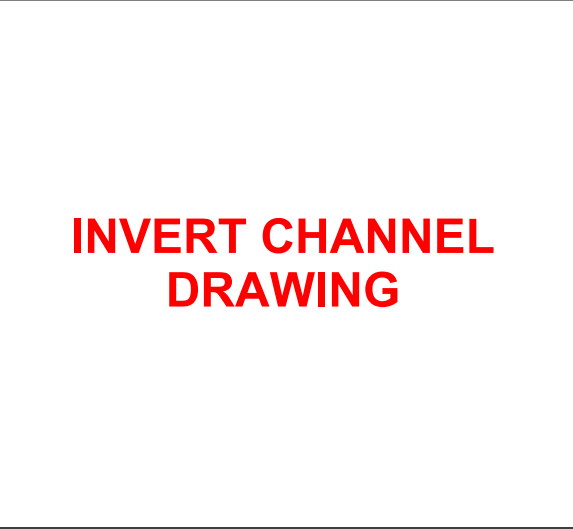

**INVERT CHANNEL
DRAWING**

INSIDE WALL DIMENSIONS

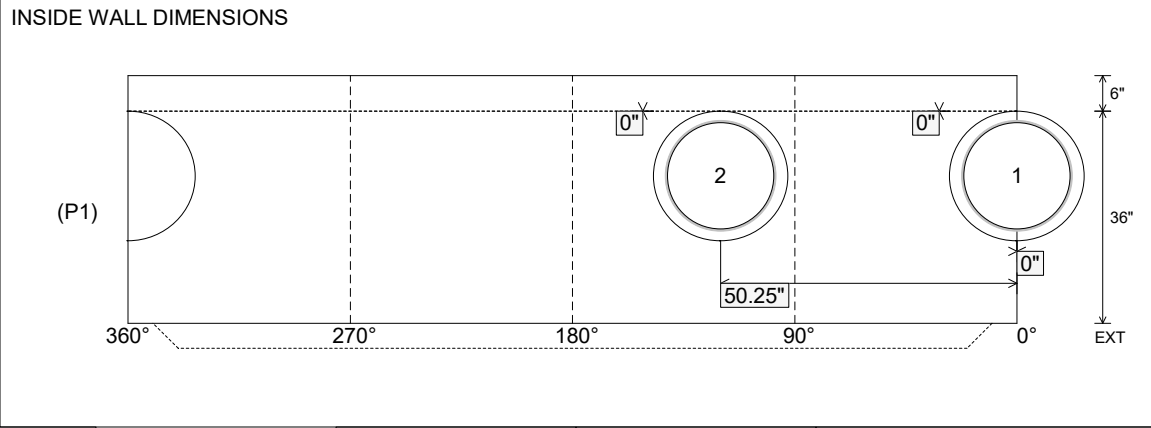

(P1)

360° 270° 180° 90° 0°

50.25"

6"

36"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3516 lb Volume (Net): 0.9cu.yd
----------------------------------	---------------------------------	--	--	---
