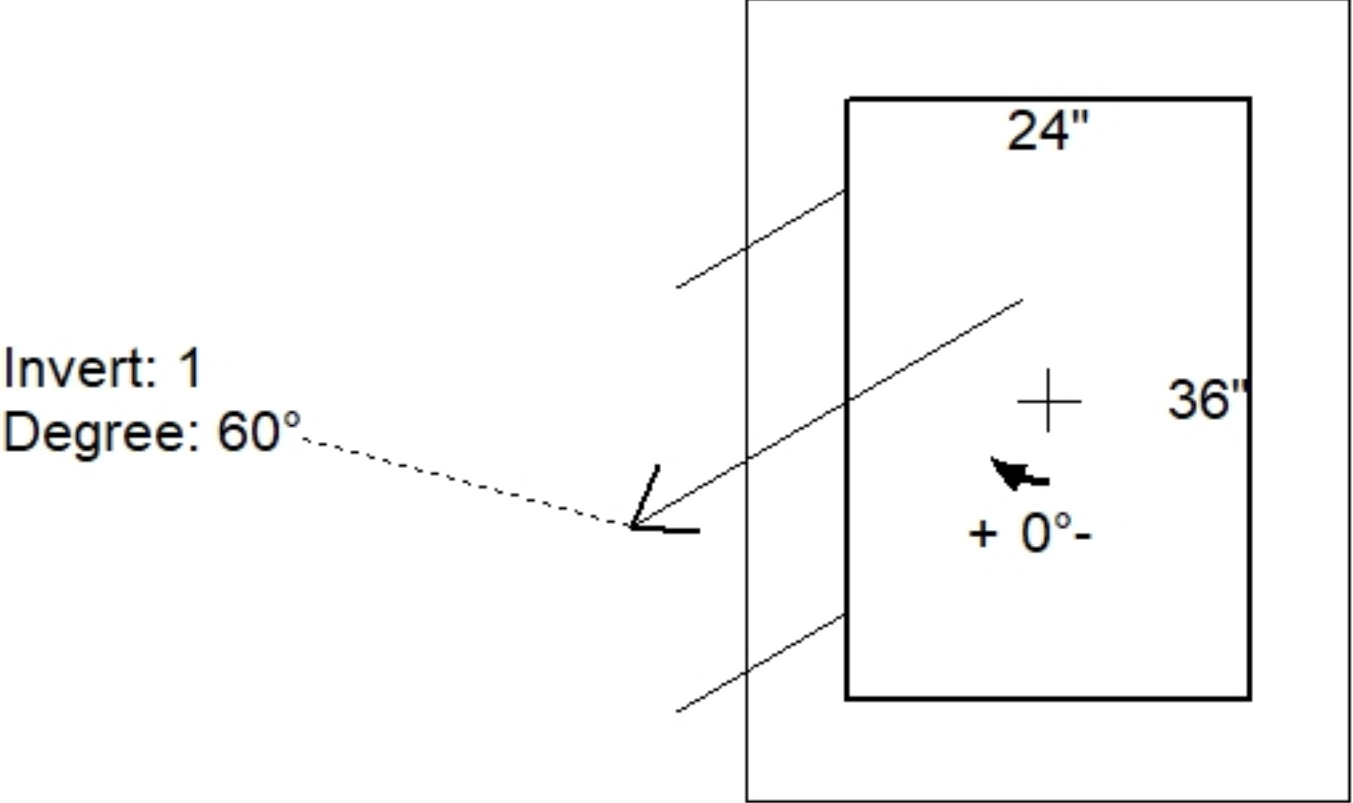
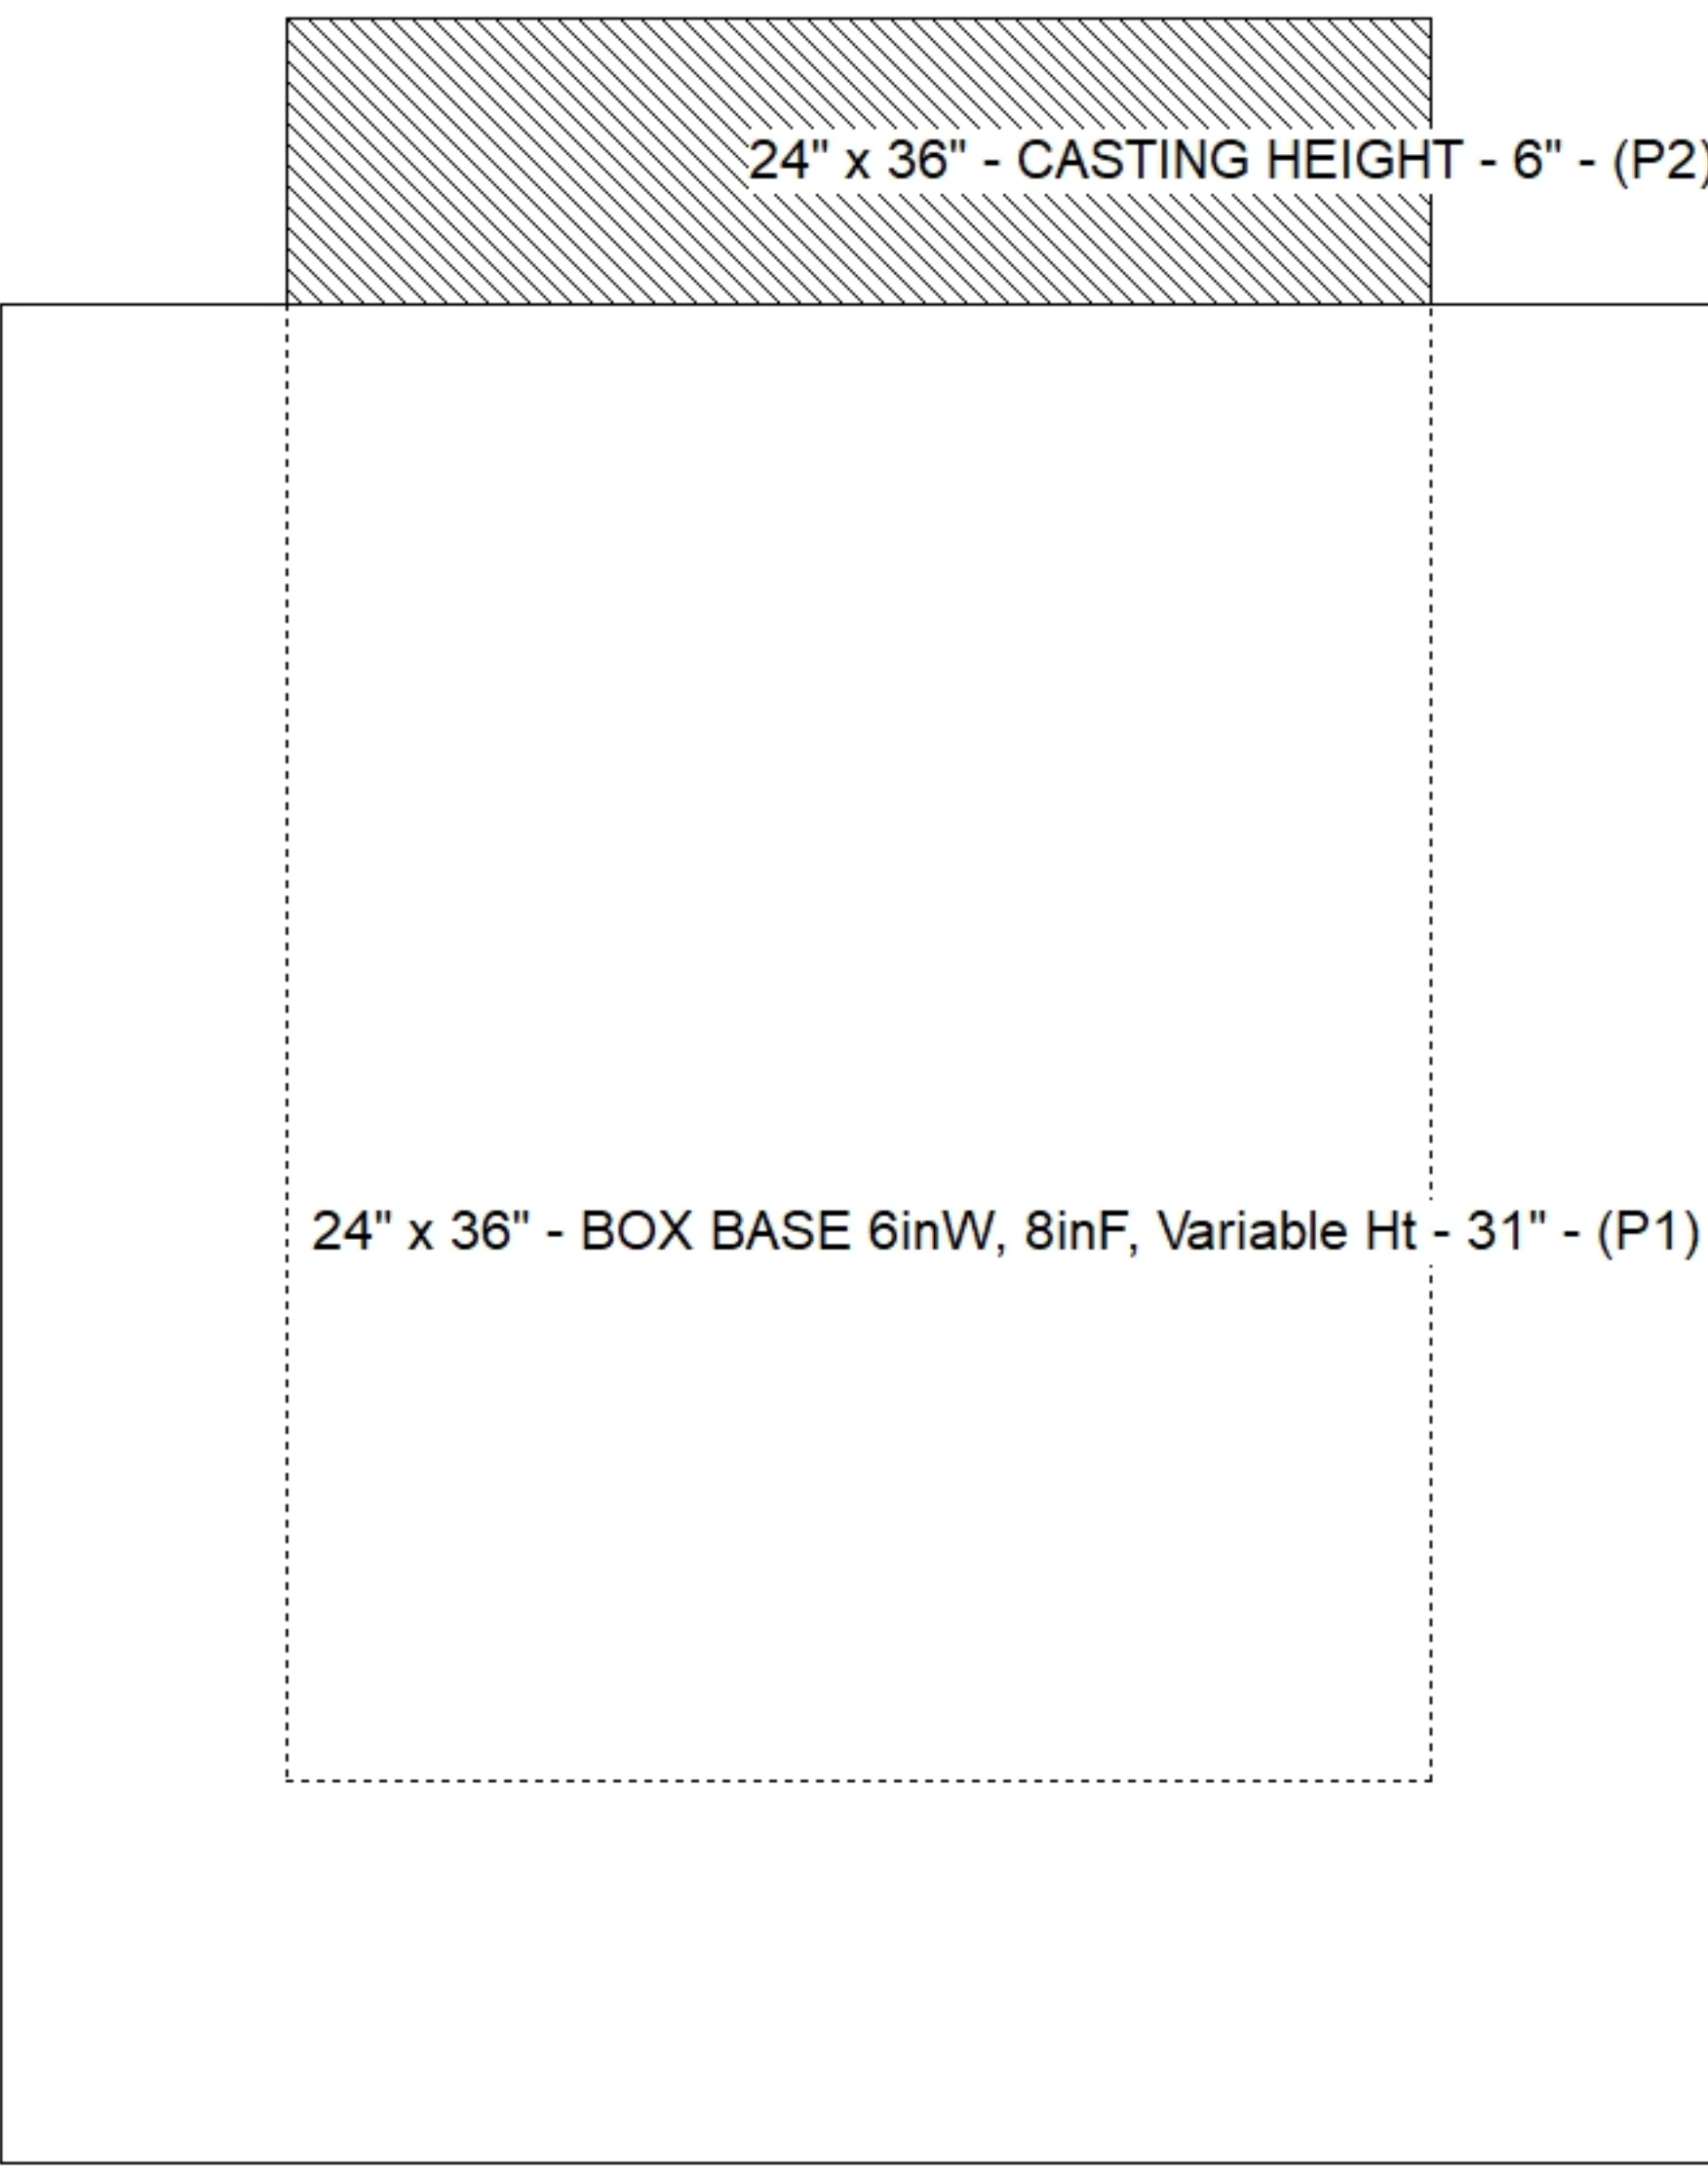
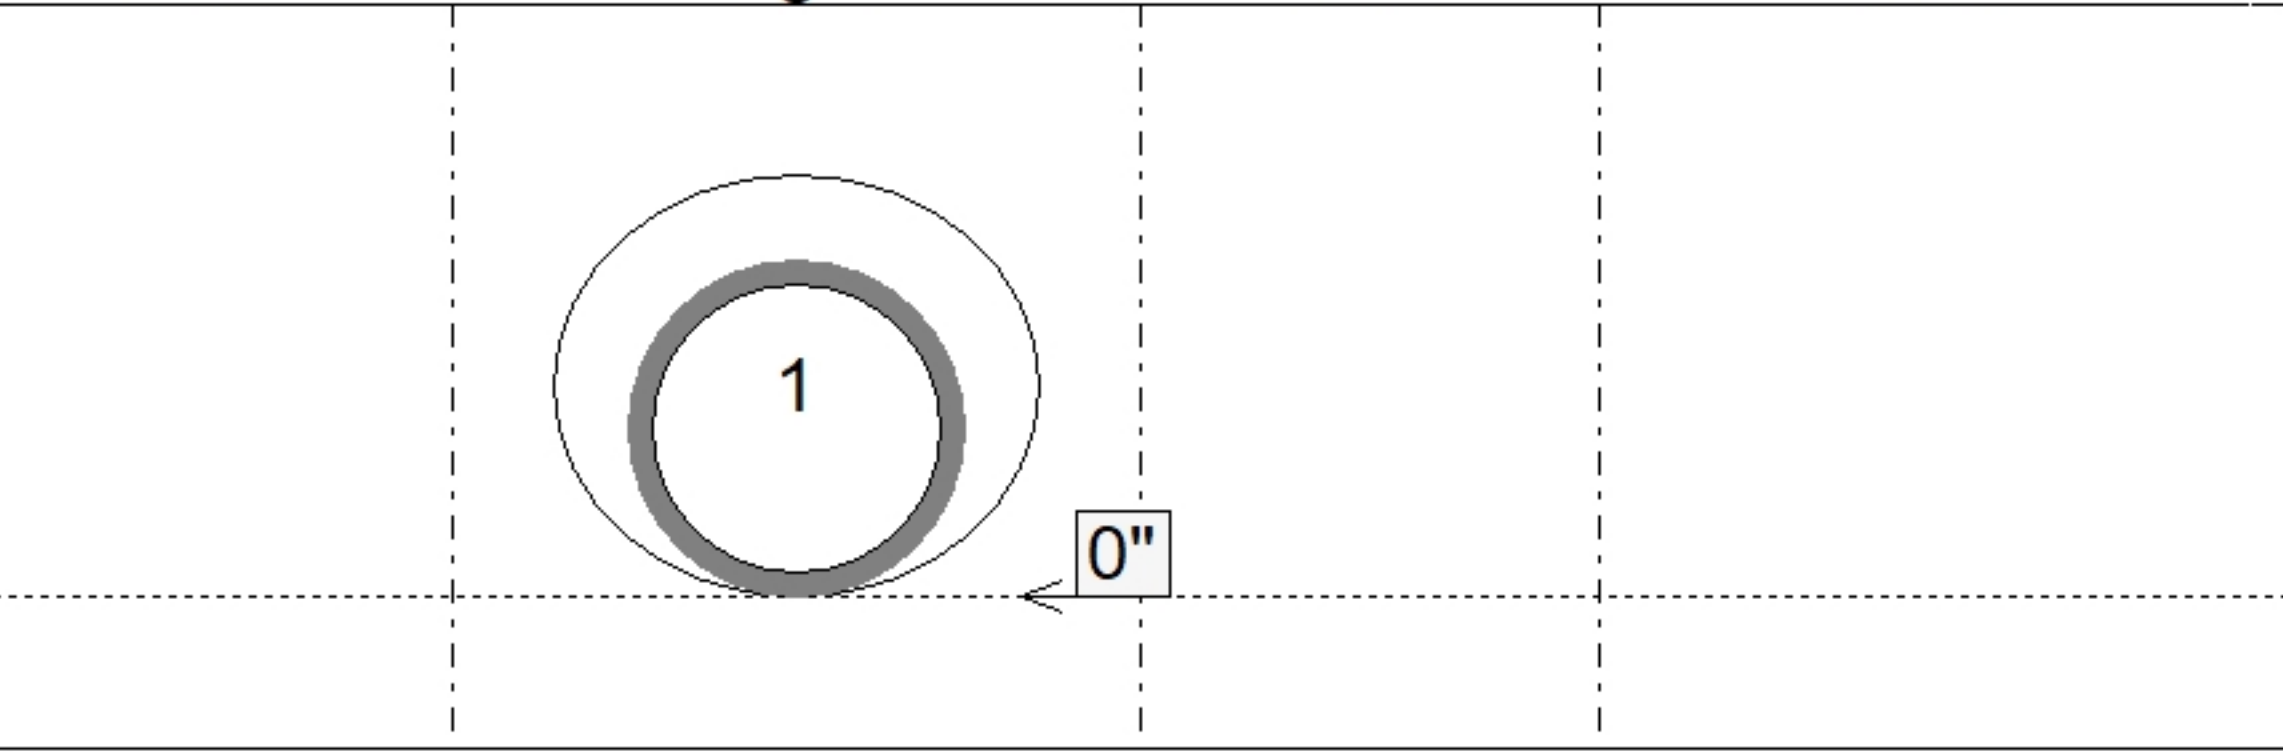


Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.				PC: E. Bradley TECH: J. Coppinge Plant: Beaver Dam																																																																																																								
Structure ID: 101 INJ10 Spec: INDOT Type: INLET TYPE J Size: 24" x 36"				Rim: 614.19' Invert: 611' Rim to Invert: 3.19'		Sump: 1.3" Floor (Top): 610.892' Floor Height: 8"		Floor (Bot): 610.225' Overall Height: 3.75' Slack: 2.58"																																																																																																				
Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT INLET TYPE J / ASTM C913 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				STRUCTURE SUMMARY: P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 6inW, 8inF, Variable Ht - 31" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22 0 lb 3187 lb 0 lb 0 lb ----- Structure Total: 3187 lb																																																																																																								
				<table><tr><th>Position</th><th>Elev</th><th>Angle</th><th>Pipe</th><th>Pipe OD</th><th>Hole</th><th>Connector</th><th>Up ()</th><th>Ref</th></tr><tr><td>Rim</td><td>614.19'</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Reducer</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 1</td><td>611'</td><td>60°</td><td>15" HDPE</td><td>17.6"</td><td>22"</td><td>Hole 22</td><td>0"</td><td>P1</td></tr><tr><td>Invert 2</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 3</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 4</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 5</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 6</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 7</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 8</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr></table>						Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref	Rim	614.19'								Reducer									Invert 1	611'	60°	15" HDPE	17.6"	22"	Hole 22	0"	P1	Invert 2									Invert 3									Invert 4									Invert 5									Invert 6									Invert 7									Invert 8								
Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref																																																																																																				
Rim	614.19'																																																																																																											
Reducer																																																																																																												
Invert 1	611'	60°	15" HDPE	17.6"	22"	Hole 22	0"	P1																																																																																																				
Invert 2																																																																																																												
Invert 3																																																																																																												
Invert 4																																																																																																												
Invert 5																																																																																																												
Invert 6																																																																																																												
Invert 7																																																																																																												
Invert 8																																																																																																												
				Default - Interior Dimensions Front Right Back Left  EXT 31" 8"																																																																																																								
Submittal Drawing 8/20/2026 8:58:54 AM				SUBMITTAL APPROVED BY:																																																																																																								
