




Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:38:24 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 102 INM10											
P1		BX2436-06W08F-BAVF			BOX BASE 6inW, 8inF, Variable Ht						
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 6inW, 8inF, Variable Ht - 34" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 22"					0 lb 3221 lb 0 lb 0 lb ----- Structure Total: 3221 lb		<u>Structure Notes:</u> **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT INLET TYPE M / ASTM C913 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 610.87' Rim to Invert: 3.41' Slack: 2.22" Sump: 1.3" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	607.46'	0°	18"	15" HDPE	17.6"	Hole 22	22"	22"	0"	0"	
Invert 2	607.56'	155°	15.061"	15" HDPE	17.6"	Hole 22	22"	23.996", 0.598"	1.2"	7.479"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

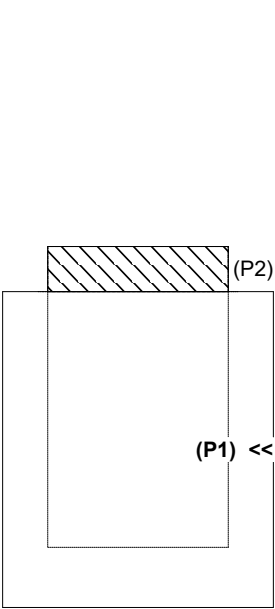

RIGHT-SIDE UP VIEW (int. dimensions)

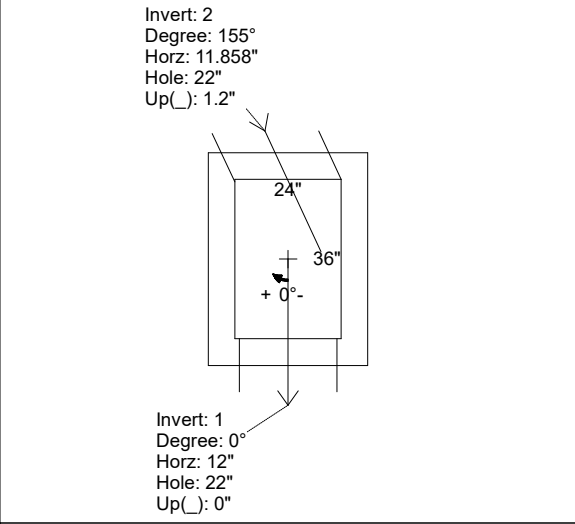

UPSIDE-DOWN VIEW (int. dimensions)

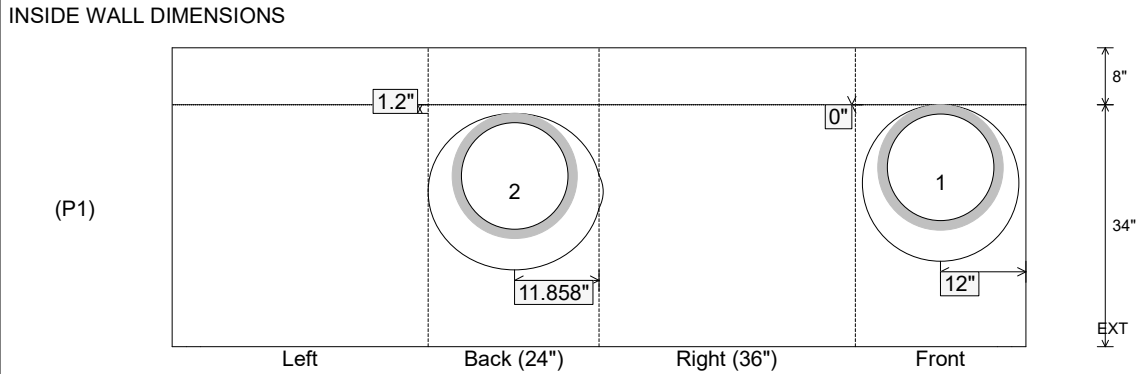

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 34" Height (Ext): 42"	Weight (Net): 3221 lb Volume (Net): 0.82cu.yd
----------------------------------	-------------------------------	--	--	--
