




Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:38:25 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 103 INM10											
P1 BX2436-06W08F-BAVF		BOX BASE 6inW, 8inF, Variable Ht									
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 6inW, 8inF, Variable Ht - 44" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 24 1) Hole - 22						0 lb 3988 lb 0 lb 0 lb 0 lb ----- 0 lb Structure Total: 3988 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT INLET TYPE M / ASTM C913 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 610.13' Rim to Invert: 4.08' Slack: 0.56" Sump: 1.6" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	606.05'	0°	18"	18" HDPE	21.2"	Hole 24	24"	24"	0"	0"	
Invert 2	606.15'	180°	18"	15" HDPE	17.6"	Hole 22	22"	22"	1.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											



RIGHT-SIDE UP VIEW (int. dimensions)

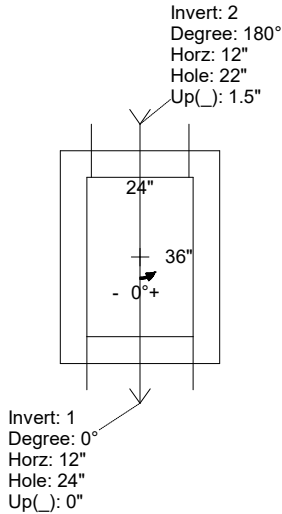


UPSIDE-DOWN VIEW (int. dimensions)

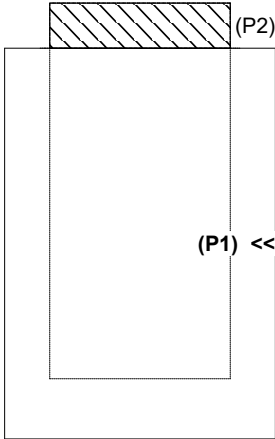

(P1) <<

(P2)

INSIDE WALL DIMENSIONS

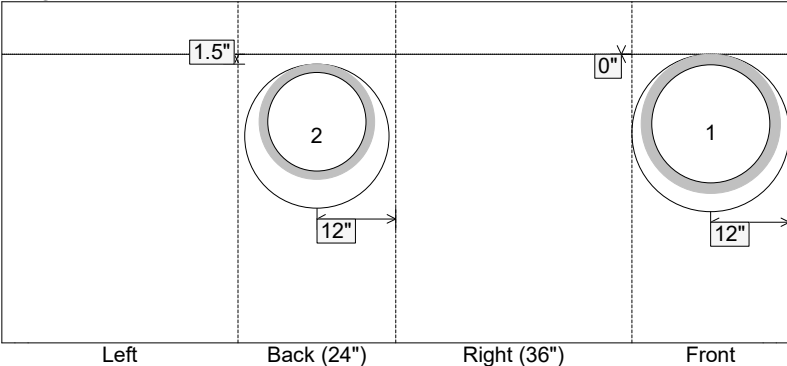

Left Back (24") Right (36") Front

EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 44" Height (Ext): 52"	Weight (Net): 3988 lb Volume (Net): 1.02cu.yd
----------------------------------	-------------------------------	--	--	--
