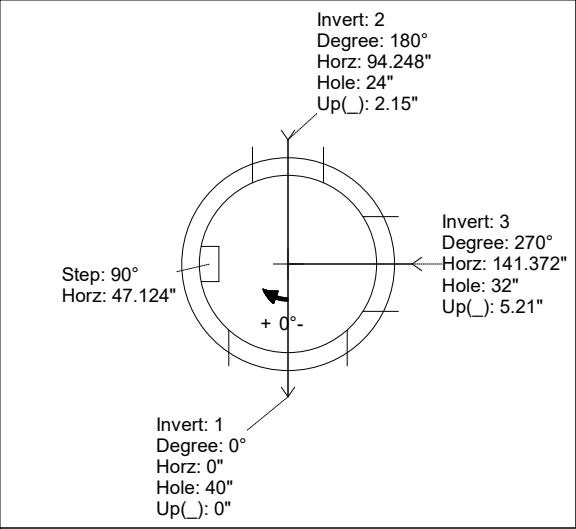
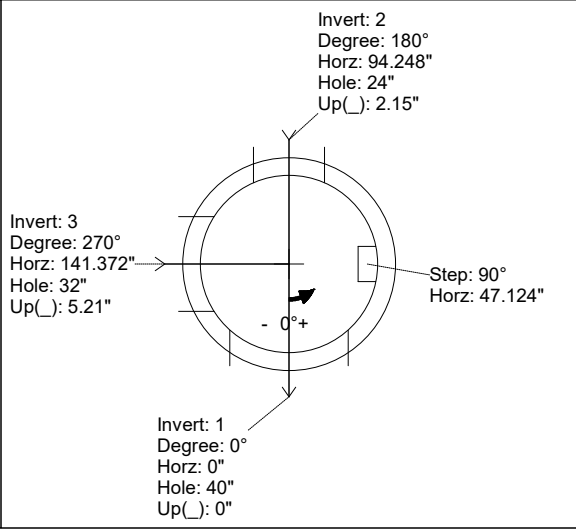

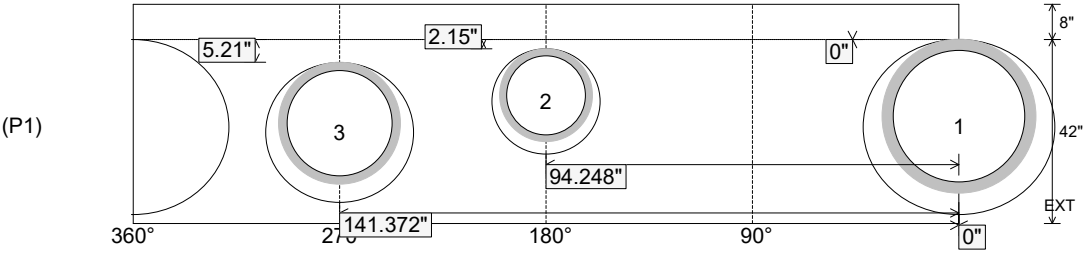


Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:38:26 PM		Tech: J. Coppage PC: E. Bradley														
Structure ID: 104 ST-MH																					
P1 MH060BAVF		MH BASE Custom Ht																			
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 60" - MH FLAT TOP w/24"x36" Hole - 8" P1) 60" - MH BASE Custom Ht - 42" 1) 60" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 40 1) Hole - 24 1) Hole - 32 3) MH Step ML-10-TDS-NCR - 10"						0 lb 2153 lb 5779 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7933 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT MH TYPE C / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.													
Rim: 607.88'		Rim to Invert: 4.49'		Slack: 0.43"		Sump: 2.55"		Step Position: 90°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset											
Invert 1	603.39'	0°	0"	30" HDPE	35.1"	Hole 40	40"	43.784"	0"	0"											
Invert 2	603.49'	180°	113.097"	18" HDPE	21.2"	Hole 24	24"	24.691"	2.15"	0"											
Invert 3	603.77'	270°	169.646"	24" HDPE	27.8"	Hole 32	32"	33.752"	5.21"	0"											
Invert 4																					
Invert 5																					
Invert 6																					
Invert 7																					
Invert 8																					
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)    INSIDE WALL DIMENSIONS 												Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 42" Height (Ext): 50"		Weight (Net): 5779 lb Volume (Net): 1.48cu.yd	
