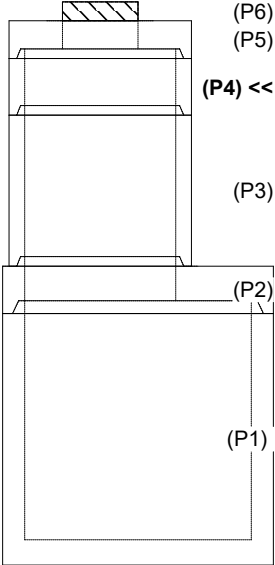
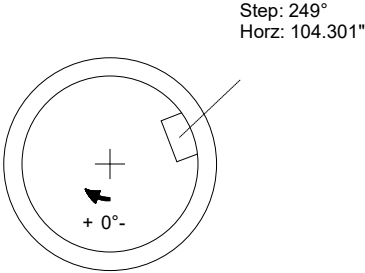



Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:42:53 PM		Tech: J. Coppage PC: E. Bradley						
Structure ID: 110 ST-MH													
P4 MH048RS18			MH RISER										
P6) 24" x 36" - CASTING HEIGHT - 6" P5) 48" - MH FLAT TOP w/24"x36" Hole - 12" P4) 48" - MH RISER - 18" P3) 48" - MH RISER - 48" P2) 72" - MH Transition Slab 48" Hole - 15" P1) 72" - MH BASE Custom Ht - 72" 1) 72" - Conseal CS-102 1.00" 3) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 52 13) MH Step ML-10-TDS-NCR - 10"						0 lb 1300 lb 1257 lb 3353 lb 3864 lb 11662 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 21437 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT MH TYPE K / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.					
Rim: 607.91' Rim to Invert: 14.48' Slack: 5.91' Sump: 3.15' Step Position: 249°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 18" Height (Ext): 18"		Weight (Net): 1257 lb Volume (Net): 0.32cu.yd				
