




Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:38:36 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 202 ST-MH											
P1 MH060BAVF		MH BASE Custom Ht									
P3) 24" x 48" - CASTING HEIGHT - 8" P2) 60" - MH FLAT TOP w/24"x48" Hole - 13" P1) 60" - MH BASE Custom Ht - 46" 1) 60" - Conseal CS-102 1.00" 1) 24" x 48" - Conseal CS-102 1.00" 1) Hole - 40 1) Hole - 24 4) MH Step ML-10-TDS-NCR - 10"						0 lb 2272 lb 6620 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 8892 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (NEENAH R-3287-15 PROVIDED BY OTHERS) 2. INDOT MH TYPE J / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.			
Rim: 607.39'		Rim to Invert: 5.38'		Slack: 0.11"		Sump: 2.55"		Step Position: 135°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	602.01'	0°	0"	30" HDPE	35.1"	Hole 40	40"	43.784"	0"	0"	
Invert 2	602.11'	270°	169.646"	18" HDPE	21.2"	Hole 24	24"	24.691"	2.15"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

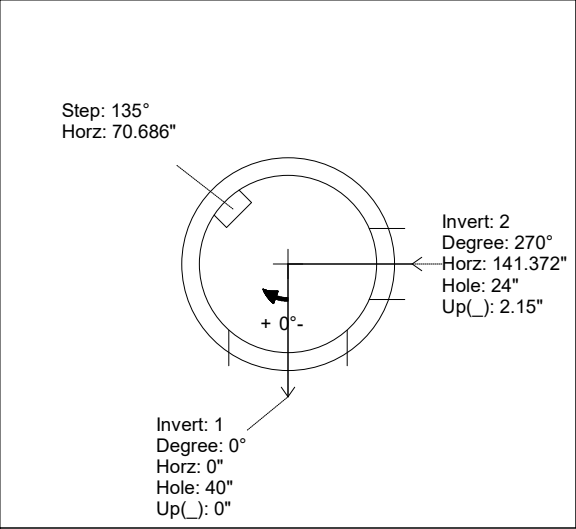

RIGHT-SIDE UP VIEW (int. dimensions)

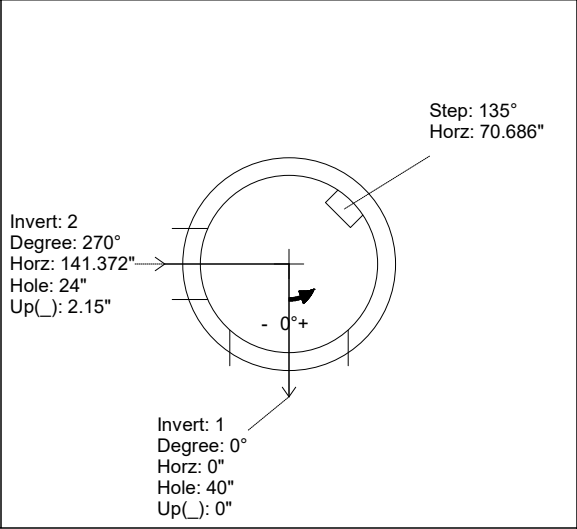

UPSIDE-DOWN VIEW (int. dimensions)

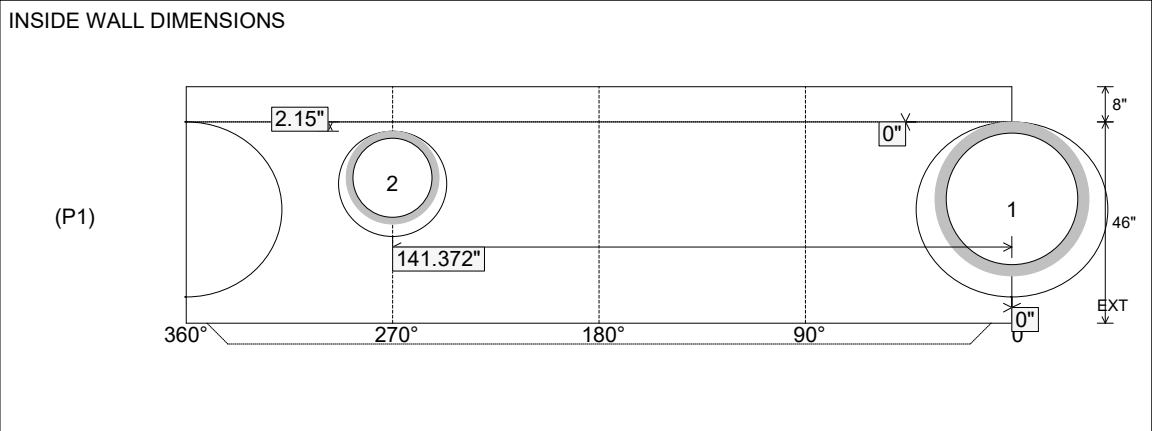

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 46" Height (Ext): 54"	Weight (Net): 6620 lb Volume (Net): 1.69cu.yd
----------------------------------	---------------------------------	--	--	--
