


Floor (Bot): 599.836'
Overall Height: 6.083'
Slack: 0.73"

1. (GREEN HAT CI3158-F PROVIDED BY OTHERS)
2. INDOT MH TYPE J / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.


P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 60" - MH FLAT TOP w/24"x36" Hole - 8"
P1) 60" - MH BASE Custom Ht - 51"
1) 60" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 44
1) Hole - 40
4) MH Step ML-10-TDS-NCR - 10"

0 lb
2153 lb
6534 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 8687 lb

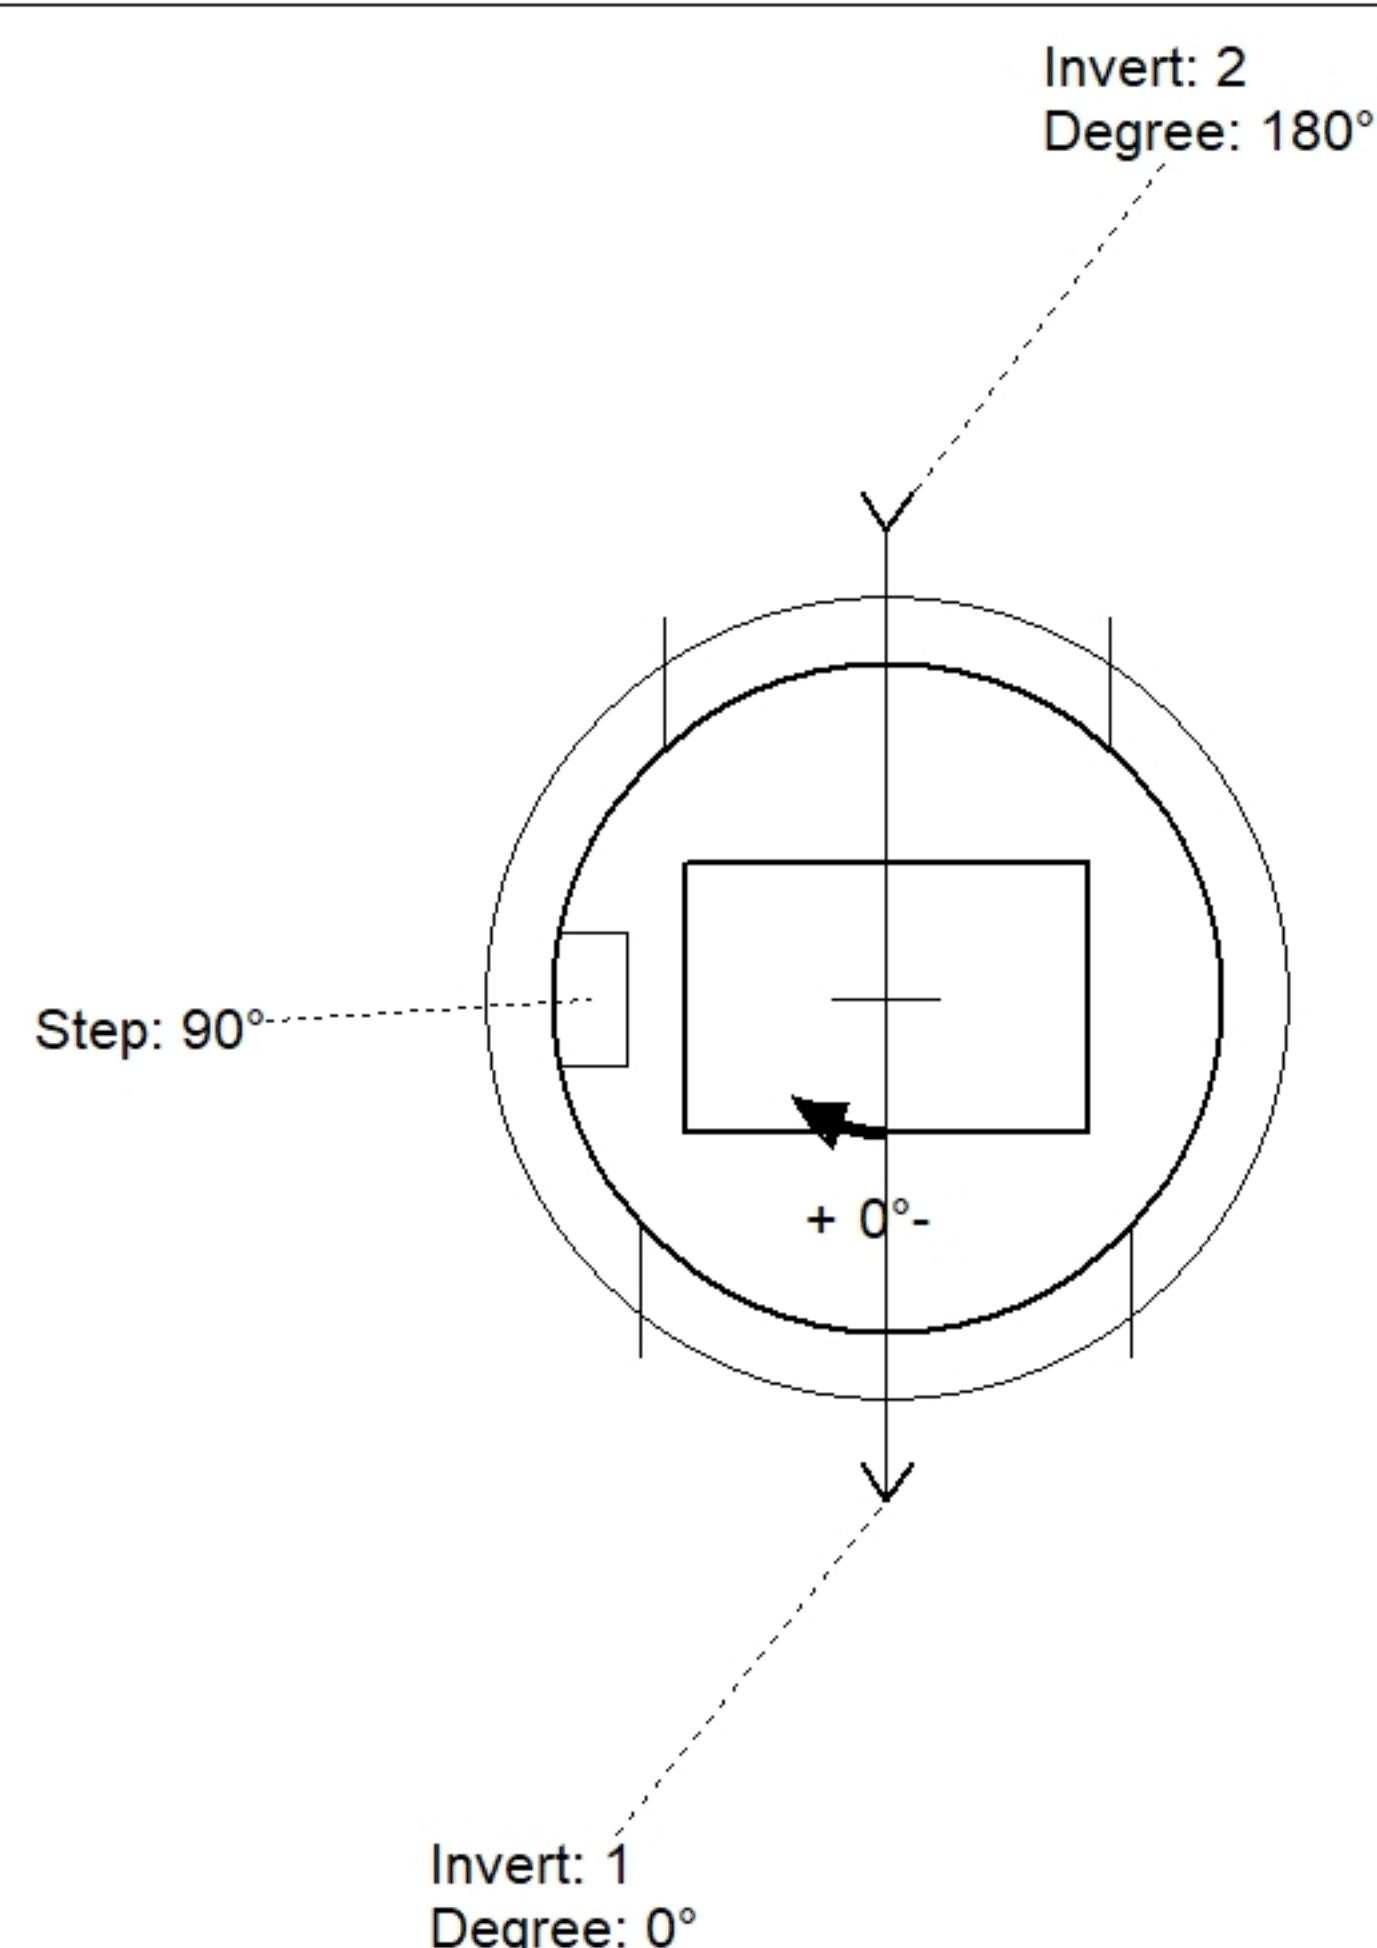

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	605.98'							
Reducer								
Invert 1	600.74'	0°	36" HDPE	41.7"	44"	Hole 44	0"	P1
Invert 2	600.84'	180°	30" HDPE	35.1"	40"	Hole 40	1.5"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

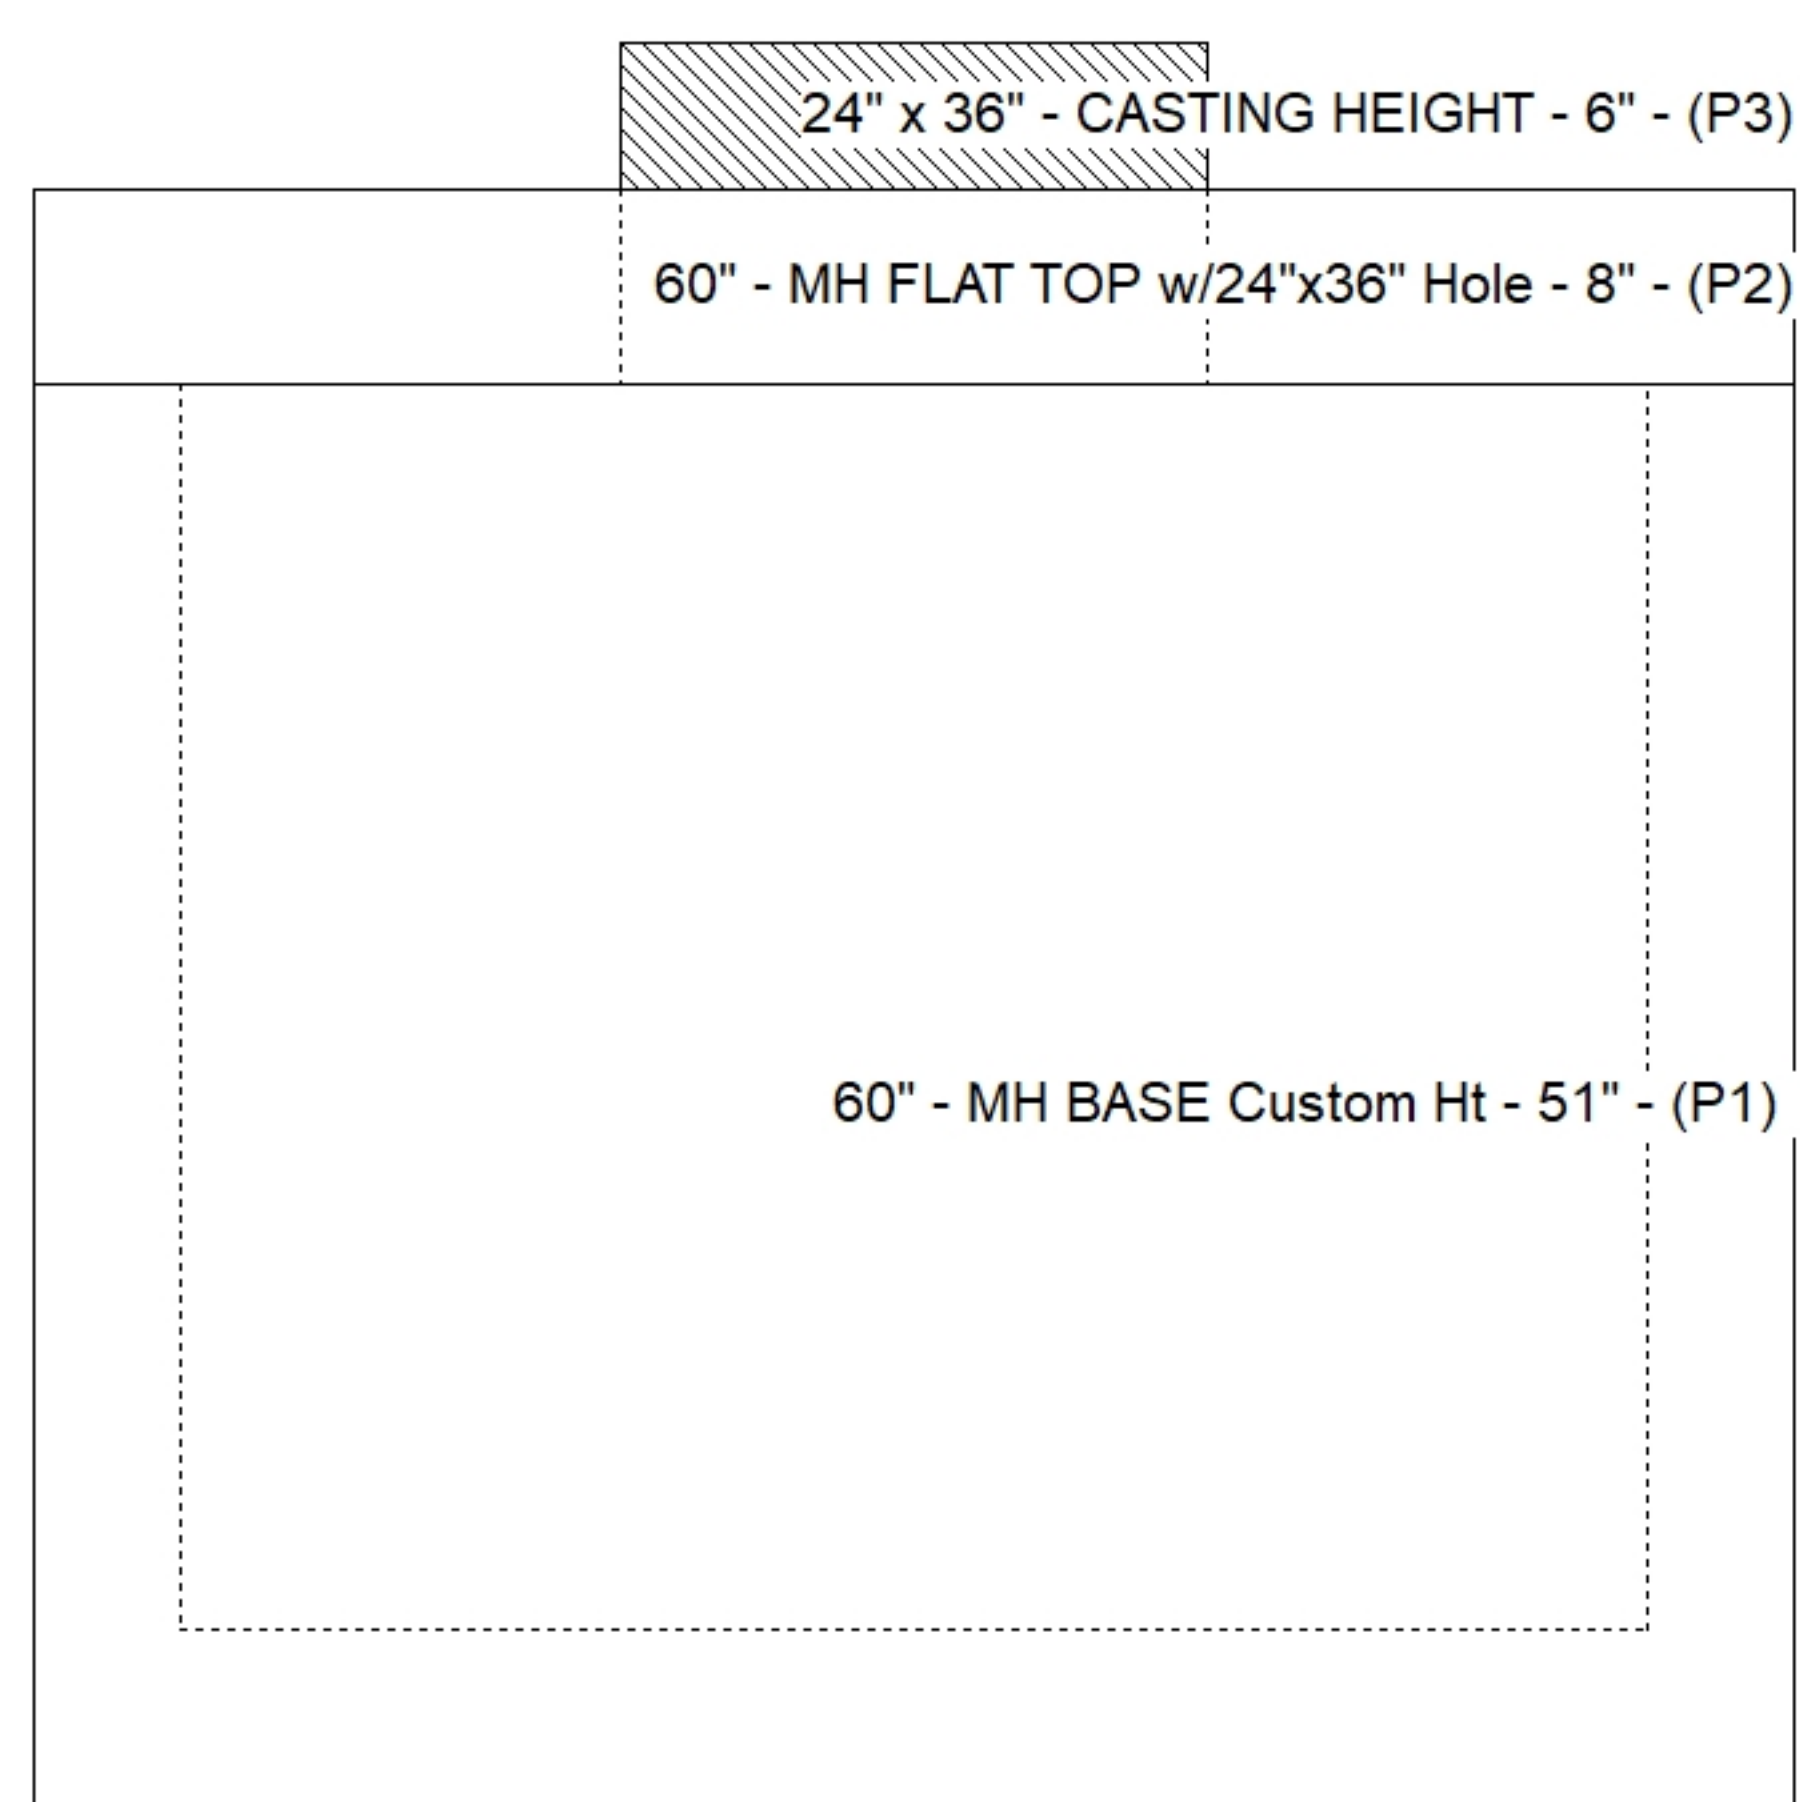

Default - Interior Dimensions

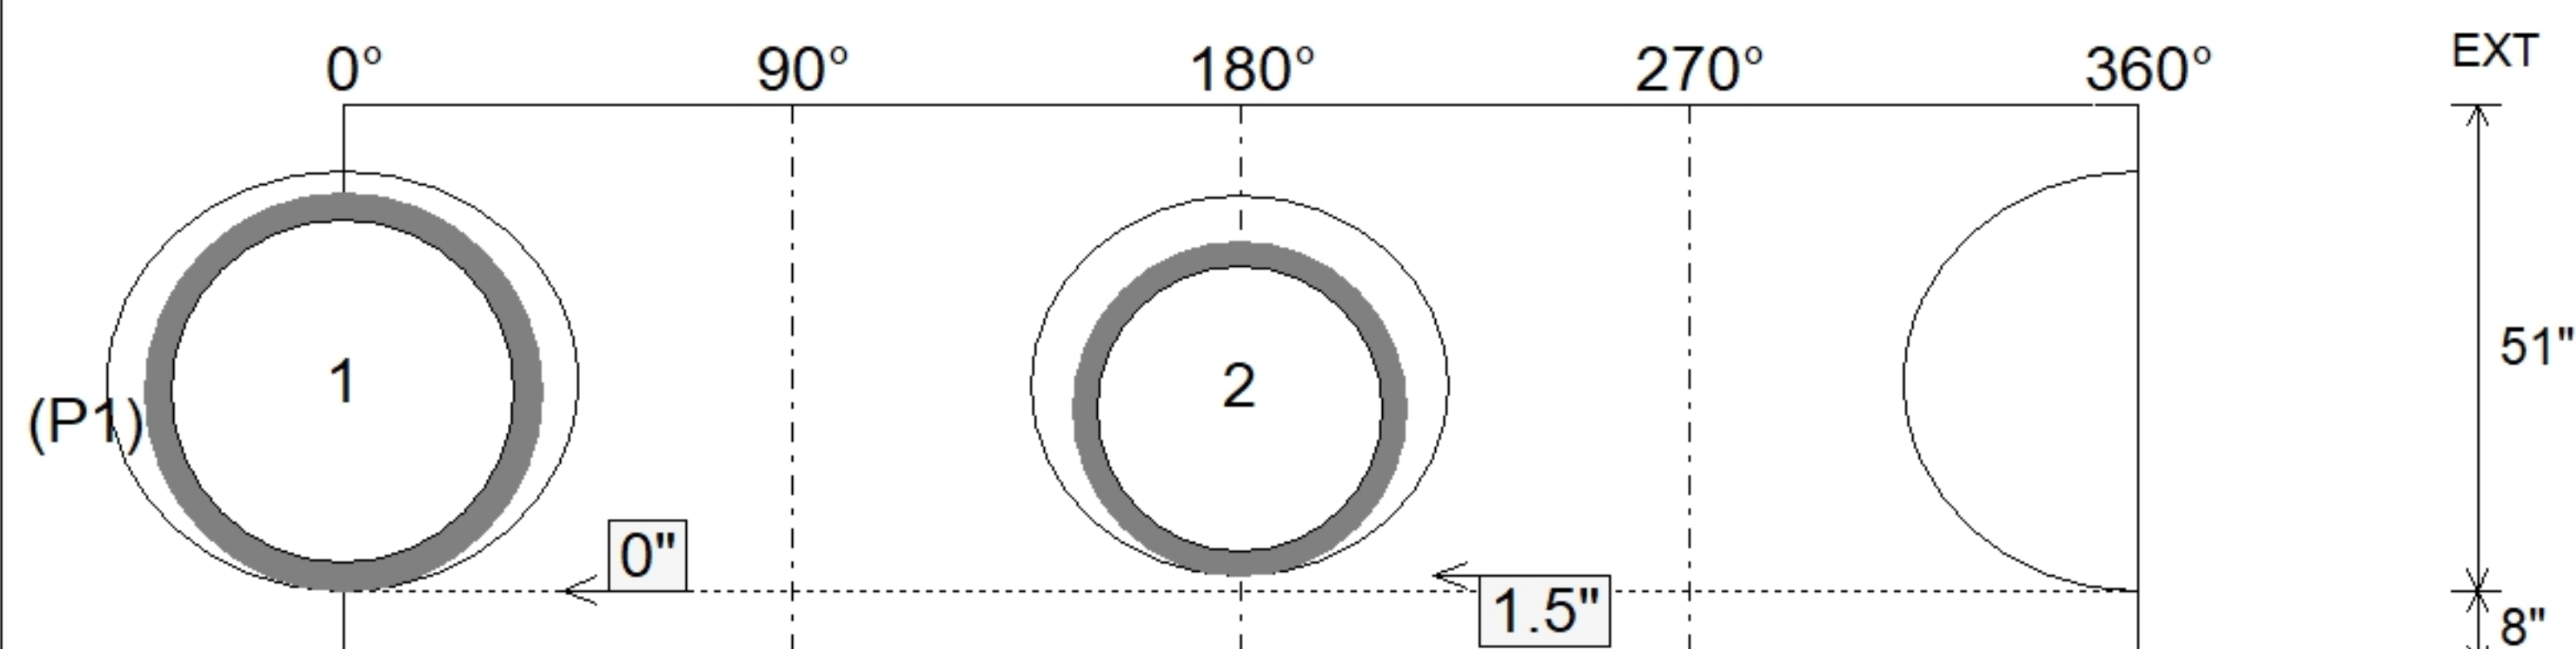

SUBMITTAL
APPROVED BY:
