



Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:38:37 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 204 ST-MH											
P1 MH072BAVF		MH BASE Custom Ht									
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 24" x 36" - GRADE RING - 4" P2) 72" - MH FLAT TOP w/24"x36" Hole - 15" P1) 72" - MH BASE Custom Ht - 60" 1) 72" - Conseal CS-102 1.00" 2) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 52 1) Hole - 44 5) MH Step ML-10-TDS-NCR - 10"					0 lb 408 lb 4530 lb 10330 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 15268 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT MH TYPE K / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.				
Rim: 606.39' Rim to Invert: 6.92' Slack: 1.19' Sump: 3.15' Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	599.47'	0°	0"	42" HDPE	47.7"	Hole 52	52"	58.105"	0"	0"	
Invert 2	599.57'	180°	135.088"	36" HDPE	41.7"	Hole 44	44"	47.337"	1.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

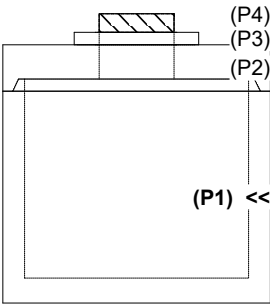


(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

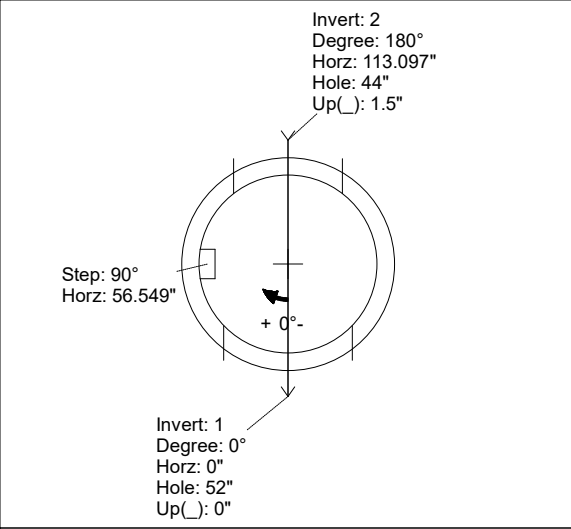

UPSIDE-DOWN VIEW (int. dimensions)

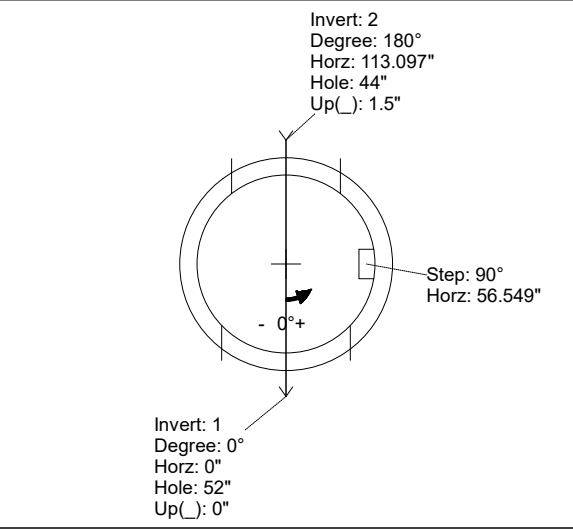

INSIDE WALL DIMENSIONS

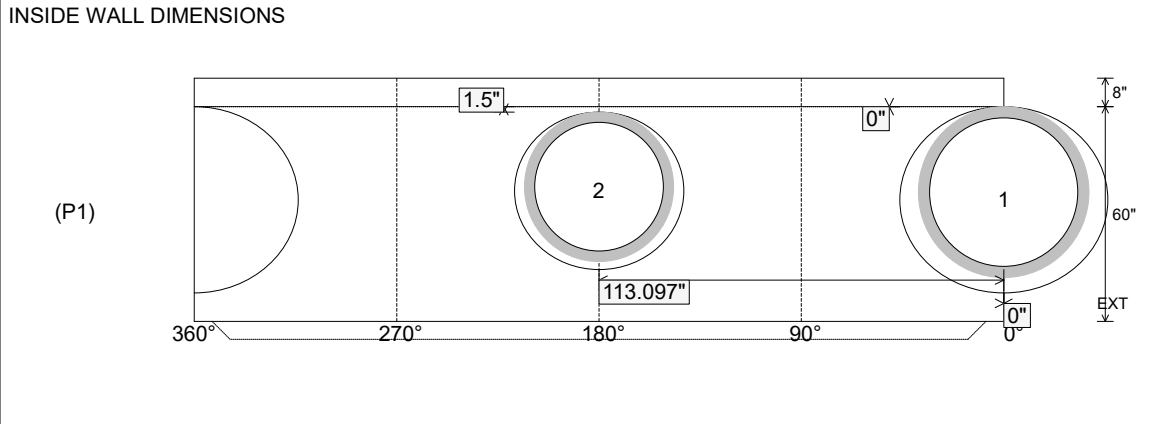

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 7" Floor Height: 8"	Height (Int): 60" Height (Ext): 68"	Weight (Net): 10330 lb Volume (Net): 2.64cu.yd
----------------------------------	---------------------------------	--	--	---
