




Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:38:39 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 206 ST-MH											
P1 MH072BAVF		MH BASE Custom Ht									
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 72" - MH FLAT TOP w/24"x36" Hole - 15" P2) 72" - MH RISER - 12" P1) 72" - MH BASE Custom Ht - 84" 2) 72" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 50 2) Hole - 24 8) MH Step ML-10-TDS-NCR - 10"					0 lb 4530 lb 1749 lb 13099 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT MH TYPE K / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.				
Structure Total:					19378 lb						
Rim: 606.38' Rim to Invert: 9.5' Slack: 0.156" Sump: 3.156" Step Position: 234°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	596.88'	0°	0"	42" HDPE	47.7"	Hole 50	50"	55.271"	0.006"	0"	
Invert 2	596.98'	95°	71.297"	42" HDPE	47.7"	Hole 50	50"	55.271"	1.206"	0"	
Invert 3	601.25'	180°	135.088"	18" HDPE	21.2"	Hole 24	24"	24.468"	53.996"	0"	
Invert 4	600.2'	288°	216.142"	18" HDPE	21.2"	Hole 24	24"	24.468"	41.396"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											

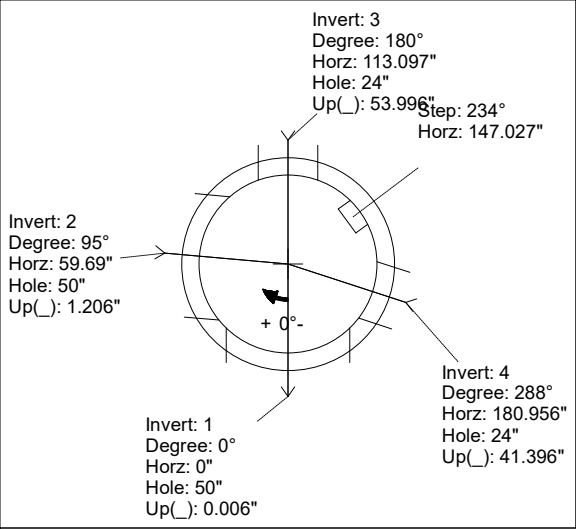

RIGHT-SIDE UP VIEW (int. dimensions)

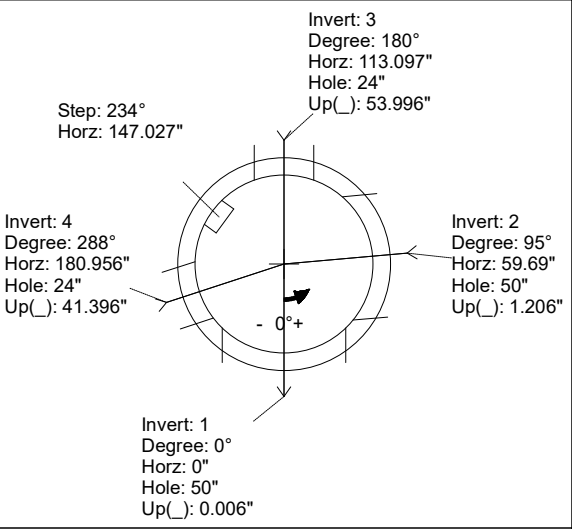

UPSIDE-DOWN VIEW (int. dimensions)

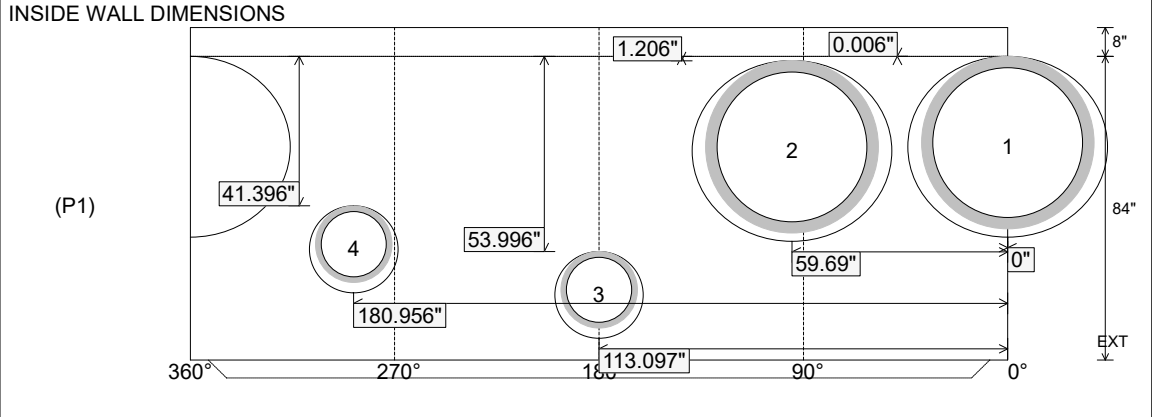

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 7" Floor Height: 8"	Height (Int): 84" Height (Ext): 92"	Weight (Net): 13099 lb Volume (Net): 3.35cu.yd
----------------------------------	---------------------------------	--	--	---
