




Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:38:40 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 208 ST-MH											
P1 MH048BAVF			MH BASE Custom Ht								
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole - 7" P1) 48" - MH BASE Custom Ht - 26" 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 24 2) MH Step ML-10-TDS-NCR - 10"						0 lb 1044 lb 2949 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 3994 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT MH TYPE C / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W. - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..			
Rim: 605.52'		Rim to Invert: 3.25'		Slack: 1.6"		Sump: 1.6"		Step Position: 180°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	602.27'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											




RIGHT-SIDE UP VIEW (int. dimensions)

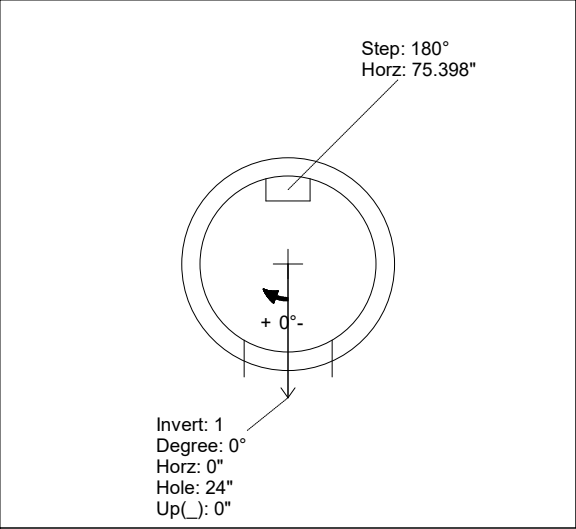

UPSIDE-DOWN VIEW (int. dimensions)

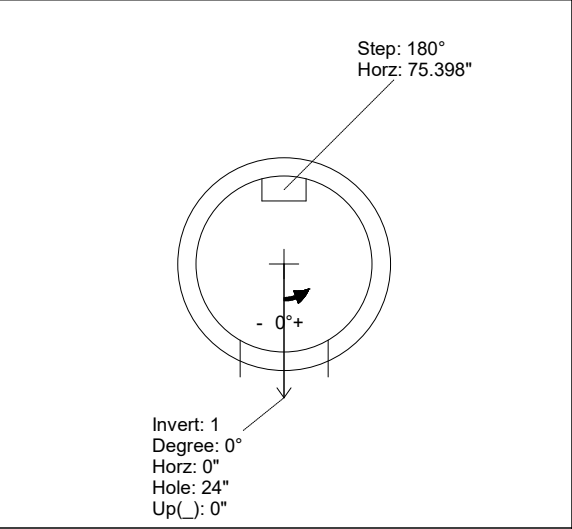

INSIDE WALL DIMENSIONS

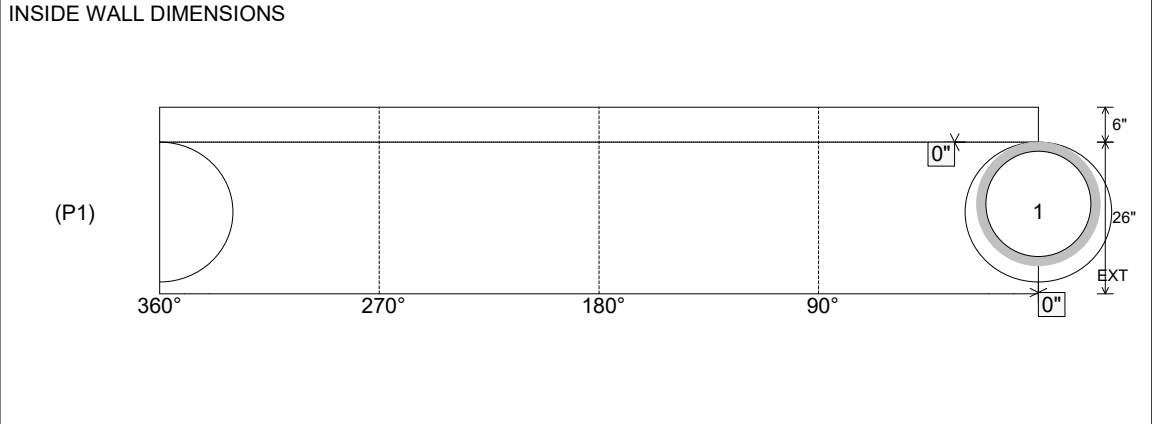

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 26" Height (Ext): 32"	Weight (Net): 2949 lb Volume (Net): 0.75cu.yd
----------------------------------	-------------------------------	--	--	--
