




Floor (Bot): 601.637'
Overall Height: 3.75'
Slack: 1.6"

1. (GREEN HAT CI3158-F PROVIDED BY OTHERS)
2. INDOT MH TYPE C / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..

P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 7"
P1) 48" - MH BASE Custom Ht - 26"
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 24
2) MH Step ML-10-TDS-NCR - 10"



0 lb
1044 lb
2949 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 3994 lb

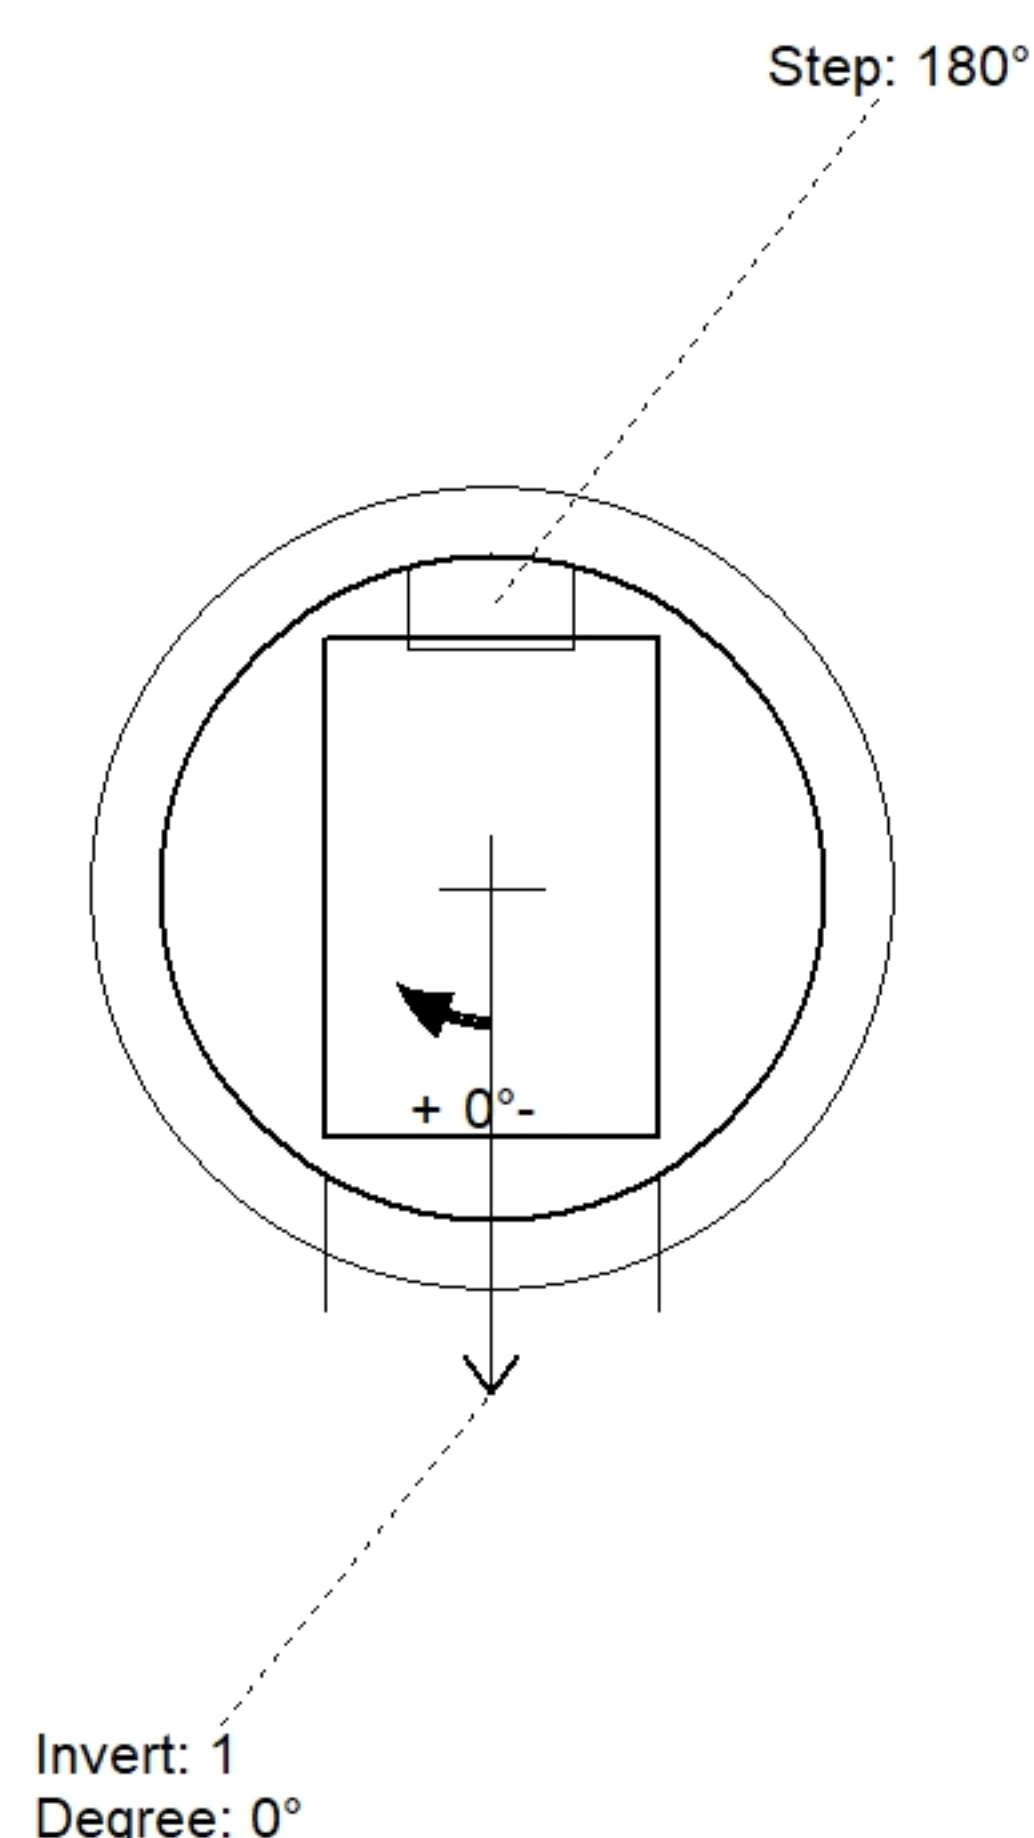

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	605.52'							
Reducer								
Invert 1	602.27'	0°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

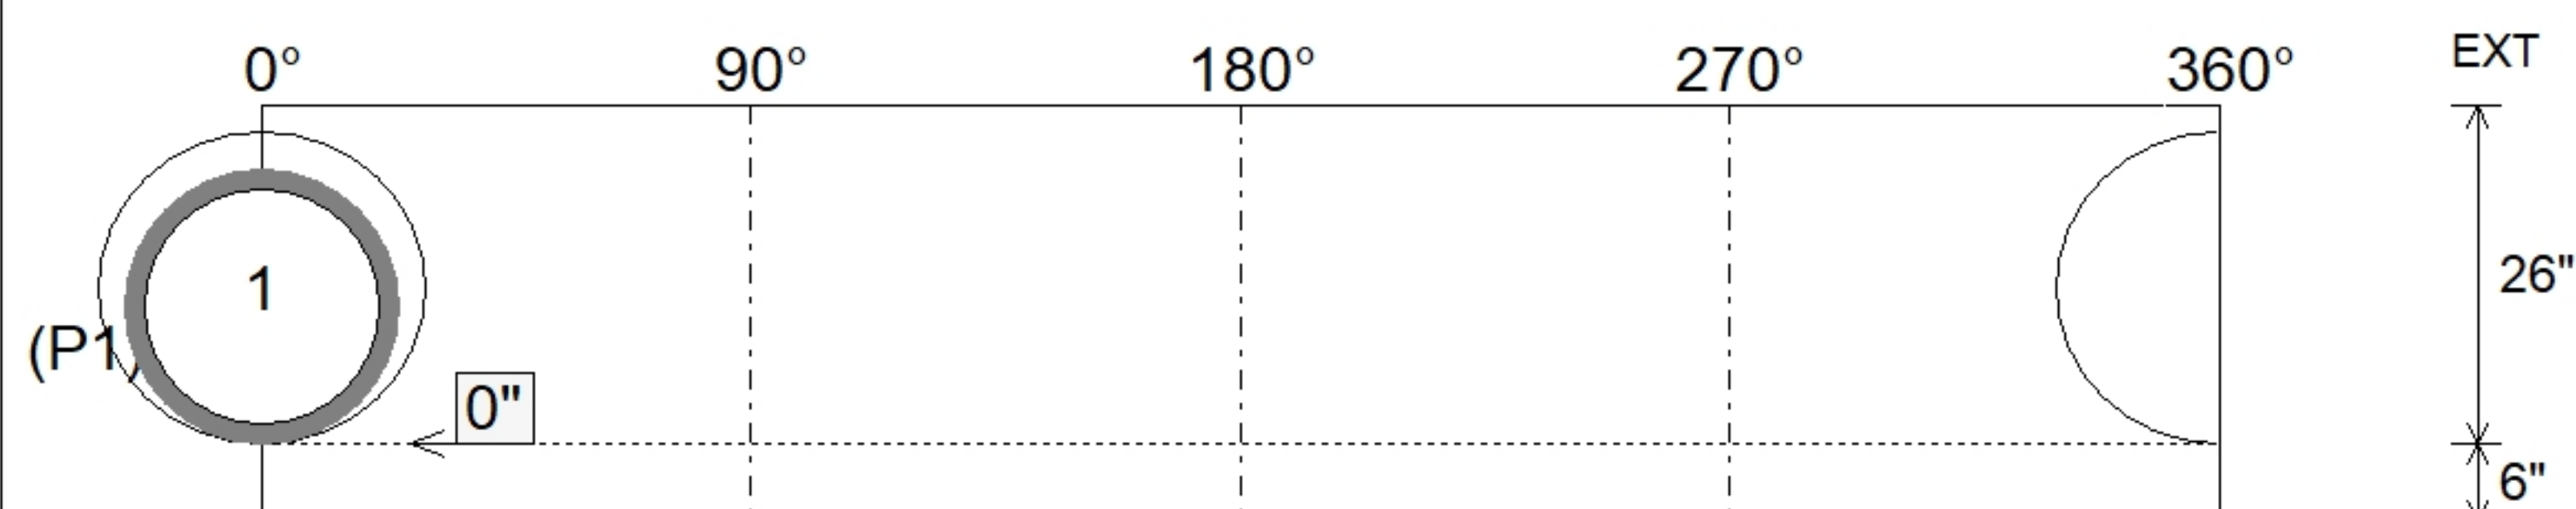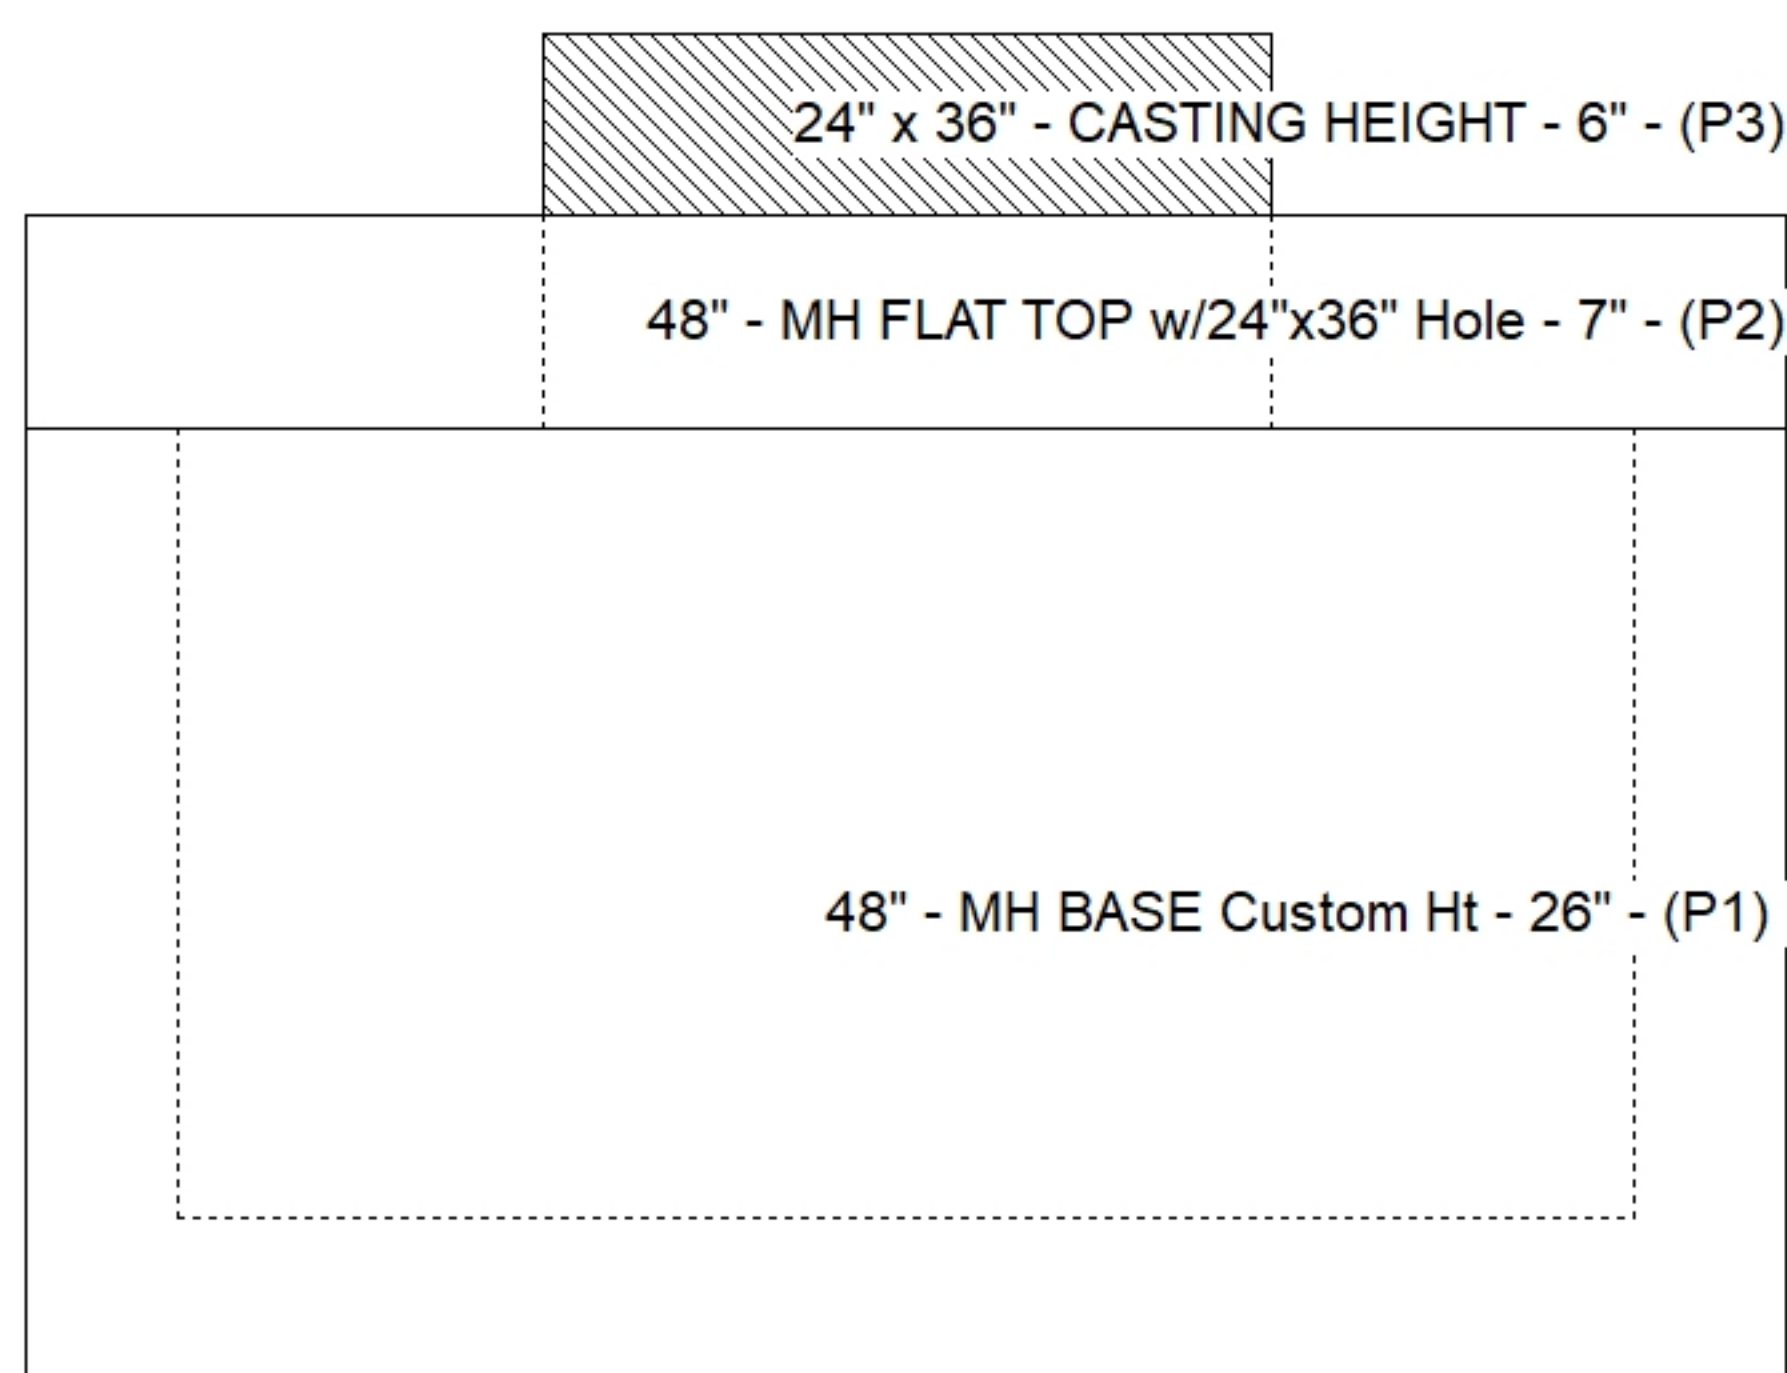

SUBMITTAL
APPROVED BY:
