

Job Name: 26-2212 - CDTI Building 1
Job Location: Charlestown, IN
Contractor: Dan Cristiani Excavating Co. Inc.

Plant: Beaver Dam

Tech: J. Coppage

8/18/2026 12:40:37 PM

PC: E. Bradley



Structure ID: 209 ST-MH

P4 MH048LD12-24X36RECT

MH FLAT TOP w/24"x36" Hole



- P5) 24" x 36" - CASTING HEIGHT - 7"
P4) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P3) 48" - MH RISER Custom Ht - 57"
P2) 72" - MH Transition Slab 48" Hole - 15"
P1) 72" - MH BASE Custom Ht - 72"
1) 72" - Conseal CS-102 1.00"
2) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 50
1) Hole - 24
12) MH Step ML-10-TDS-NCR - 10"

0 lb
1300 lb
3785 lb
3864 lb
11890 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 20839 lb

Structure Notes:

INDOT STATE PROJECT

1. (GREEN HAT CB2436-7-F PROVIDED BY OTHERS)
2. INDOT MH TYPE K / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #4 BARS AT 10" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

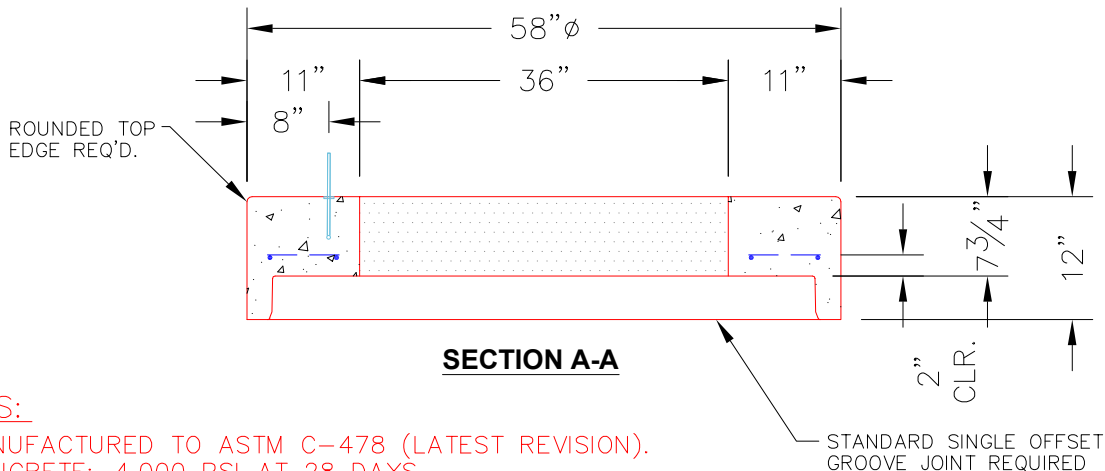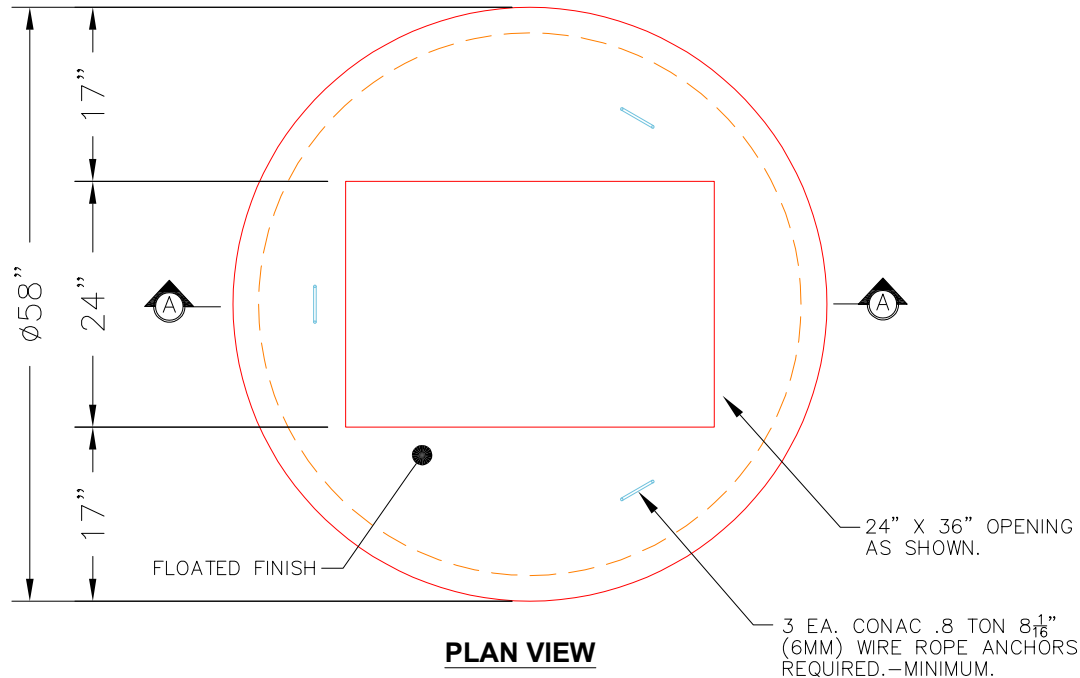

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #4 BAR @ 10" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1300 lb
Volume (Net): 0.46cu.yd
