



Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:42:59 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 211 ST-MH											
P4 MH048RSVF		MH RISER Custom Ht									
P6) 24" x 36" - CASTING HEIGHT - 7" P5) 48" - MH FLAT TOP w/24"x36" Hole - 7" P4) 48" - MH RISER Custom Ht - 30" P3) 48" - MH RISER Custom Ht - 63" P2) 72" - MH Transition Slab 48" Hole - 15" P1) 72" - MH BASE Custom Ht - 67" 1) 72" - Conseal CS-102 1.00" 3) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 58 2) Hole - 32 14) MH Step ML-10-TDS-NCR - 10"					0 lb 1044 lb 1870 lb 3900 lb 3864 lb 10159 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 20838 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CB2436-7-F PROVIDED BY OTHERS) 2. INDOT MH TYPE K / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.				
Rim: 607.73' Rim to Invert: 15.51' Slack: 0.07" Sump: 2.95" Step Position: 45°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2	603.14'	90°	45.553"	24" HDPE	27.8"	Hole 32	32"	35.027"	-17.16"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

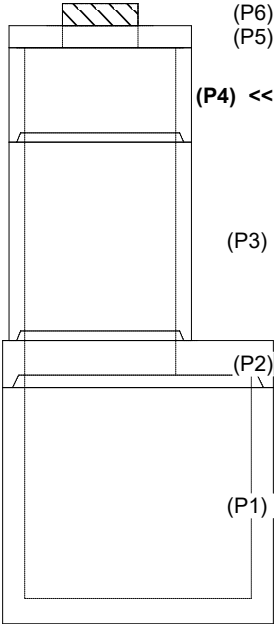

(P6)
(P5)
(P4) <<
(P3)
(P2)
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)

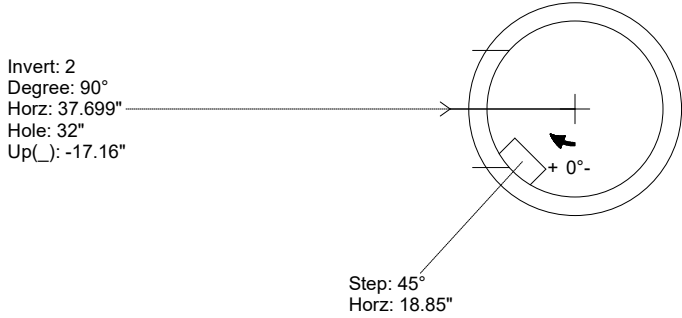


Invert: 2
Degree: 90°
Horz: 37.699"
Hole: 32"
Up(): -17.16"

Step: 45°
Horz: 18.85"

+ 0°

INSIDE WALL DIMENSIONS



(P4)

0° 90° 180° 270° 360°

37.699"

2

-17.16"

EXT 30"

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 30" Height (Ext): 30"	Weight (Net): 1870 lb Volume (Net): 0.48cu.yd
----------------------------------	----------------------------------	--	--	--
