

Job Name: 26-2212 - CDTI Building 1
Job Location: Charlestown, IN
Contractor: Dan Cristiani Excavating Co. Inc.

Plant: Beaver Dam

8/18/2026 12:40:39 PM

Tech: J. Coppage

PC: E. Bradley



Structure ID: 211 ST-MH

P5 MH048LD07-24X36RECT

MH FLAT TOP w/24"x36" Hole

P6) 24" x 36" - CASTING HEIGHT - 7"
P5) 48" - MH FLAT TOP w/24"x36" Hole - 7"
P4) 48" - MH RISER Custom Ht - 30"
P3) 48" - MH RISER Custom Ht - 63"
P2) 72" - MH Transition Slab 48" Hole - 15"
P1) 72" - MH BASE Custom Ht - 67"
1) 72" - Conseal CS-102 1.00"
3) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 58
2) Hole - 32
14) MH Step ML-10-TDS-NCR - 10"



0 lb
1044 lb
1870 lb
3900 lb
3864 lb
10159 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 20838 lb

Structure Notes:

INDOT STATE PROJECT

1. (GREEN HAT CB2436-7-F PROVIDED BY OTHERS)
2. INDOT MH TYPE K / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #4 BARS AT 10" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

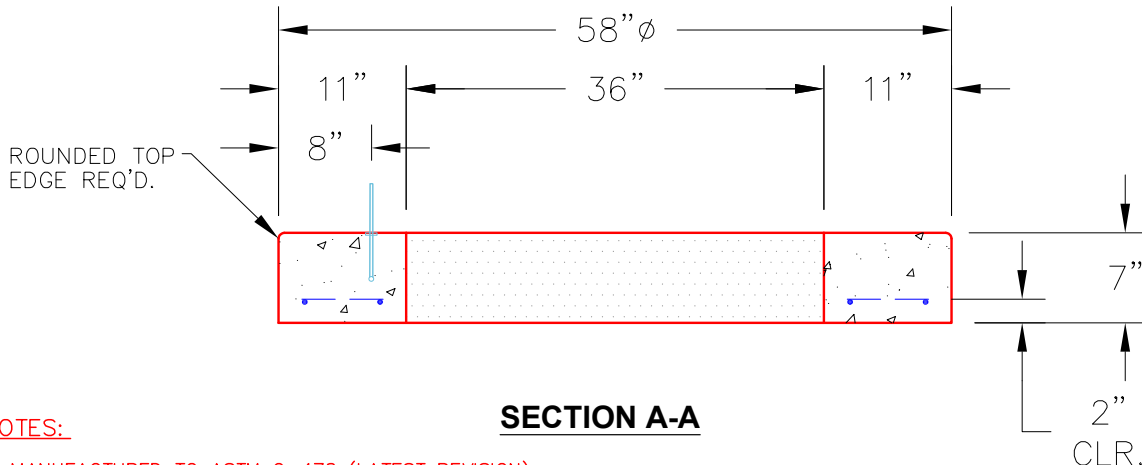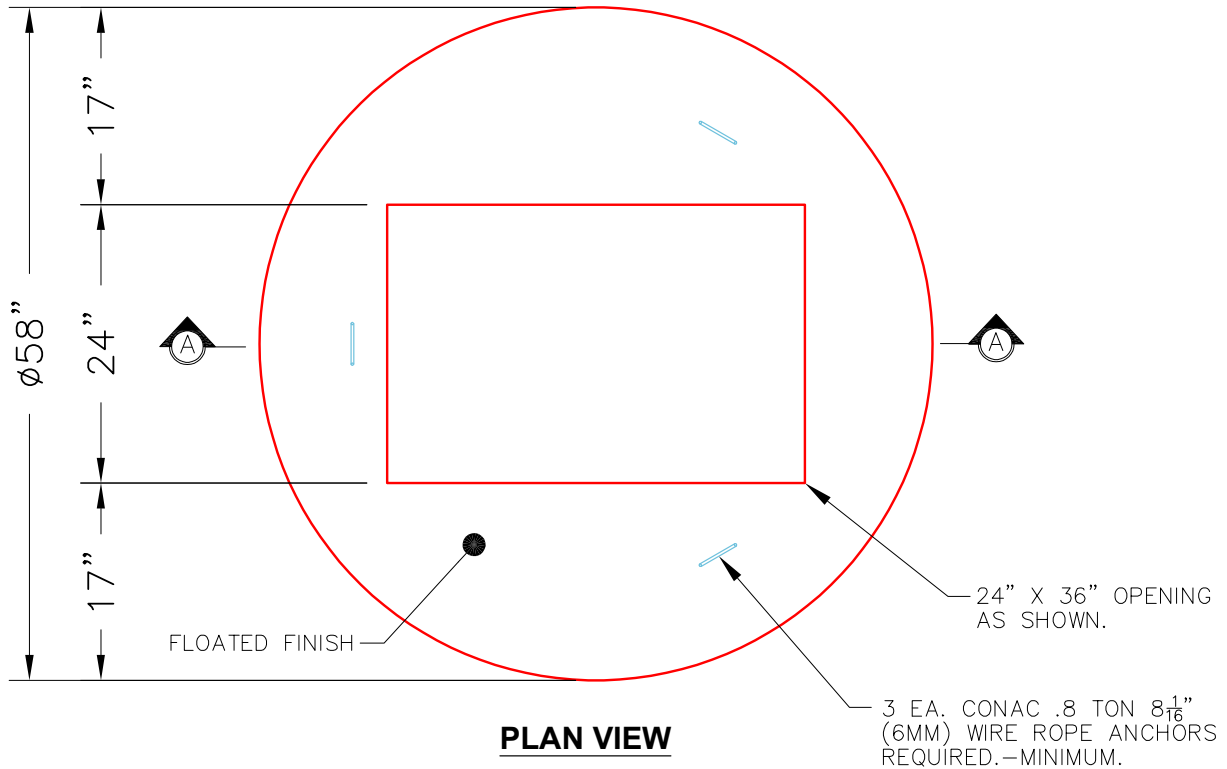

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #4 BAR @ 10" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 5"

Height (Ext): 7"

Weight (Net): 1044 lb
Volume (Net): 0.27cu.yd
