




Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:38:43 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 212 ST-MH											
P1 MH048BAVF		MH BASE Custom Ht									
P3) 34" x 34" - RECESS/GRATE SEAT - 1" P2) 48" - MH FLAT TOP w/30"x30" Hole W/ Recess for Grate - 7" P1) 48" - MH BASE Custom Ht - 37" 1) 48" - Conseal CS-102 1.00" 1) 30" x 30" - Conseal CS-102 1.00" 1) Hole - 32 3) MH Step ML-10-TDS-NCR - 10"						0 lb 1022 lb 3552 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4573 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CB3030BH-F PROVIDED BY OTHERS) 2. INDOT MH TYPE C / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W. - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. 6. A 1" DEEP X 2.25" WIDE RECESS SHALL BE PLACED ON THE INSIDE PERIMETER OF THE TOP SLAB FOR THE GRATE TO RECESS INTO.			
Rim: 604.53'		Rim to Invert: 3.67'		Slack: 1.94"		Sump: 1.9"		Step Position: 180°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	600.86'	0°	0"	24" HDPE	27.8"	Hole 32	32"	35.027"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

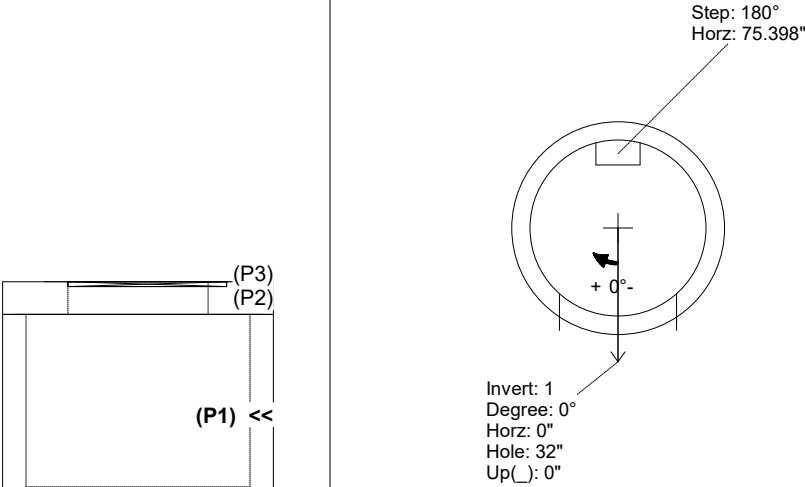

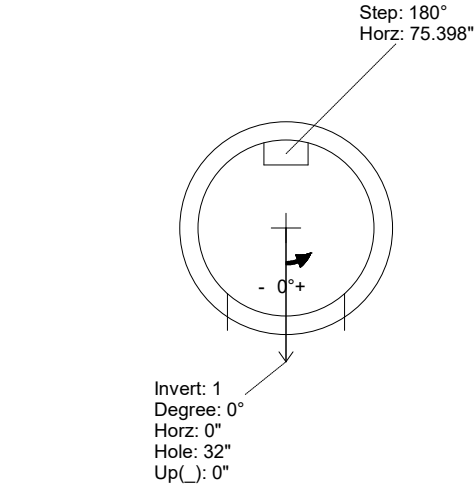

INSIDE WALL DIMENSIONS

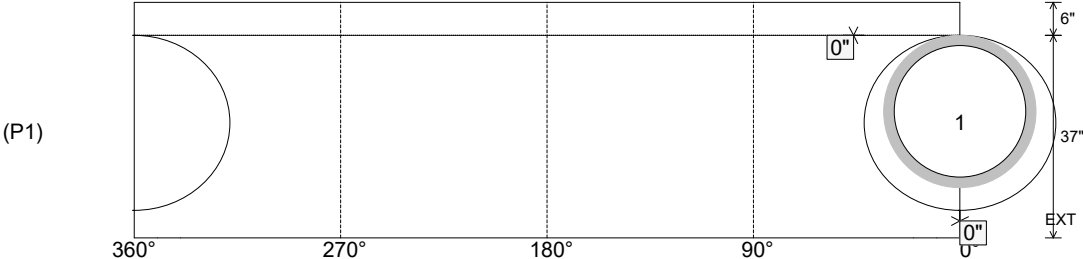

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 37" Height (Ext): 43"	Weight (Net): 3552 lb Volume (Net): 0.91cu.yd
----------------------------------	-------------------------------	--	--	--
