

Job Name: 26-2212 - CDTI Building 1
Job Location: Charlestown, IN
Contractor: Dan Cristiani Excavating Co. Inc.

Plant: Beaver Dam

Tech: J. Coppage

8/18/2026 12:40:41 PM

PC: E. Bradley



Structure ID: 213 ST-MH

P2 MH072TS15-48ECC

MH Transition Slab 48" Hole

P6) 24" x 36" - CASTING HEIGHT - 7"
P5) 48" - MH FLAT TOP w/24"x36" Hole - 7"
P4) 48" - MH RISER Custom Ht - 52"
P3) 48" - MH RISER - 48"
P2) 72" - MH Transition Slab 48" Hole - 15"
P1) 72" - MH BASE Custom Ht - 84"
1) 72" - Conseal CS-102 1.00"
3) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 58
1) DOGHOUSE INVRTD - 32"x32"
16) MH Step ML-10-TDS-NCR - 10"

0 lb
1044 lb
3189 lb
3353 lb
3864 lb
12637 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 24088 lb


Structure Notes:

INDOT STATE PROJECT


1. (GREEN HAT CB2436-7-F PROVIDED BY OTHERS)
2. INDOT MH TYPE C / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB AS SHOWN BELOW
 - RISER/WALLS (As .12)
 - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #4 & #5 BAR AS SHOWN (GRADE 60).
4. TONGUE REQUIRED OFFSET FOR 48"Ø COMPONENTS.

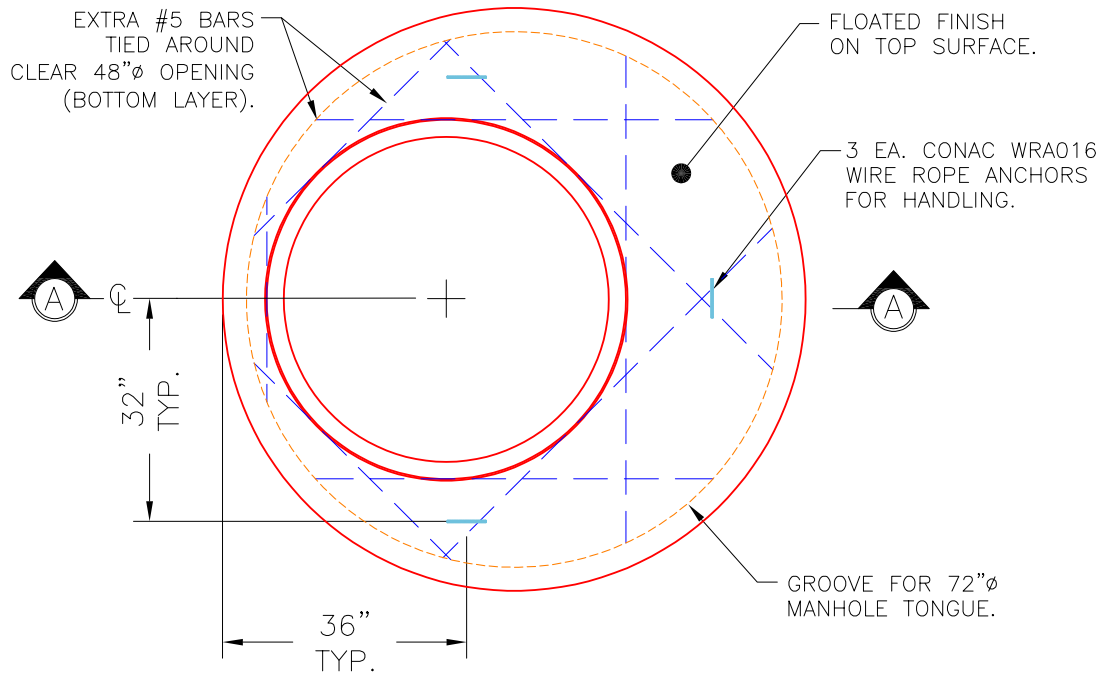

PLAN VIEW

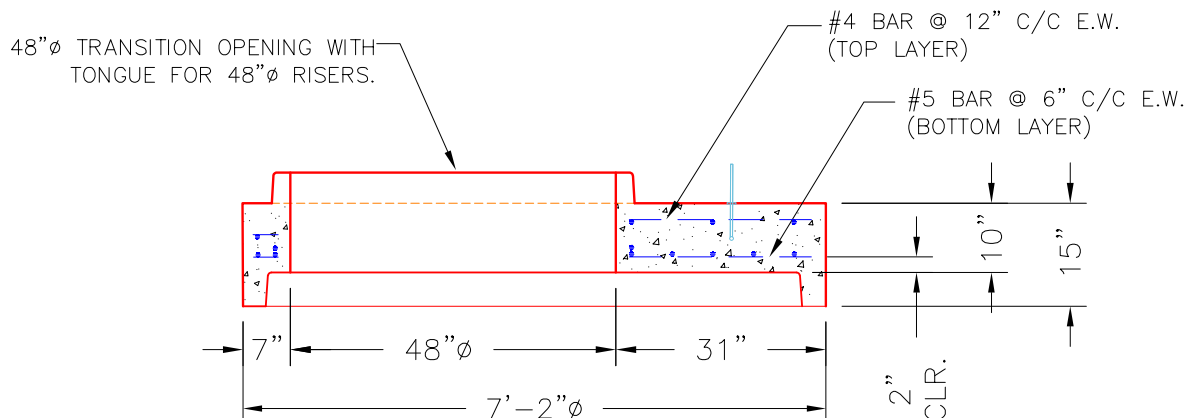

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 7"

Height (Ext): 15"

Weight (Net): 3864 lb
Volume (Net): 0.99cu.yd
