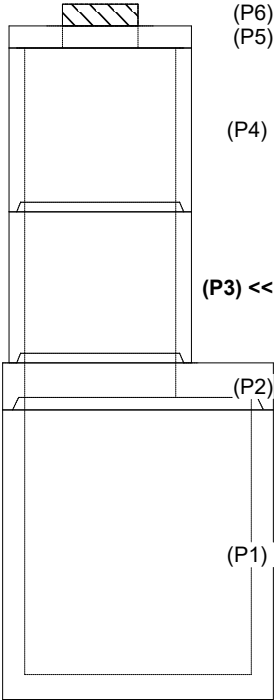




Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:43:01 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 213 ST-MH											
P3 MH048RS48			MH RISER								
P6) 24" x 36" - CASTING HEIGHT - 7" P5) 48" - MH FLAT TOP w/24"x36" Hole - 7" P4) 48" - MH RISER Custom Ht - 52" P3) 48" - MH RISER - 48" P2) 72" - MH Transition Slab 48" Hole - 15" P1) 72" - MH BASE Custom Ht - 84" 1) 72" - Conseal CS-102 1.00" 3) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 58 1) DOGHOUSE INVRTD - 32"x32" 16) MH Step ML-10-TDS-NCR - 10"					0 lb 1044 lb 3189 lb 3353 lb 3864 lb 12637 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CB2436-7-F PROVIDED BY OTHERS) 2. INDOT MH TYPE C / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.				
Structure Total: 24088 lb											
Rim: 607.73' Rim to Invert: 17.61' Slack: 1.27" Sump: 2.95" Step Position: 270°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd	
