

Job Name: 26-2212 - CDTI Building 1
Job Location: Charlestown, IN
Contractor: Dan Cristiani Excavating Co. Inc.

Plant: Beaver Dam

8/18/2026 12:40:46 PM

Tech: J. Coppage

PC: E. Bradley



Structure ID: 216 ST-MH

P2 MH048LD12CC

MH FLAT LID w/24" Center Hole

- P3) 24" - CASTING HEIGHT - 1"
P2) 48" - MH FLAT LID w/24" Center Hole - 12"
P1) 48" - MH BASE Custom Ht - 54"
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 24"
4) MH Step ML-10-TDS-NCR - 10"

Structure Total:



0 lb
1580 lb
4708 lb
0 lb
0 lb
0 lb
0 lb

6288 lb

Structure Notes:

INDOT STATE PROJECT

1. (GREEN HAT MG-BH4342-F PROVIDED BY OTHERS)
2. INDOT MH TYPE C / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - RISER/WALLS (As .12)
 - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..

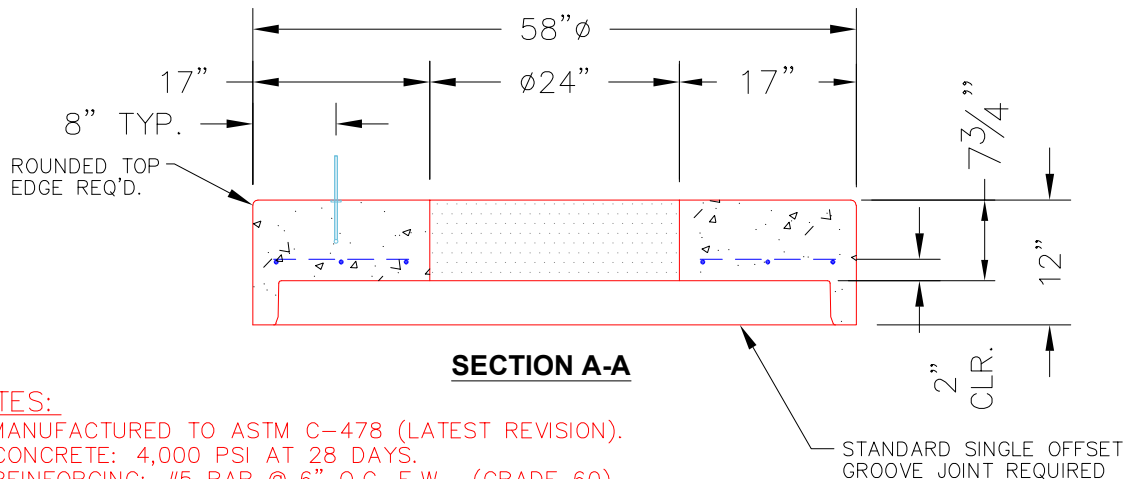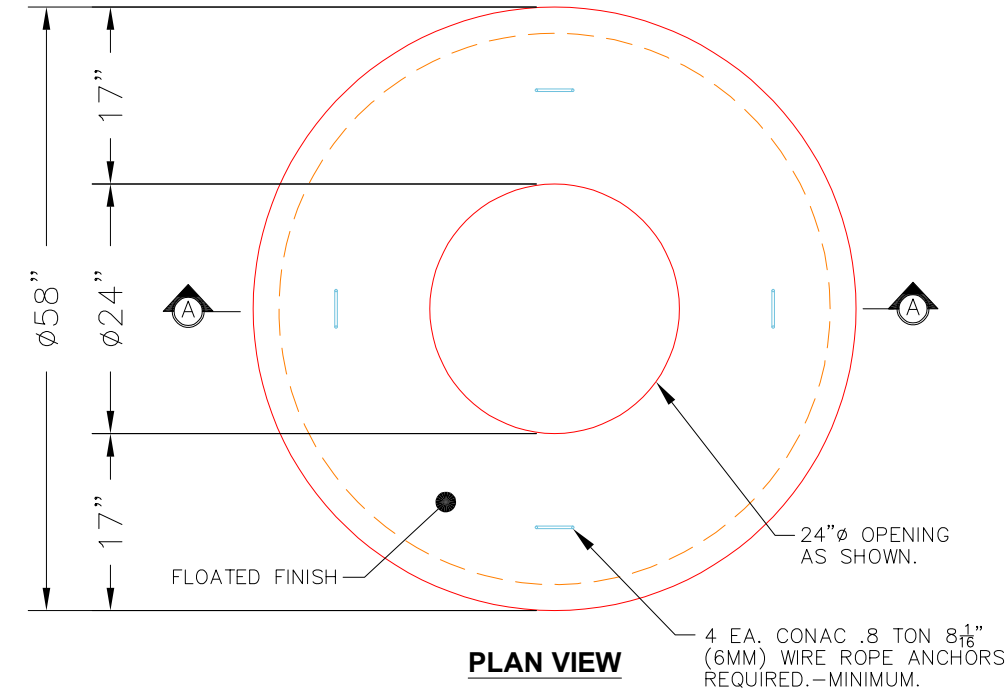

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1580 lb
Volume (Net): 0.39cu.yd
