


Floor (Bot): 598.817'
Overall Height: 6.083'
Slack: 2.88"

1. (GREEN HAT MG-BH4342-F PROVIDED BY OTHERS)
2. INDOT MH TYPE C / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..


P3) 24" - CASTING HEIGHT - 1"
P2) 48" - MH FLAT LID w/24" Center Hole - 12"
P1) 48" - MH BASE Custom Ht - 54"
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 24
4) MH Step ML-10-TDS-NCR - 10"

0 lb
1580 lb
4708 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 6288 lb

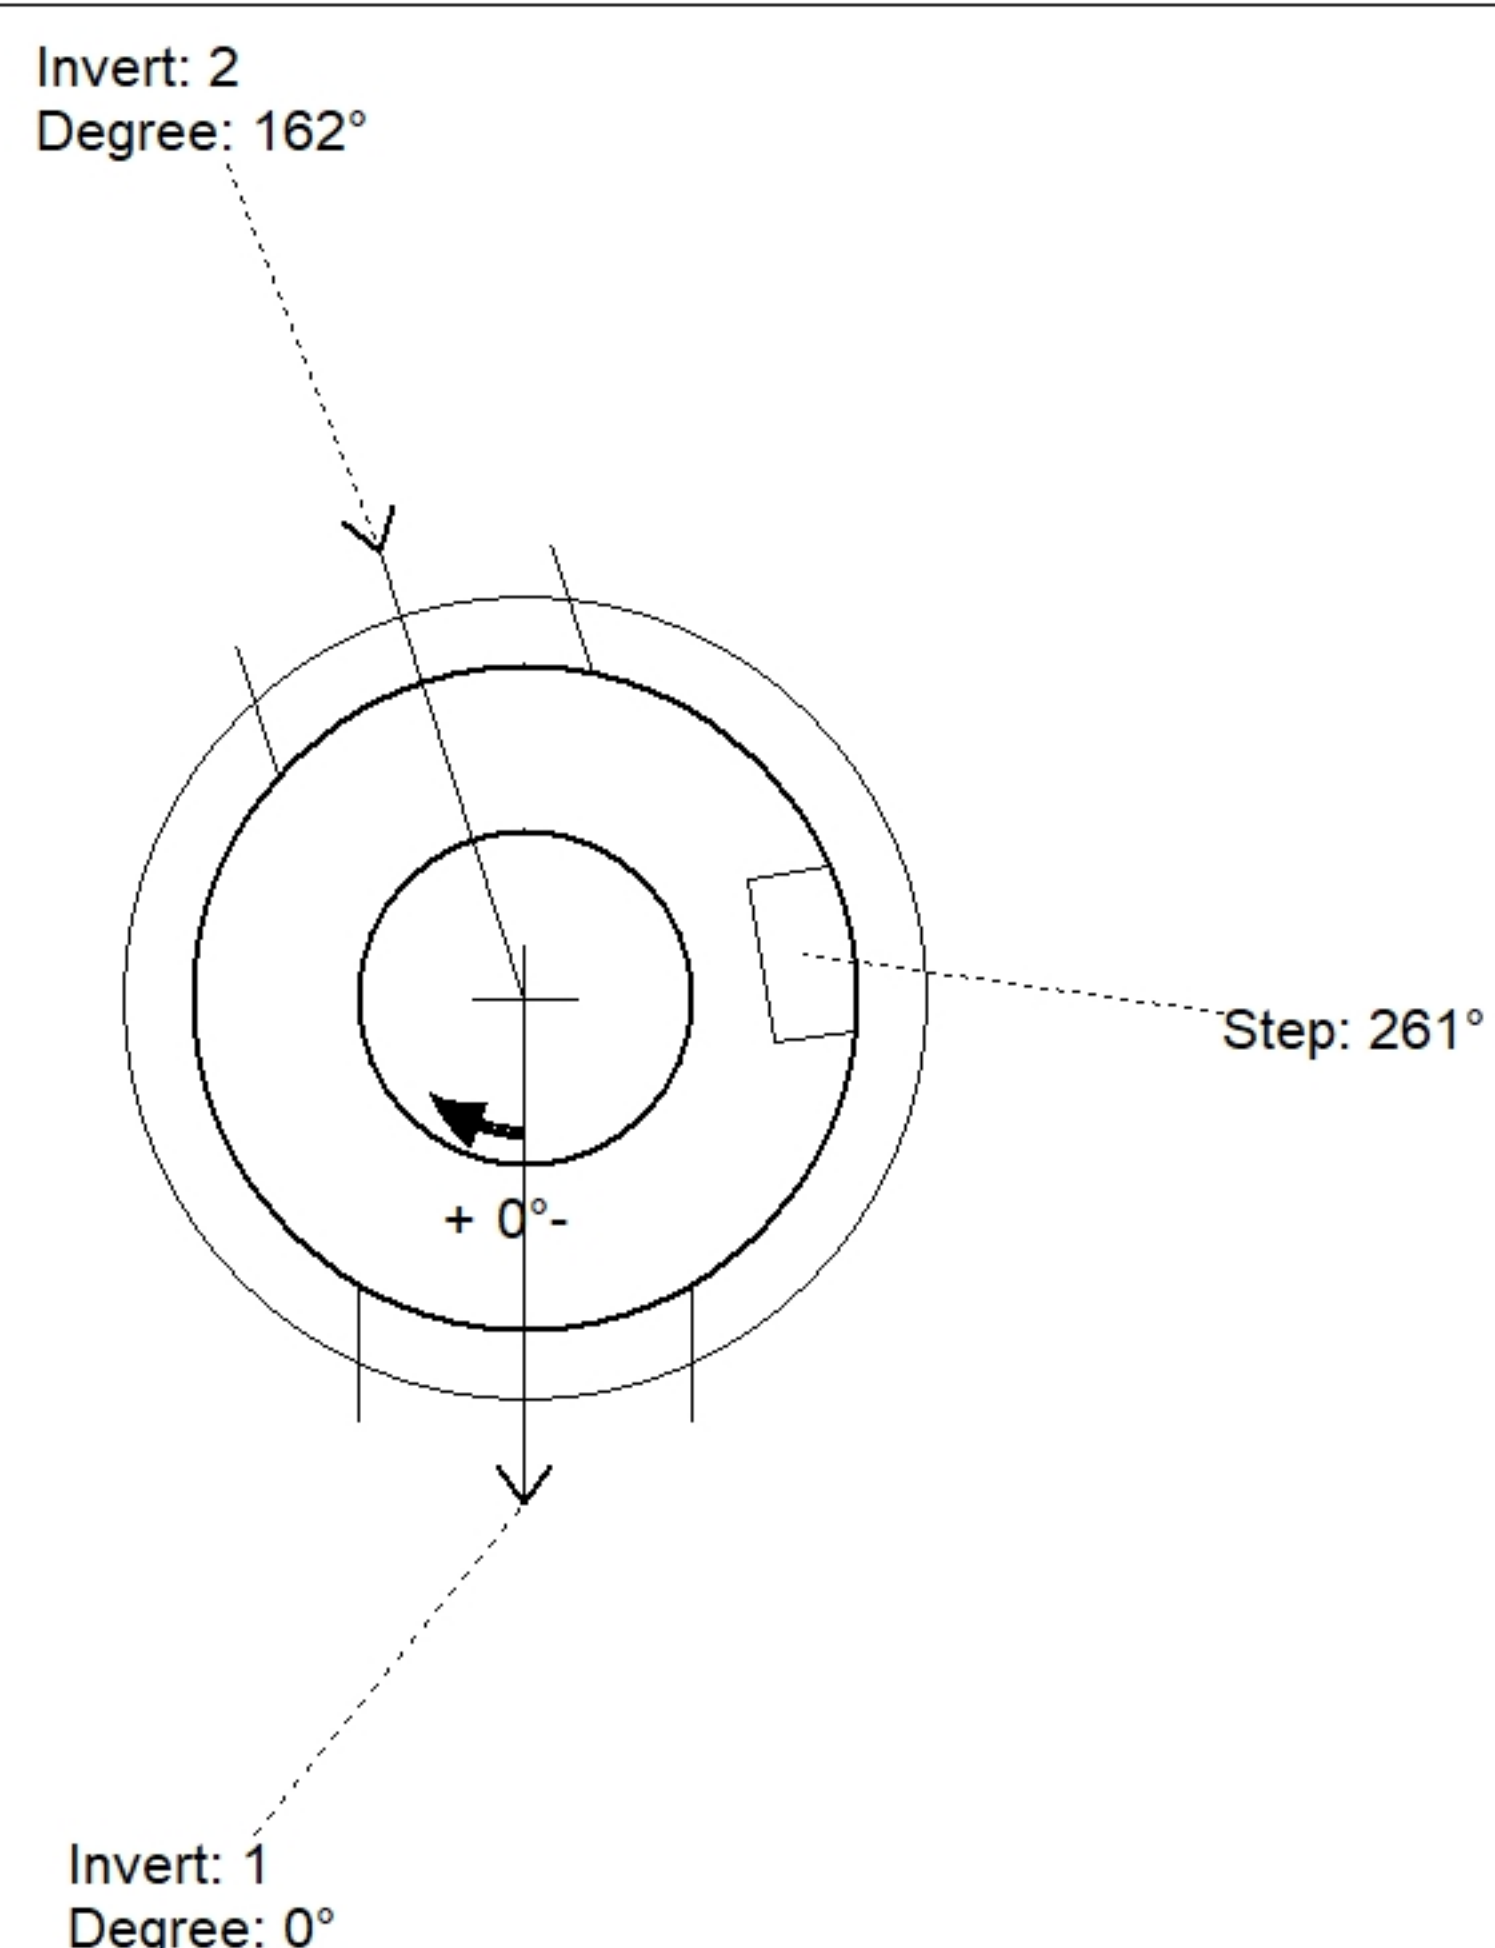

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	605.14'							
Reducer								
Invert 1	599.45'	0°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 2	599.55'	162°	18" HDPE	21.2"	24"	Hole 24	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

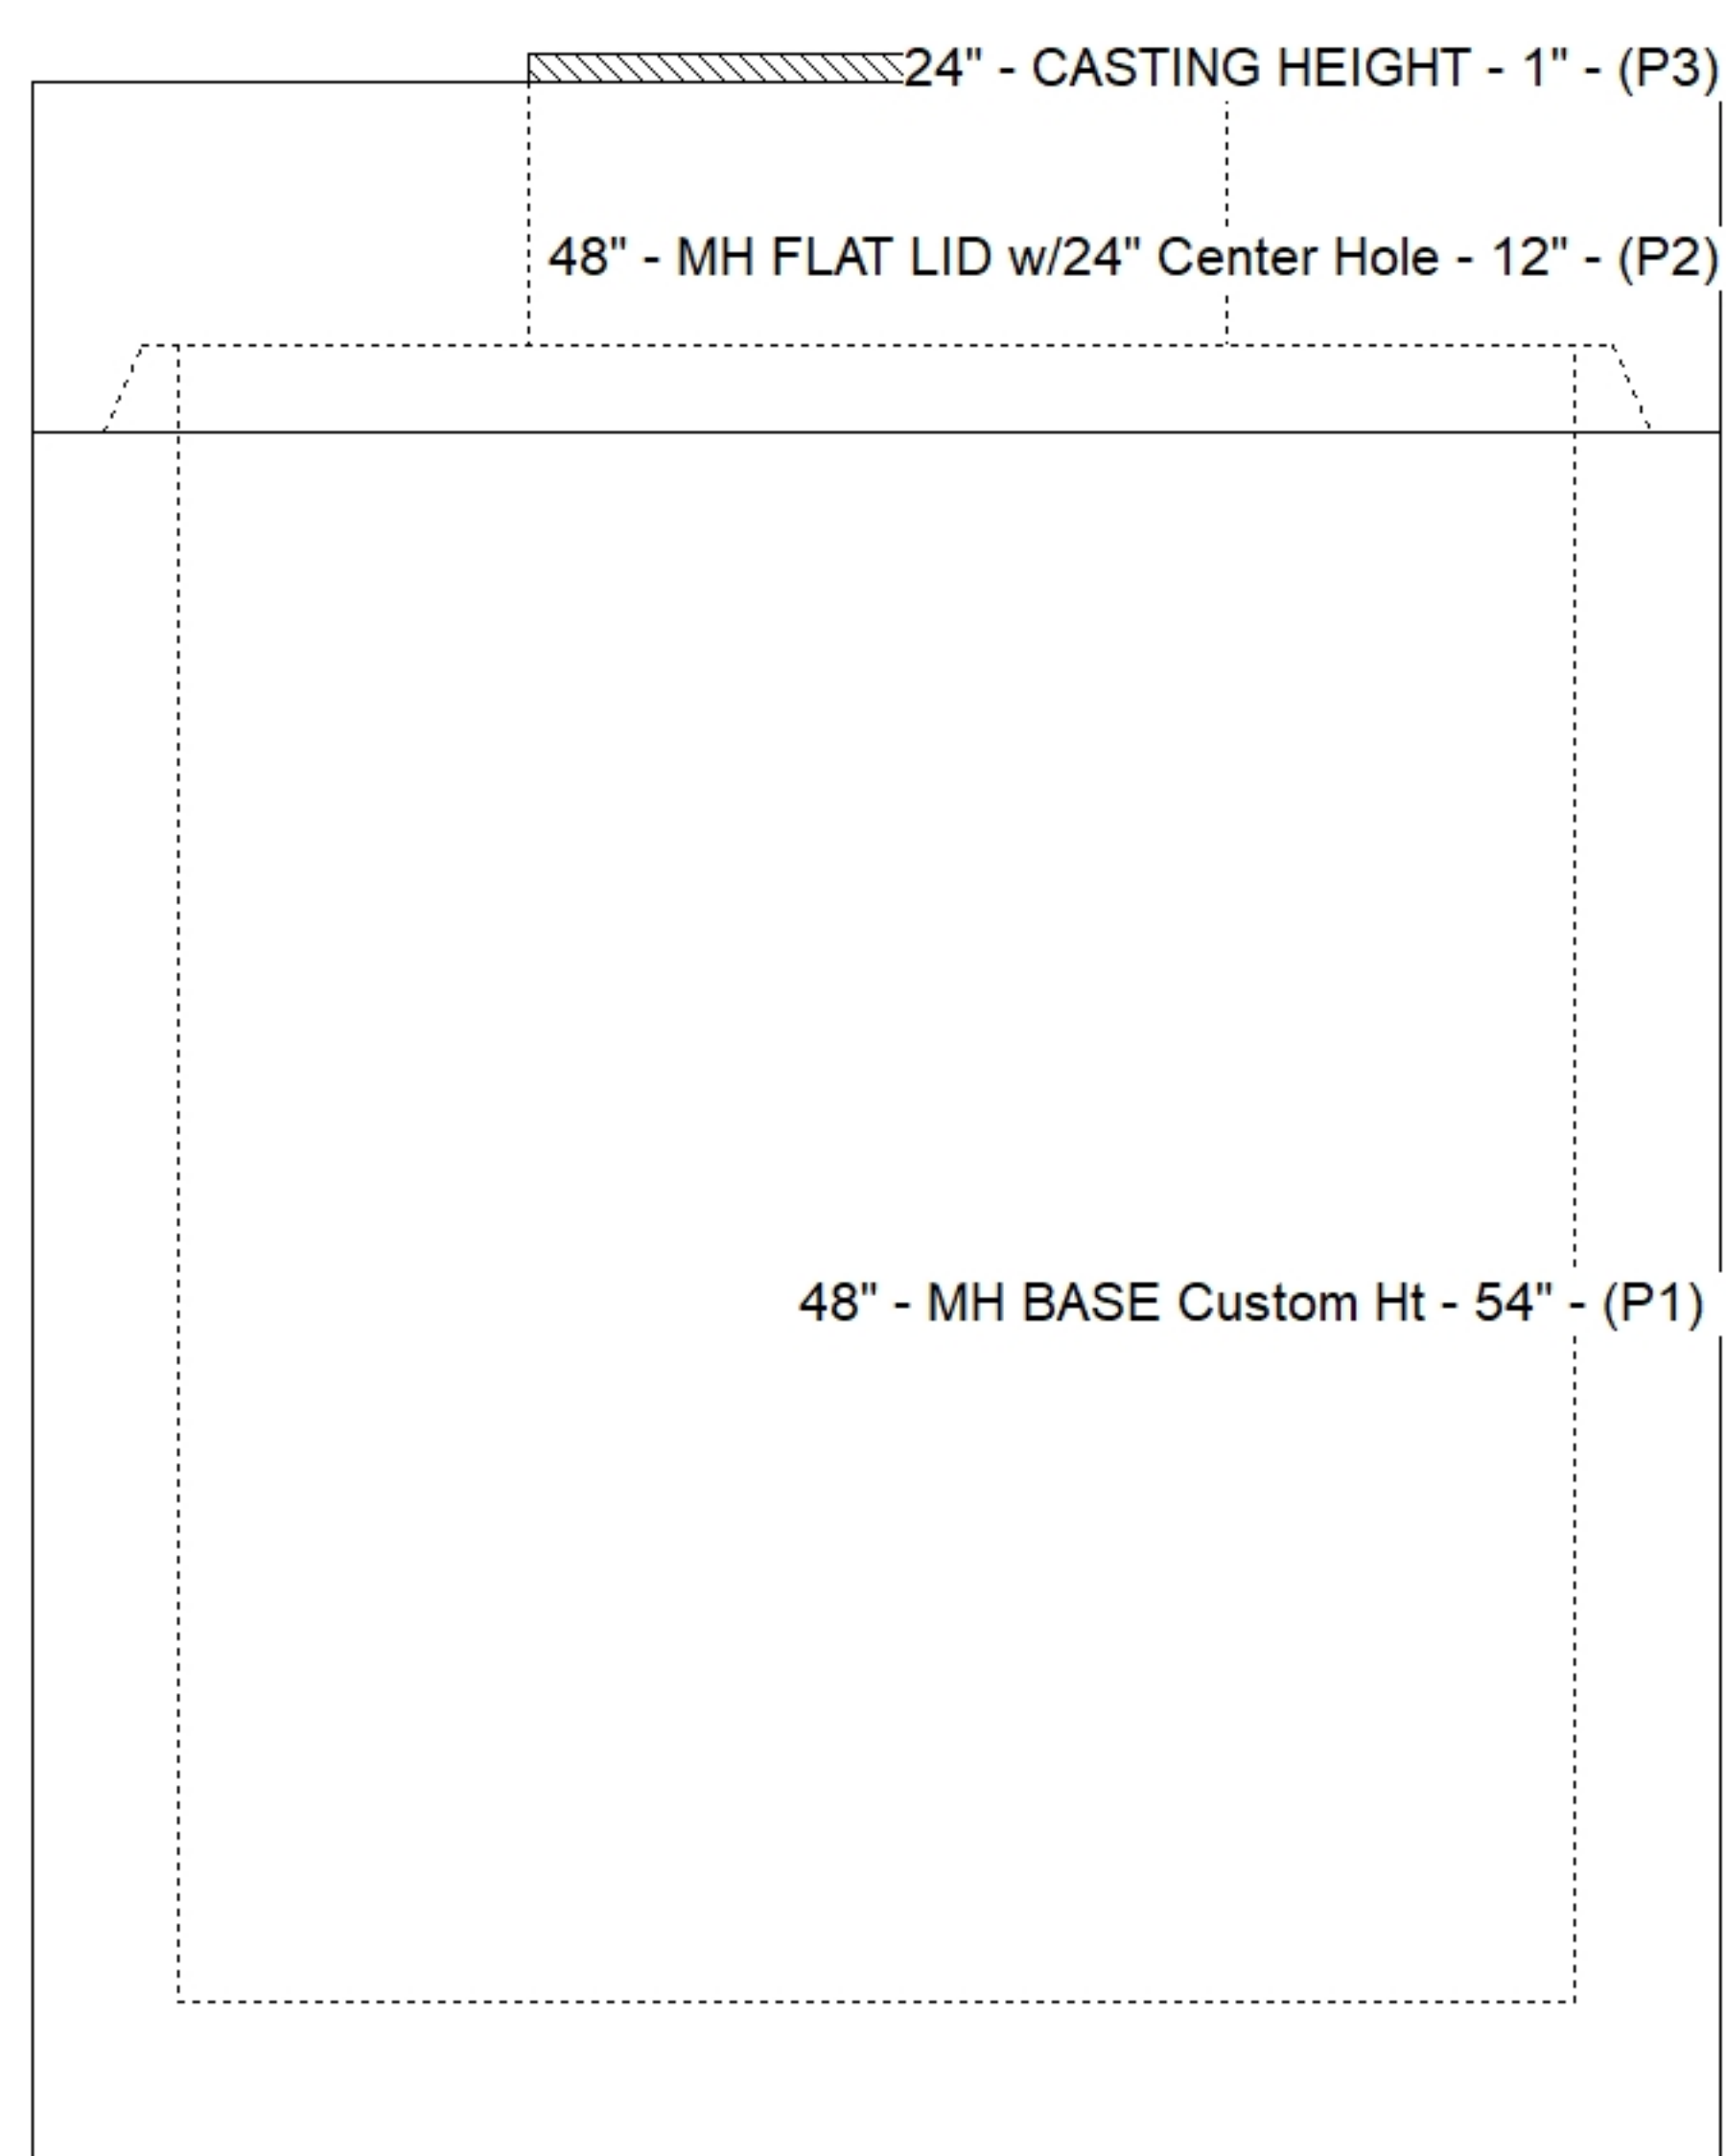

Default - Interior Dimensions

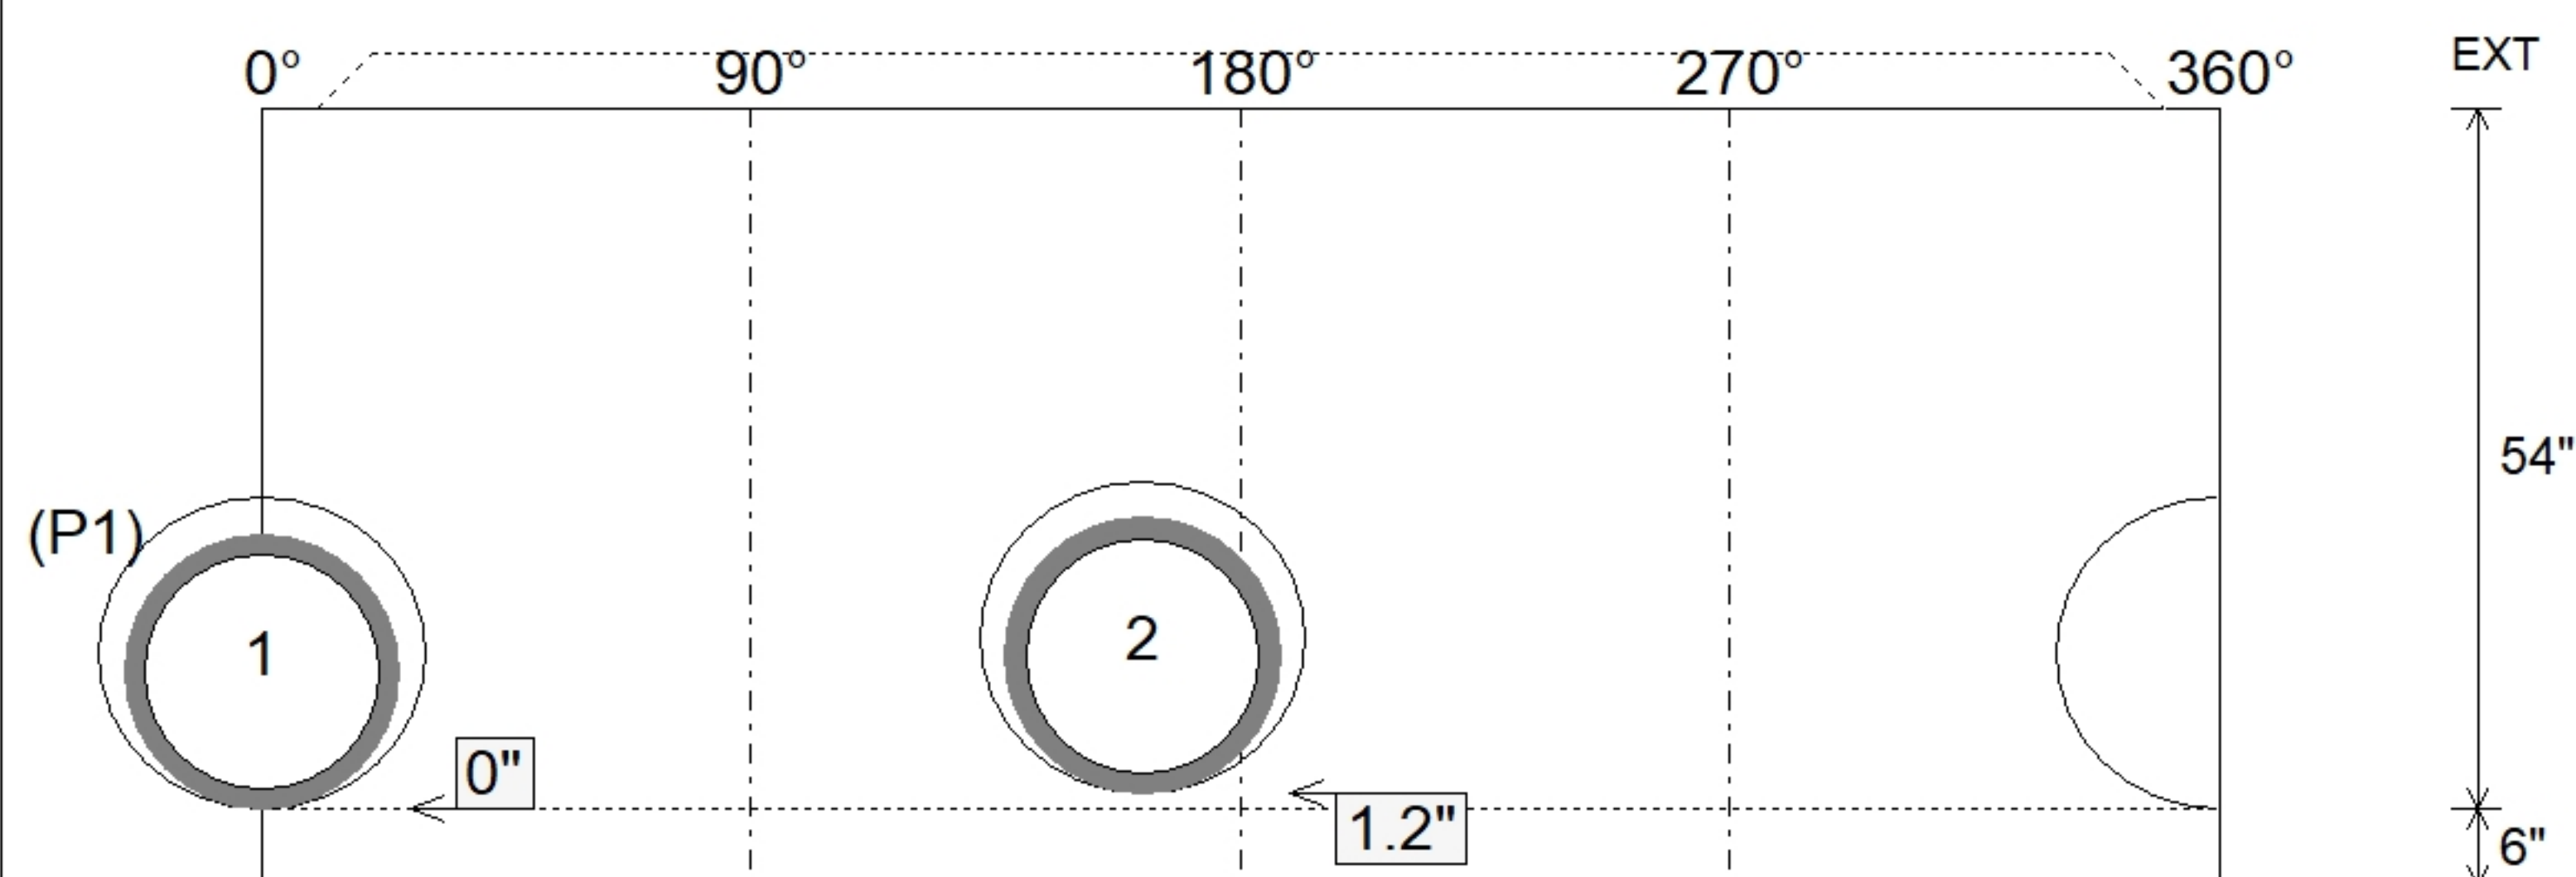

SUBMITTAL
APPROVED BY:
