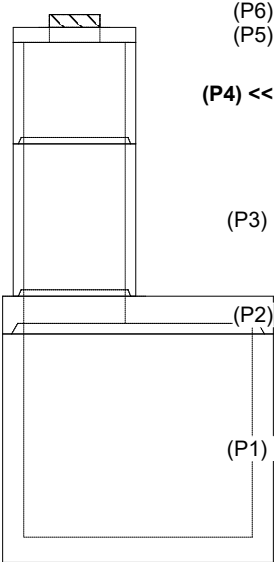

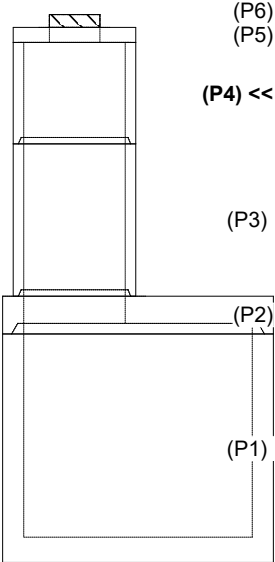



Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:43:08 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 217 ST-MH											
P4 MH048RSVF			MH RISER Custom Ht								
P6) 24" x 36" - CASTING HEIGHT - 6" P5) 48" - MH FLAT TOP w/24"x36" Hole - 7" P4) 48" - MH RISER Custom Ht - 48" P3) 48" - MH RISER Custom Ht - 72" P2) 108" - MH Transition Slab 48" Hole - 18" P1) 108" - MH BASE - 96" 1) 108" - Conseal CS-102 1.00" 3) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 70 1) Hole - 56 1) Hole - 24 18) MH Step ML-10-TDS-NCR - 10"					0 lb 1044 lb 3353 lb 4833 lb 12782 lb 37199 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT MH TYPE M / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. CASTING BY ICAST. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .30) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.				
Rim: 607.91' Rim to Invert: 20.55' Slack: 3" Sump: 3.4" Step Position: 83°					Structure Total: 59212 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd		
