

Job Name: 26-2217 Kroger COB
Job Location: Bowling Green, KY
Contractor: Stewart Richey

Plant: Beaver Dam

7/21/2026 8:12:41 AM

Tech: J. Coppage

PC: T. Lewis



Structure ID: QL4 VV

P1 BX090096-06W08F-BAVF

BOX BASE 6inW, 8inF, Variable Ht

- P3) 36" x 36" - HATCH (CAST FLUSH) - 0"
P2) 90" x 96" - BX FLAT LID 6"W w/36"x36" HATCH - 8"
P1) 90" x 96" - BOX BASE 6inW, 8inF, Variable Ht - 96"
1) HATCH (Alum.) - HALLIDAY H1W 36"x36"
1) This Structure Includes a Cast-in Item - 36" x 36" Hatch
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) SECONDARY POUR - WALLS
1) 90" x 96" - Conseal CS-102 1.00" (Double)
3) PSX - 12M NYLO
7) MH Step ML-10-TDS-NCR - 10"

FIRST POUR DRAWING

Structure Total: 33248 lb



Structure Notes:

1. HALLIDAY H1W 36" X 36" HATCH BY ICAST.
 2. HATCH TO BE CAST INTO THE TOP SLAB.
 3. PER ASTM C913 SPECIFICATIONS.
 4. CONCRETE = 4,000 PSI AT 28 DAYS.
 5. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 8" C.C.E.W.

Rim: 547.24' Rim to Invert: 7.24' Slack: 0.88" Sump: 18" Step Position: 180°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	540'	180°	51"	8" DI	9"	PSX 12M NYLO	12"	12"	16"	0"
Invert 2	540'	0°	33"	8" DI	9"	PSX 12M NYLO	12"	12"	16"	-18"
Invert 3	540'	0°	69"	8" DI	9"	PSX 12M NYLO	12"	12"	16"	18"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

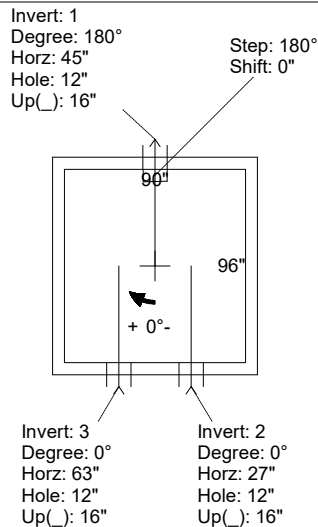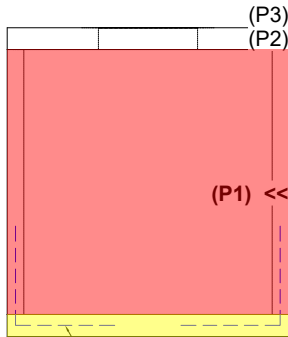


WEIGHTS:

FIRST POUR - 7,395 LBS.

SECOND POUR - 18,969 LBS.

TOTAL - 26,364 LBS.

INSIDE WALL DIMENSIONS

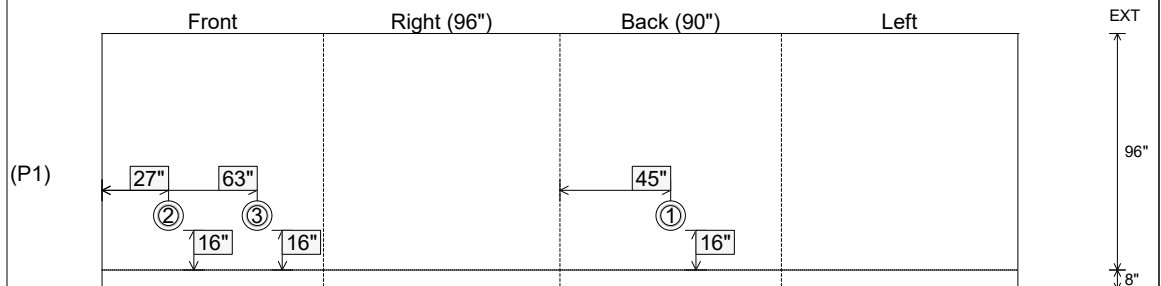

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 6"
Floor Height: 8"

Height (Int): 96"
Height (Ext): 104"

Weight (Net): 26364 lb
Volume (Net): 6.73cu.yd

Job Name: 26-2217 Kroger COB
Job Location: Bowling Green, KY
Contractor: Stewart Richey

Plant: Beaver Dam

7/21/2026 8:12:41 AM

Tech: J. Coppage

PC: T. Lewis



Structure ID: QL4 VV

P1 BX090096-06W08F-BAVF

BOX BASE 6inW, 8inF, Variable Ht

P3) 36" x 36" - HATCH (CAST FLUSH) - 0"
P2) 90" x 96" - BX FLAT LID 6"W w/36"x36" HATCH - 8"
P1) 90" x 96" - BOX BASE 6inW, 8inF, Variable Ht - 96"

- 1) HATCH (Alum.) - HALLIDAY H1W 36"x36"
1) This Structure Includes a Cast-in Item - 36" x 36" Hatch
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) SECONDARY POUR - WALLS
1) 90" x 96" - Conseal CS-102 1.00" (Double)
3) PSX - 12M NYLO
7) MH Step ML-10-TDS-NCR - 10"

SECOND POUR DRAWING

Structure Total: 33248 lb


Structure Notes:

1. HALLIDAY H1W 36" X 36" HATCH BY ICAST.
 2. HATCH TO BE CAST INTO THE TOP SLAB.
 3. PER ASTM C913 SPECIFICATIONS.
 4. CONCRETE = 4,000 PSI AT 28 DAYS.
 5. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 8" C.C.E.W.

Rim: 547.24' Rim to Invert: 7.24' Slack: 0.88" Sump: 18" Step Position: 180°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	540'	180°	51"	8" DI	9"	PSX 12M NYLO	12"	12"	16"	0"
Invert 2	540'	0°	33"	8" DI	9"	PSX 12M NYLO	12"	12"	16"	-18"
Invert 3	540'	0°	69"	8" DI	9"	PSX 12M NYLO	12"	12"	16"	18"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

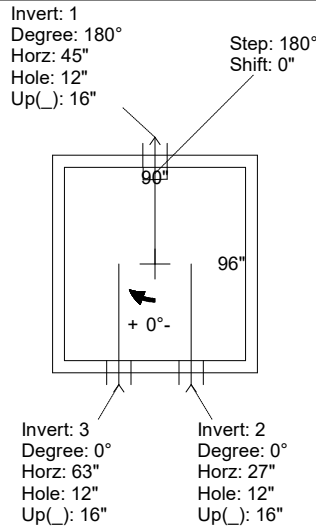


WEIGHTS:

FIRST POUR - 7,395 LBS.


SECOND POUR - 18,969 LBS.

TOTAL - 26,364 LBS.

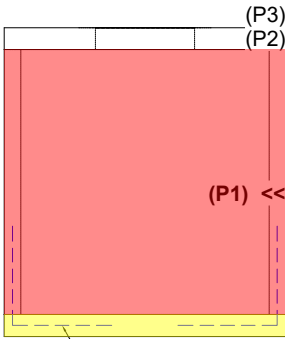

36" X 36" #5 BAR
@ 12" ON CENTER
TIED INTO THE MAT

INSIDE WALL DIMENSIONS

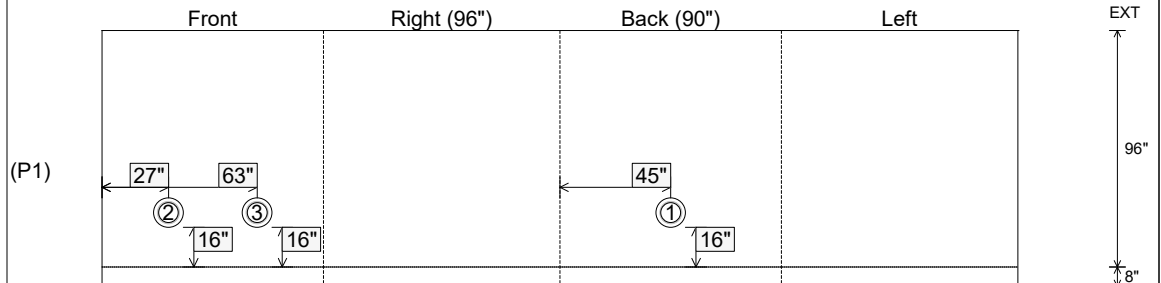

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 6"
Floor Height: 8"

Height (Int): 96"
Height (Ext): 104"

Weight (Net): 26364 lb
Volume (Net): 6.73cu.yd
