

Contractor: Scott & Ritter, Inc.


TECH: J. Horsley

Plant: 100




Slack: 2.48"

Structure Total: 6690 lb

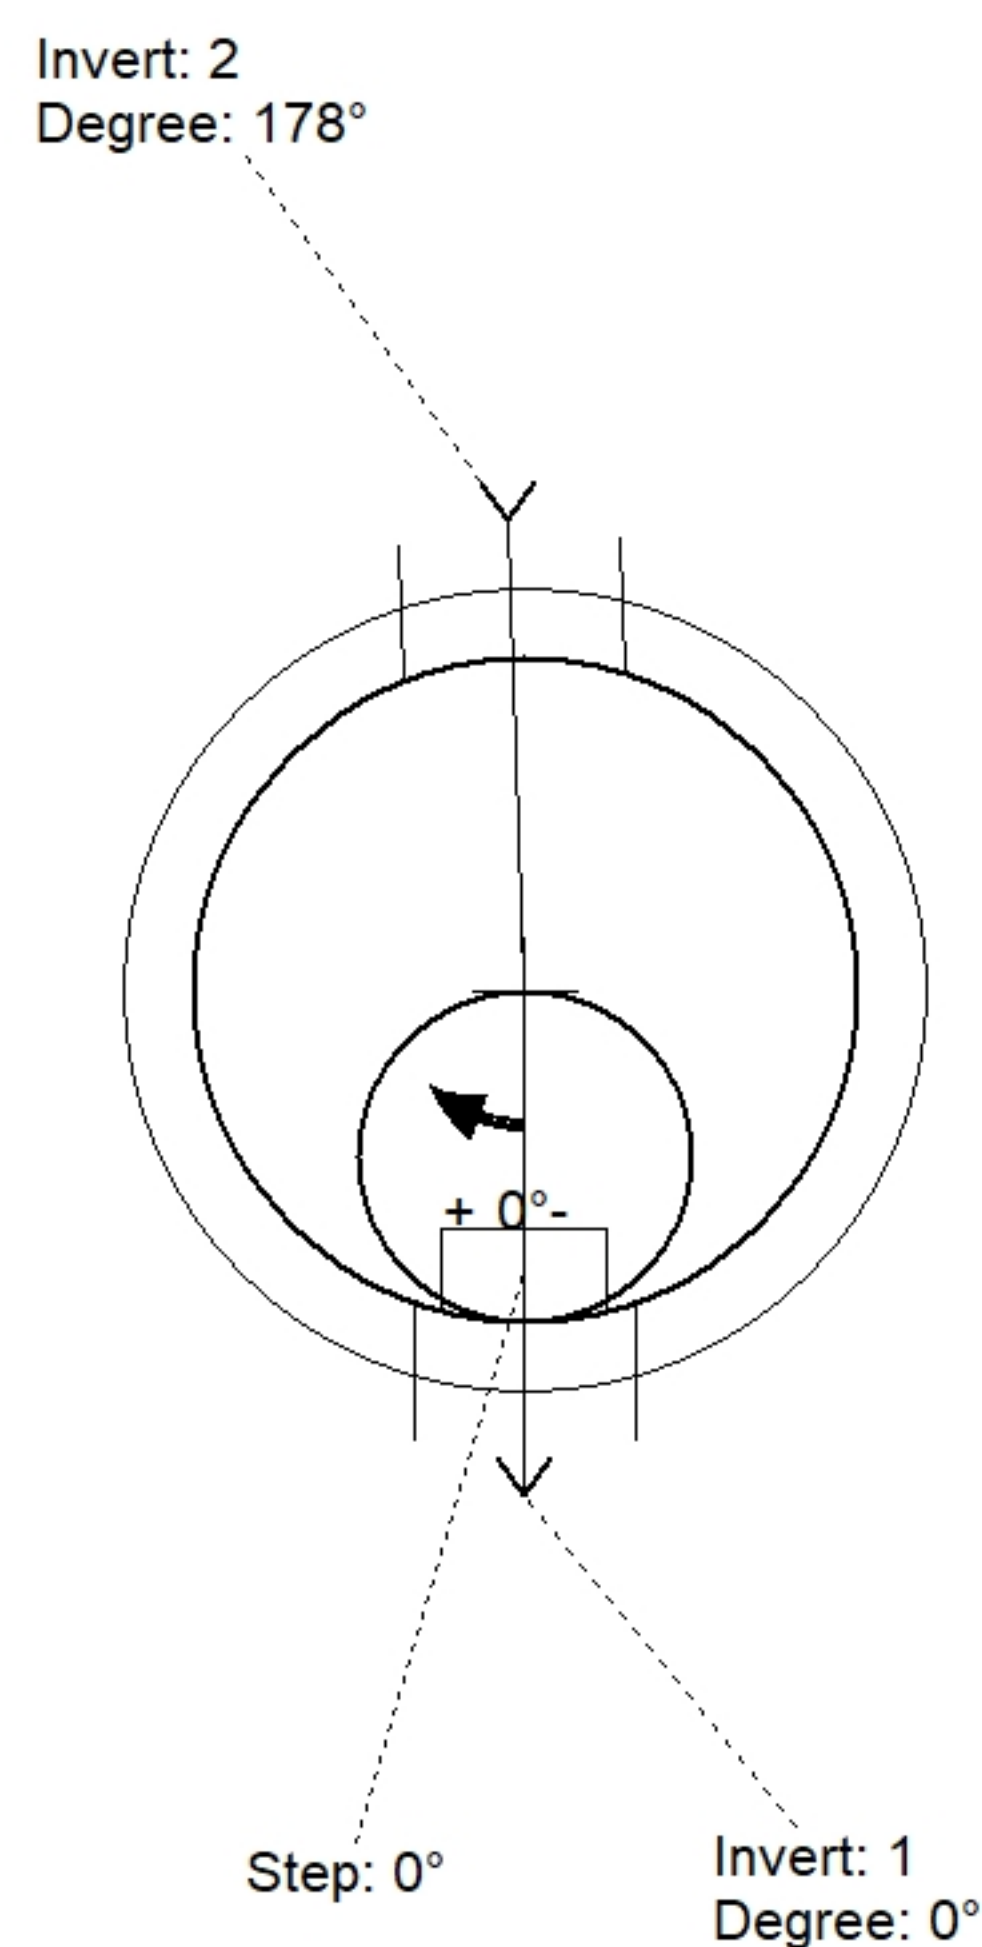

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	519'							
Reducer								
Invert 1	514.46'	0°	10" PVC SDR35	10.5"	16"	PSX 16Y DD (DBL Bands)	0"	P1
Invert 2	514.56'	178°	10" PVC SDR35	10.5"	16"	PSX 16Y DD (DBL Bands)	1.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

48" - MH BASE T/n - 36" - (P1)

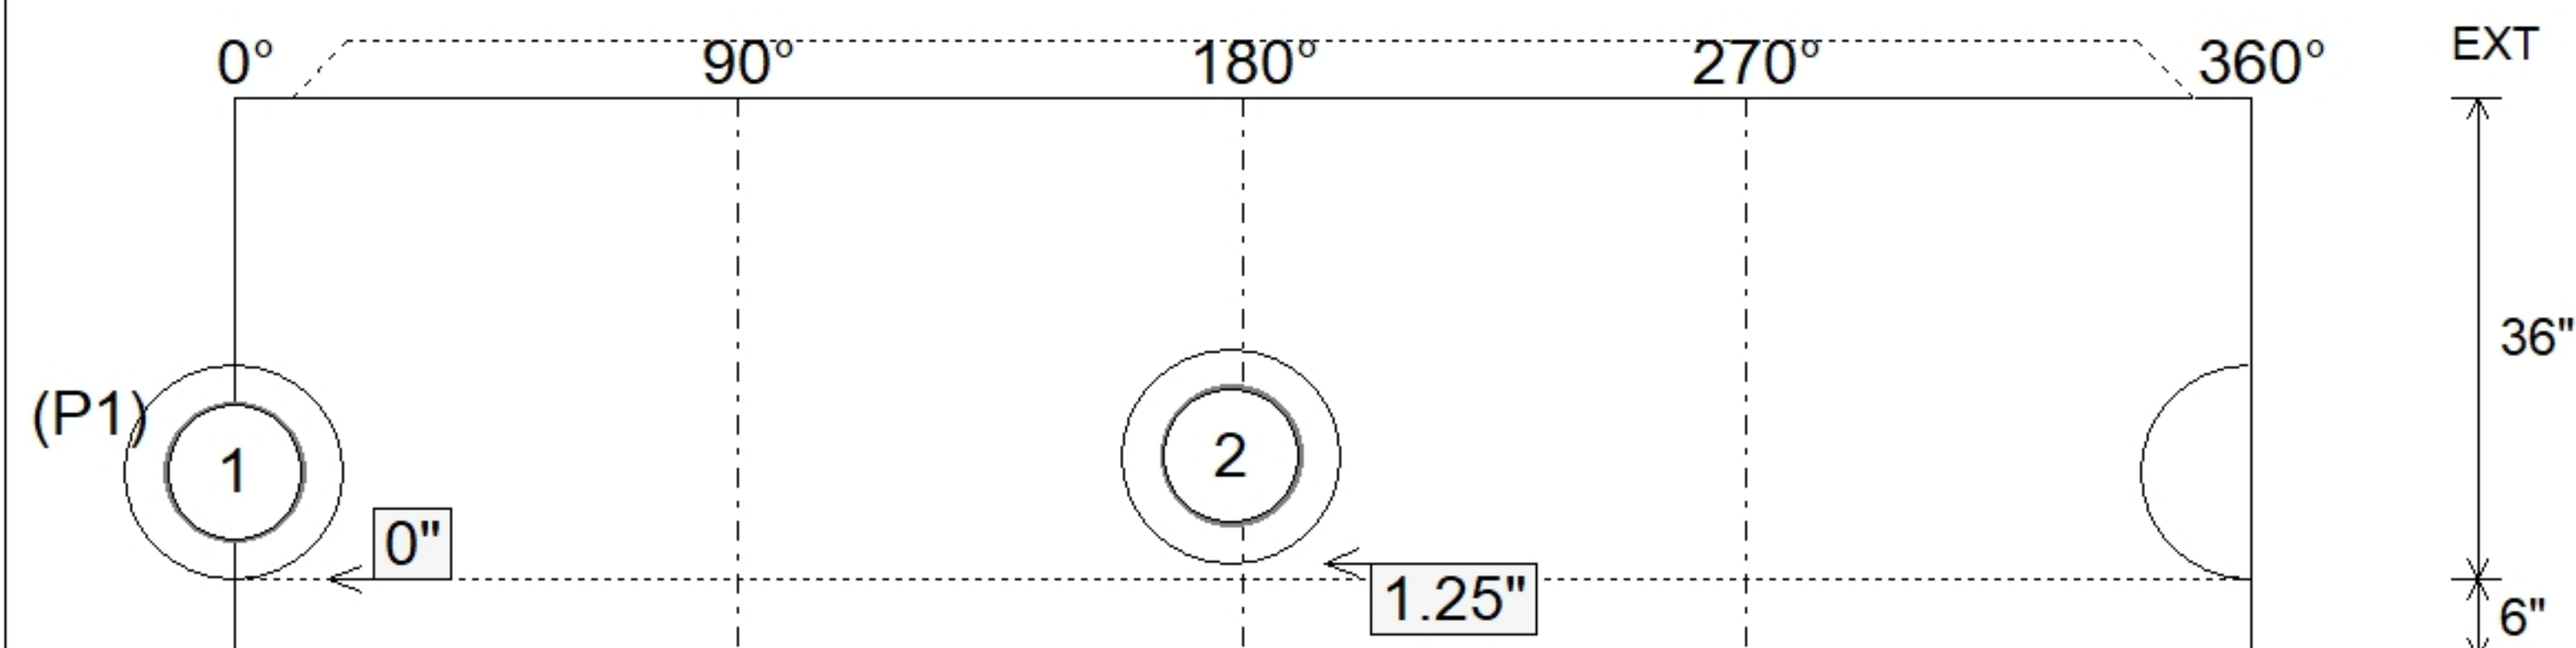

SUBMITTAL
APPROVED BY:
