

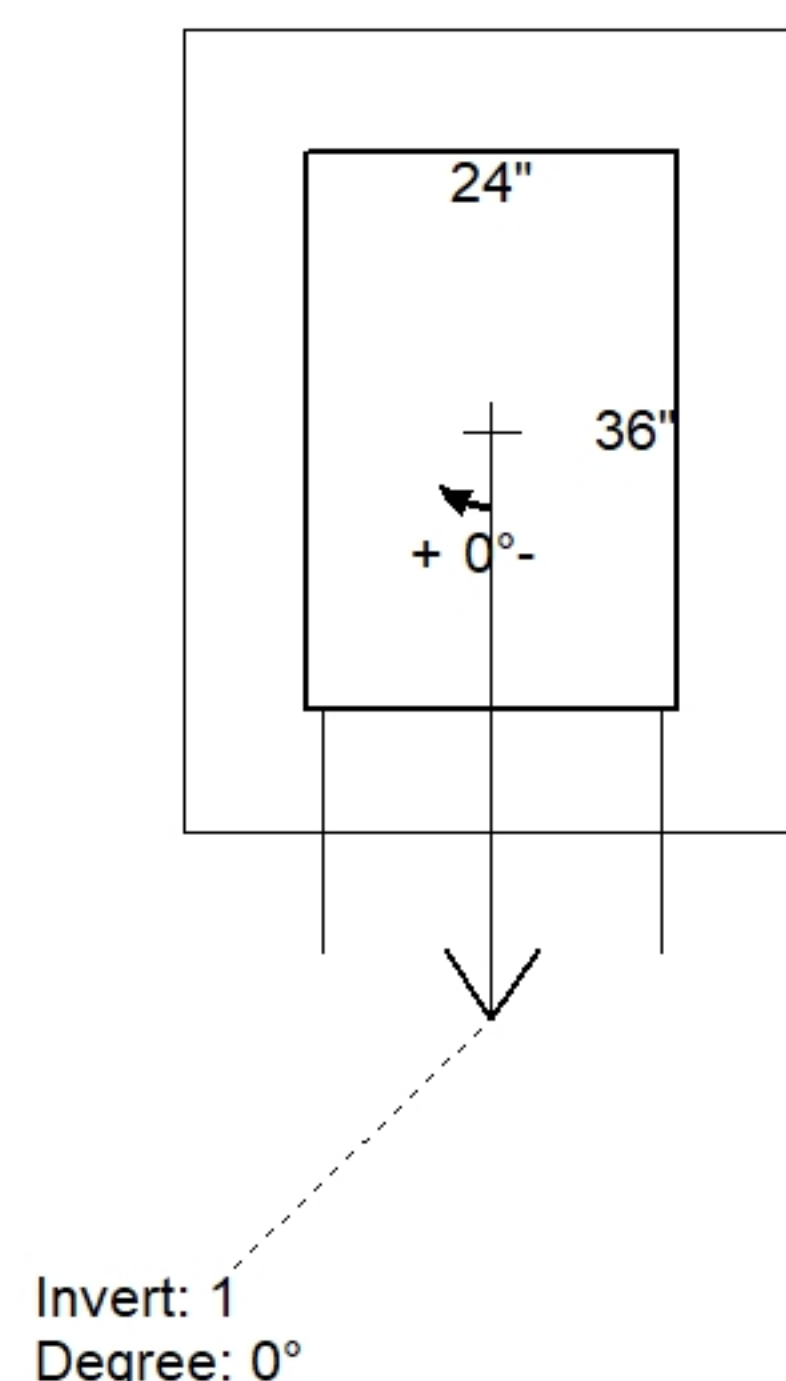


Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (JBS 3080 SET (F/G/H)). . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.	STRUCTURE SUMMARY: P2) 24" x 36" - CASTING HEIGHT - 6.5" 0 lb P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26" 3794 lb 1) CASTING - JBS 3080 SET (F/G/H) 500 lb 1) 24" x 36" - SGL 1"x14.5' Butyl 0 lb 1) Hole - 22 0 lb ----- Structure Total: 4294 lb
--	--

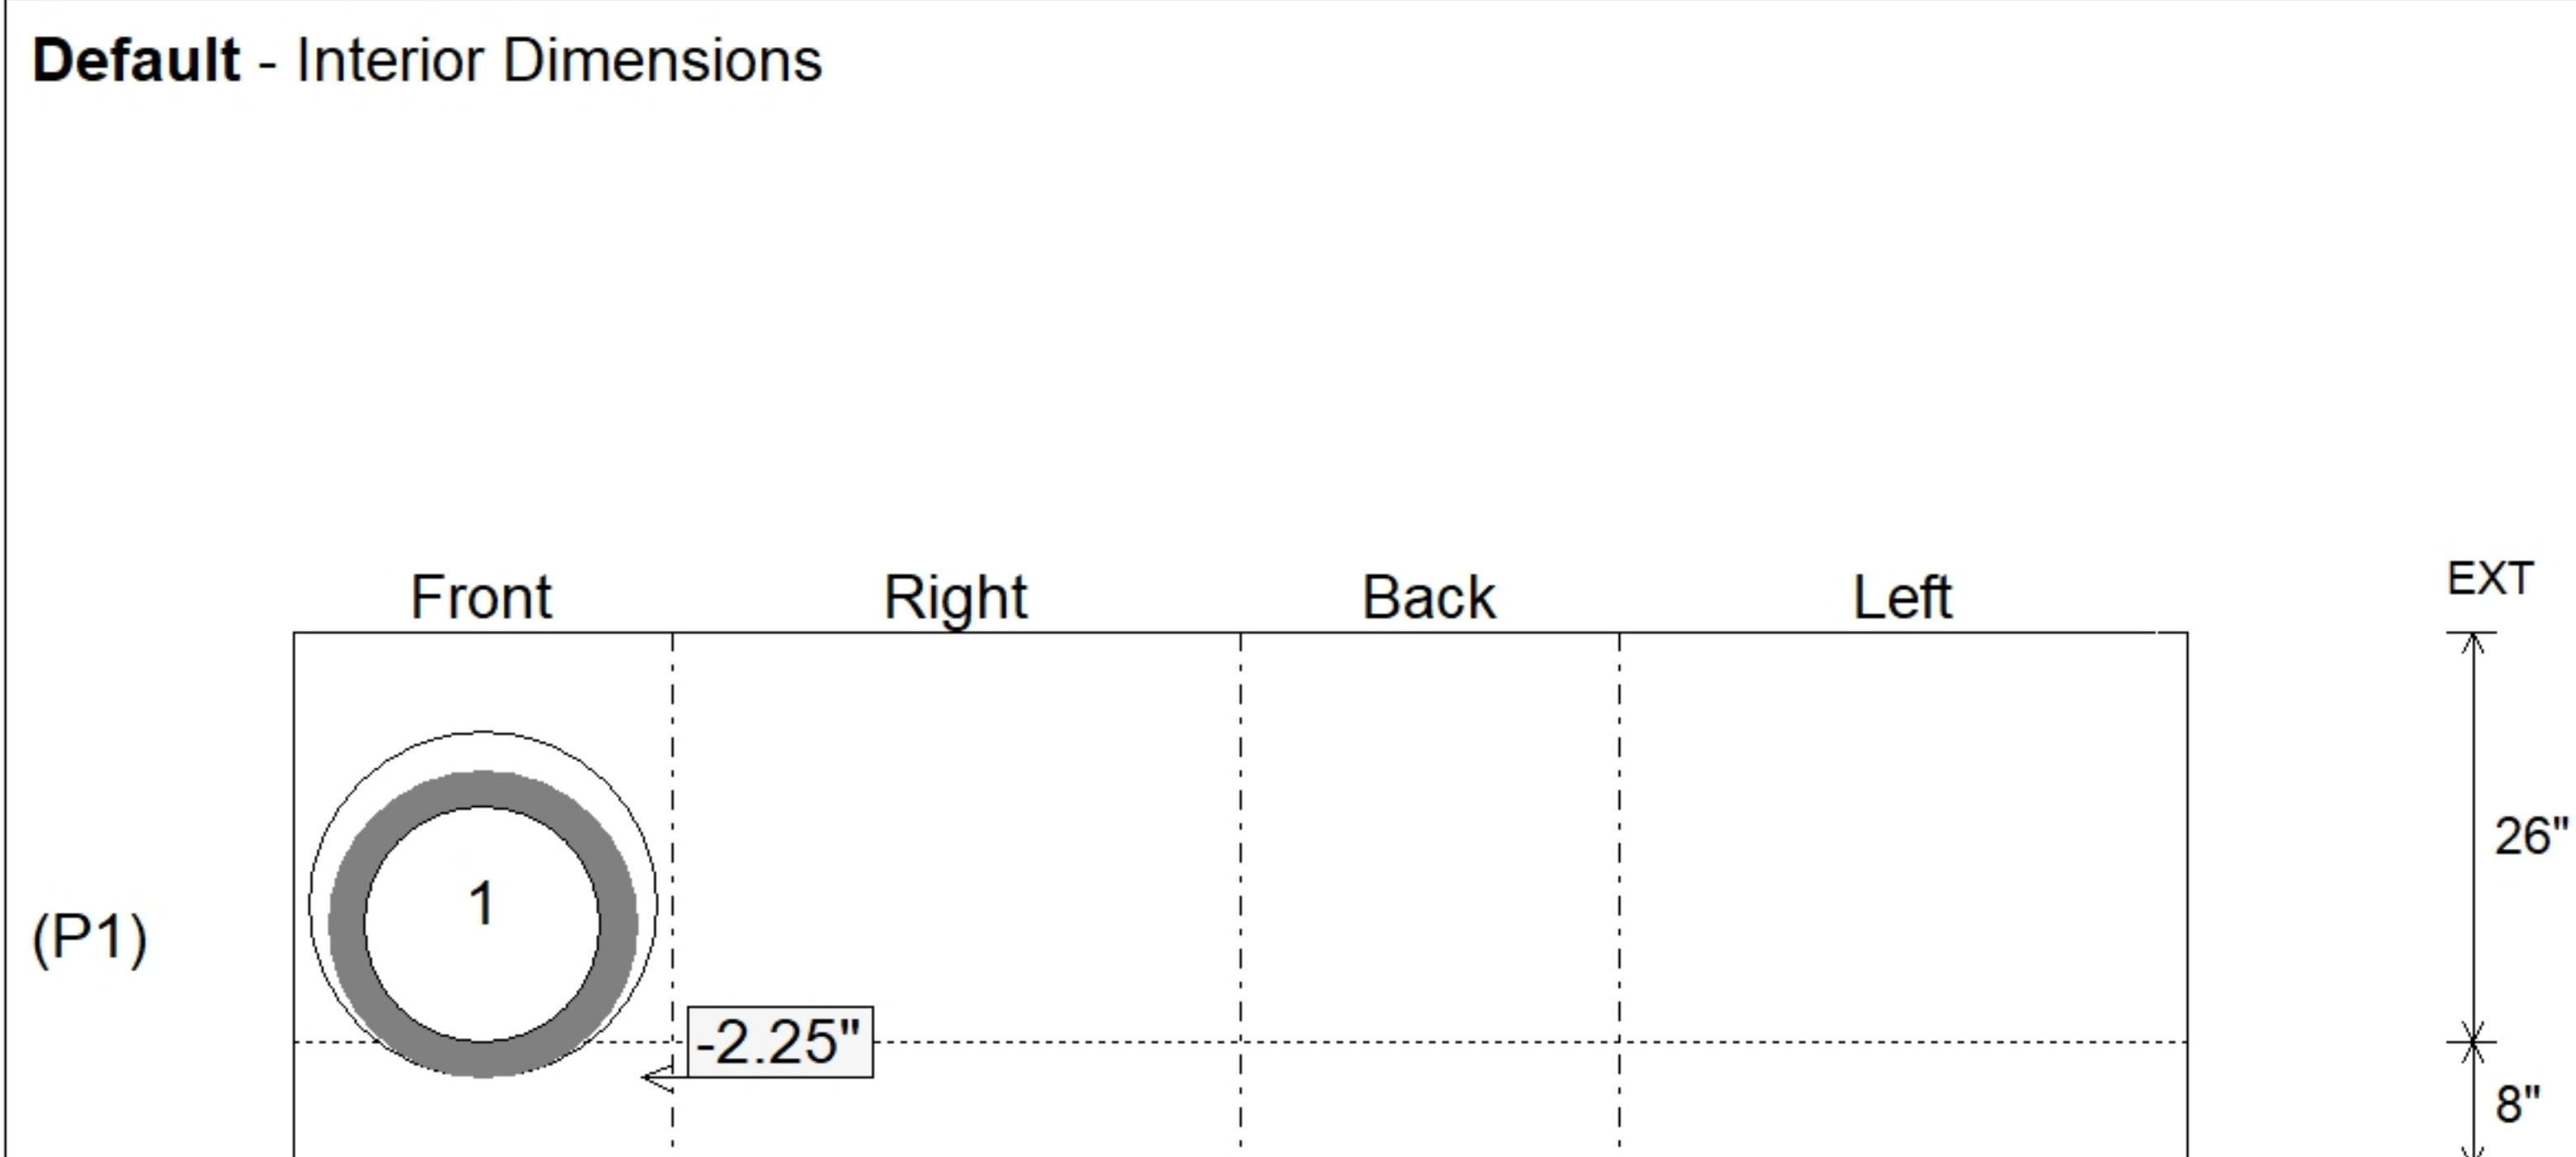

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	546.01'							
Reducer								
Invert 1	543.23'	0°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

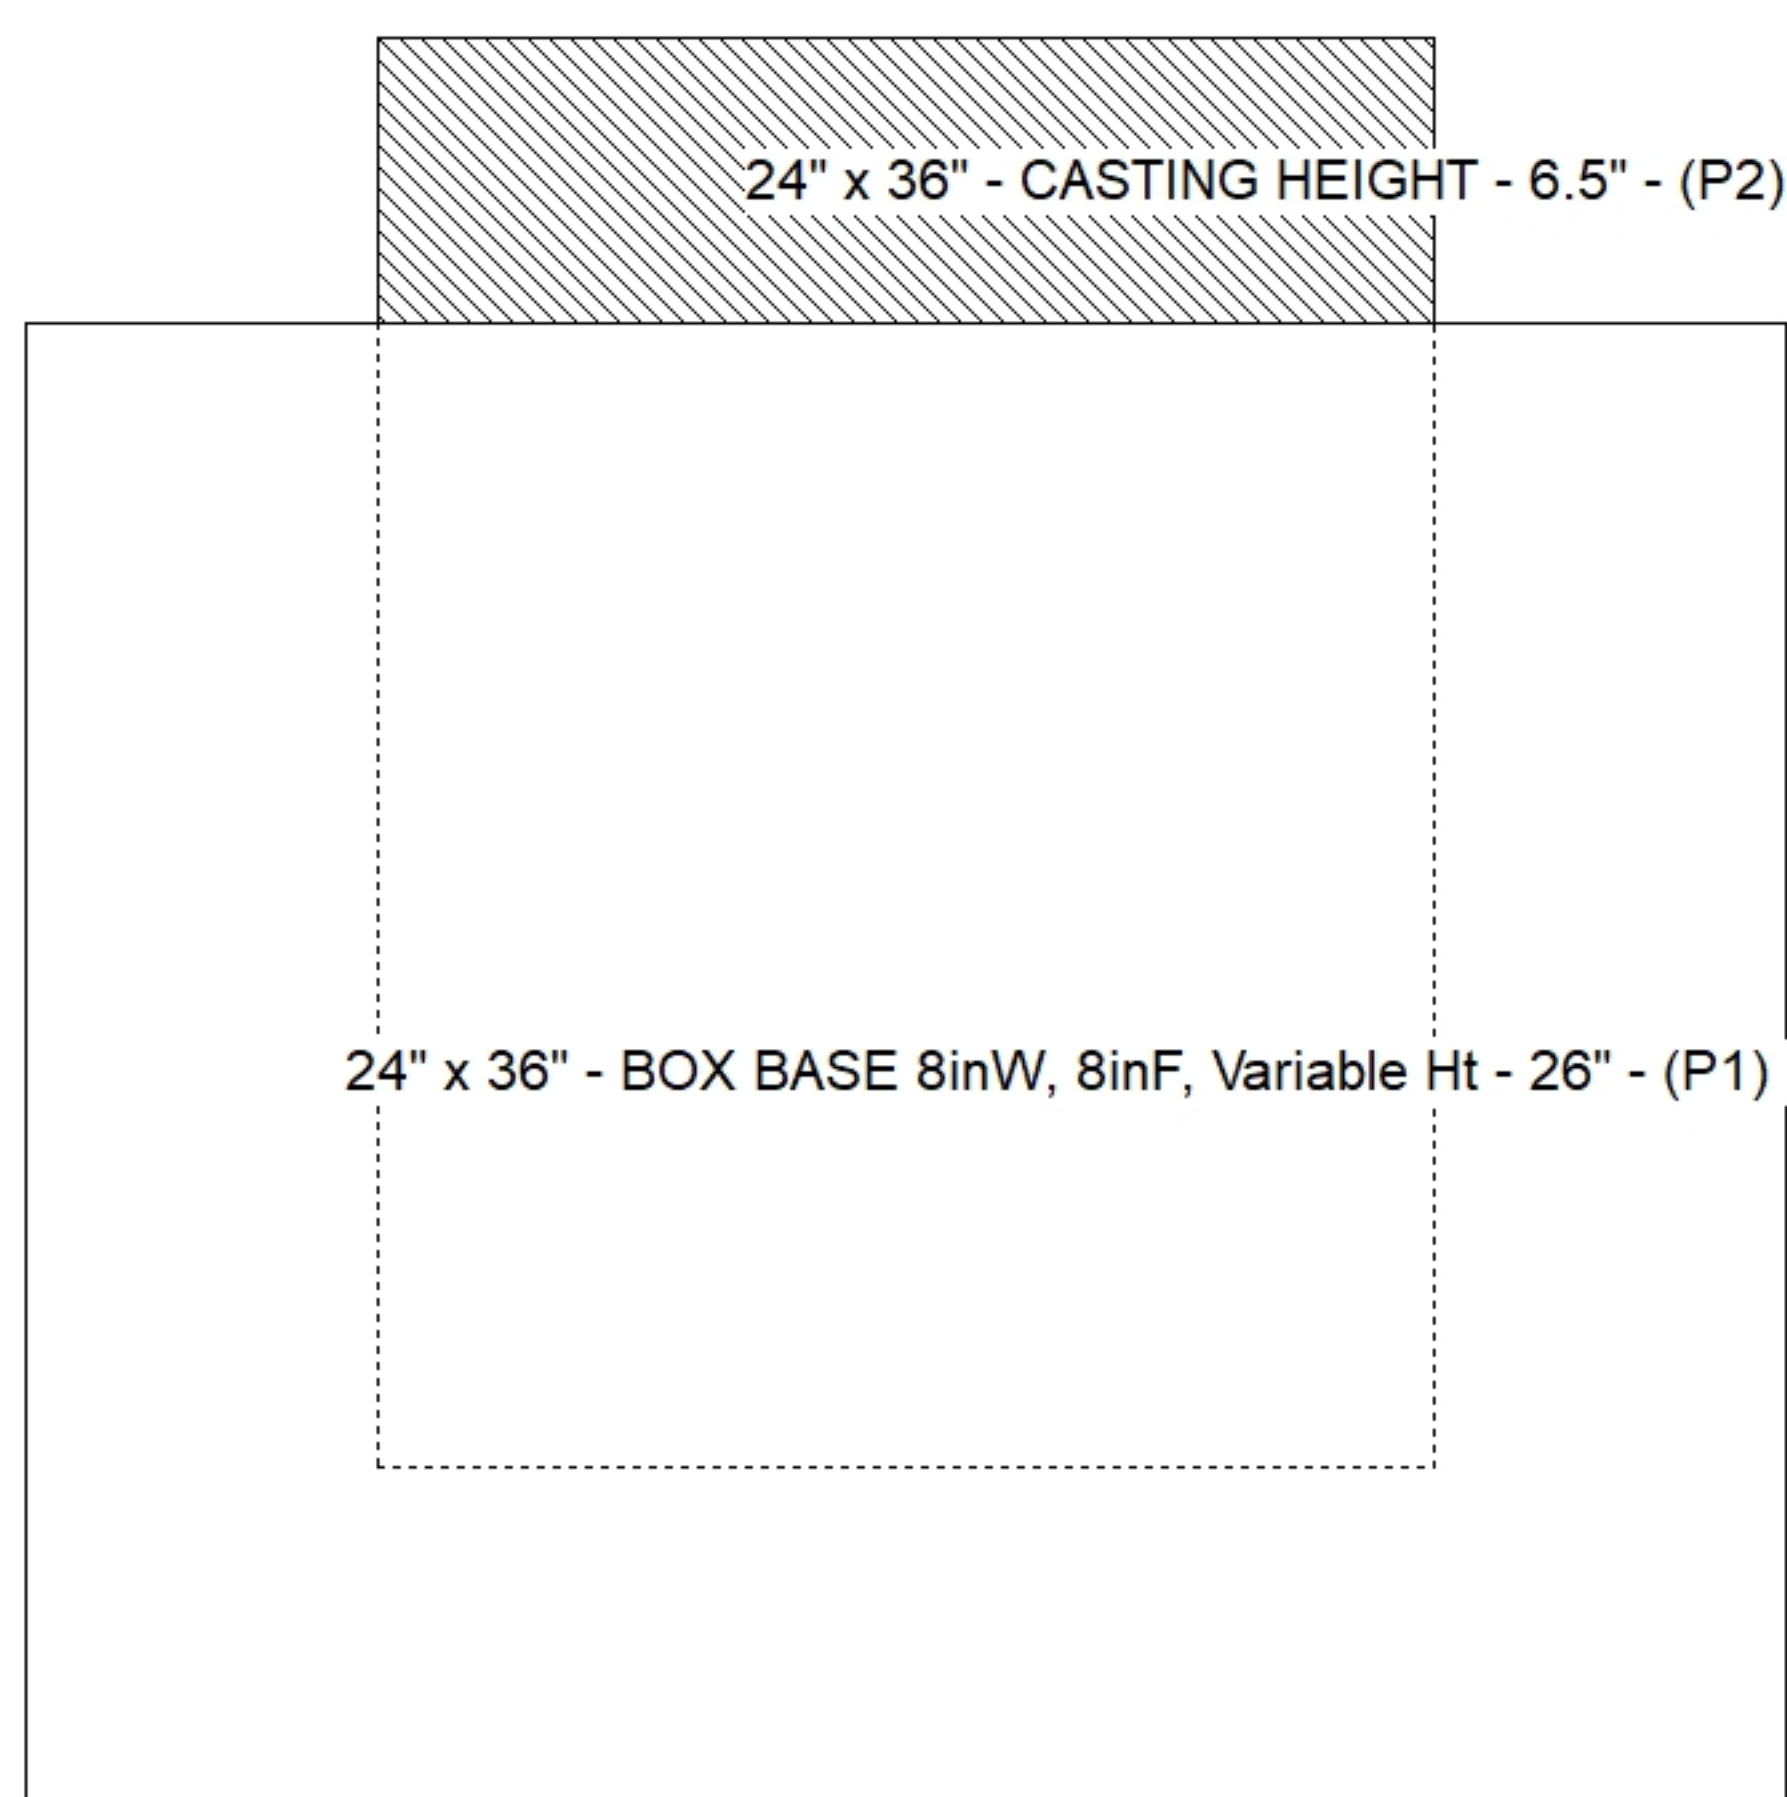

SUBMITTAL
APPROVED BY:
