



Job Name: 26-2270 - Walmart #299 Fuel Station Job Location: Bowling Green, KY Contractor: Stewart Richey					Plant: 100 8/10/2026 2:19:09 PM		Tech: Jared - F PC: T. Lewis			
Structure ID: OCS ST-OCS										
P1 BX4848-08W12F-BAVF			BOX BASE 8inW, 12inF, Variable Ht T/n							
P3) 48" x 48" - CASTING HEIGHT - 0" P2) 48" x 48" - BOX RISER 8inW, Variable Ht F/G - 45" P1) 48" x 48" - BOX BASE 8inW, 12inF, Variable Ht T/n - 40" 1) CASTING - TRASHRACKS LFS-4848-P SQ. Flush Mount Grate 2) 48" x 48" - Conseal CS-102 1.00" 1) Hole - 40 1) Hole - 8 1) Weir n/n - 6"x36" 7) MH Step ML-10-TDS-NCR - 10"					0 lb 6622 lb 9262 lb 289 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 16173 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,500 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (TRASHRACKS LFS-48 SQ. FLUSH MOUNT TRASH RACK). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 540' Rim to Invert: 7.1' Slack: 0.2" Sump: 0" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	532.9'	0°	32"	30" RCP B WALL	37"	Hole 40	40"	40"	-3.5"	0"
Invert 2	532.9'	180°	32"	6" PVC PERF	6.28"	Hole 8	8"	8"	-0.125"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

FIRST POUR DRAWING

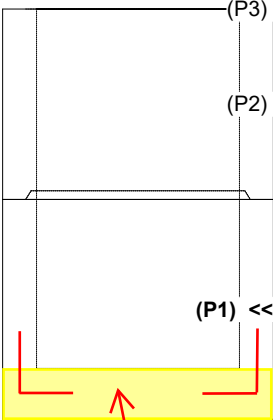

1ST POUR (FLOOR)
 STUB #5 L BARS OUT
 TOP FLOOR, SPA AT
 12" C/C FOR
 CONNECTING WALLS


RIGHT-SIDE UP VIEW (int. dimensions)

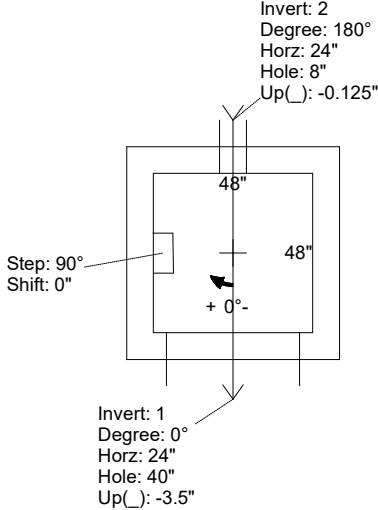

UPSIDE-DOWN VIEW (int. dimensions)

1ST POUR (FLOOR) = 4,124 LBS
 2ND POUR (WALLS) = 5,138 LBS
 TOTAL = 9,262 LBS


INSIDE WALL DIMENSIONS




Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 12"	Height (Int): 40" Height (Ext): 52"	Weight (Net): 9262 lb Volume (Net): 2.37cu.yd
----------------------------------	---------------------------------	---	--	--

Job Name: 26-2270 - Walmart #299 Fuel Station Job Location: Bowling Green, KY Contractor: Stewart Richey				Plant: 100 8/10/2026 2:19:09 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: OCS ST-OCS										
P1 BX4848-08W12F-BAVF				BOX BASE 8inW, 12inF, Variable Ht T/n						
P3) 48" x 48" - CASTING HEIGHT - 0" P2) 48" x 48" - BOX RISER 8inW, Variable Ht F/G - 45" P1) 48" x 48" - BOX BASE 8inW, 12inF, Variable Ht T/n - 40" 1) CASTING - TRASHRACKS LFS-4848-P SQ. Flush Mount Grate 2) 48" x 48" - Conseal CS-102 1.00" 1) Hole - 40 1) Hole - 8 1) Weir n/n - 6"x36" 7) MH Step ML-10-TDS-NCR - 10"				0 lb 6622 lb 9262 lb 289 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,500 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (TRASHRACKS LFS-48 SQ. FLUSH MOUNT TRASH RACK). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Structure Total: 16173 lb										
Rim: 540' Rim to Invert: 7.1' Slack: 0.2" Sump: 0" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	532.9'	0°	32"	30" RCP B WALL	37"	Hole 40	40"	40"	-3.5"	0"
Invert 2	532.9'	180°	32"	6" PVC PERF	6.28"	Hole 8	8"	8"	-0.125"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

SECOND POUR DRAWING

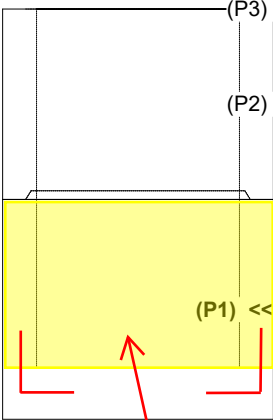


RIGHT-SIDE UP VIEW (int. dimensions)

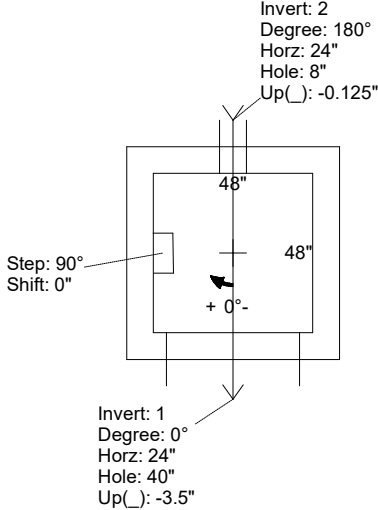


UPSIDE-DOWN VIEW (int. dimensions)

1ST POUR (FLOOR) = 4,124 LBS
2ND POUR (WALLS) = 5,138 LBS
TOTAL = 9,262 LBS



INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 12"	Height (Int): 40" Height (Ext): 52"	Weight (Net): 9262 lb Volume (Net): 2.37cu.yd
----------------------------------	---------------------------------	---	--	--
