



Job Name: 26-2310 - 3rd & Madison Townhomes - Ph. 1 Job Location: Nashville, TN 37208 Contractor: Hayes Pipe Supply				Plant: 100 6/15/2026 10:58:54 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: A3 ST-DCI										
P1 BX28640606-VH		BOX BASE 6inW, 6inF, Variable Ht F/n								
P2) 28" x 64" - CASTING HEIGHT - 7.50" P1) 28" x 64" - BOX BASE 6inW, 6inF, Variable Ht F/n - 43" 1) 28" x 64" - Conseal CS-102 1.00" 2) Hole - 40 x 28 2) LINTEL BAR SLOT n/n - 7"x1"						0 lb 5044 lb 0 lb 0 lb 0 lb ----- 0 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING SUPPLIED BY OTHERS (JBS 3300-V F/G/H - DOUBLE CURB INLET). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Structure Total: 5044 lb										
Rim: 422.35' Rim to Invert: 3.97' Slack: 0.765' Sump: 3.625' Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	418.38'	70°	36"	30" x 19" ELL RCP	37.25" x 26.25"	Hole 40 x 28	40" x 28"	42.567"	0"	5"
Invert 2	418.38'	300°	41.5"	30" x 19" ELL RCP	37.25" x 26.25"	Hole 40 x 28	40" x 28"	46.188"	0"	-7"
Invert 3	421.58'	90°	38"	7" x 1" LINTEL BAR SLOT	7" x 1"	LINTEL BAR SLOT 7"x1"	7" x 1"	7"	42"	0"
Invert 4	421.58'	270°	38"	7" x 1" LINTEL BAR SLOT	7" x 1"	LINTEL BAR SLOT 7"x1"	7" x 1"	7"	42"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

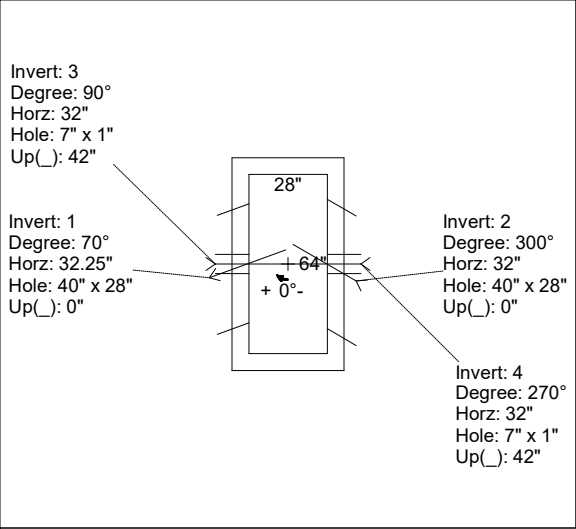

UPSIDE-DOWN VIEW (int. dimensions)

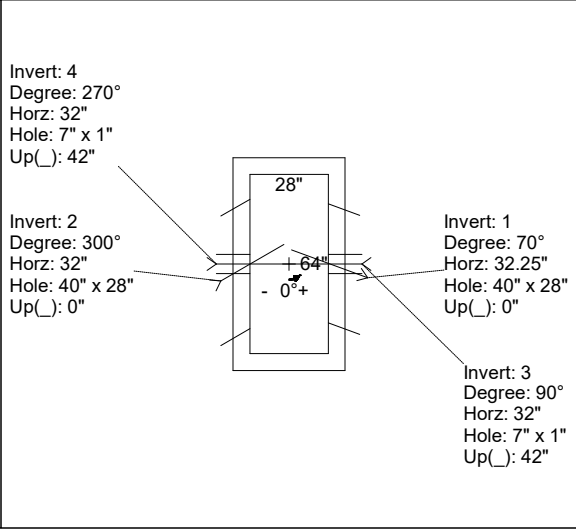

INSIDE WALL DIMENSIONS

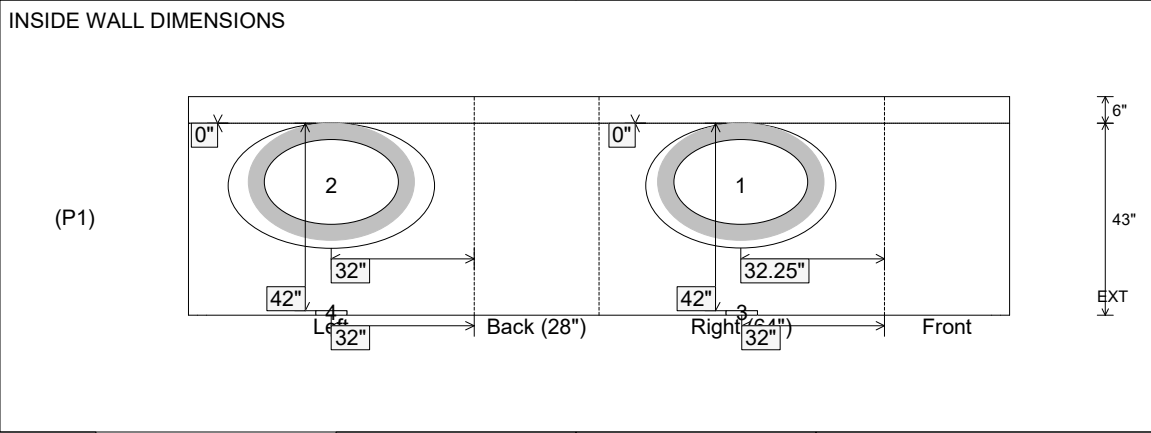

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 6"	Height (Int): 43" Height (Ext): 49"	Weight (Net): 5044 lb Volume (Net): 1.29cu.yd
----------------------------------	-------------------------------	--	--	--
