

Contractor: Hayes Pipe Supply

Plant: 100



Size: 28" x 64"

Rim to Invert: 3.97'

Floor Height: 6"


Slack: 0.765"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 28" x 64" - CASTING HEIGHT - 7.50"
P1) 28" x 64" - BOX BASE 6inW, 6inF, Variable Ht - 43"
1) 28" x 64" - Conseal CS-102 1.00"
2) Hole - 40 x 28
2) LINTEL BAR SLOT - 7"x1"


0 lb
5044 lb
0 lb
0 lb
0 lb

Structure Total: 5044 lb

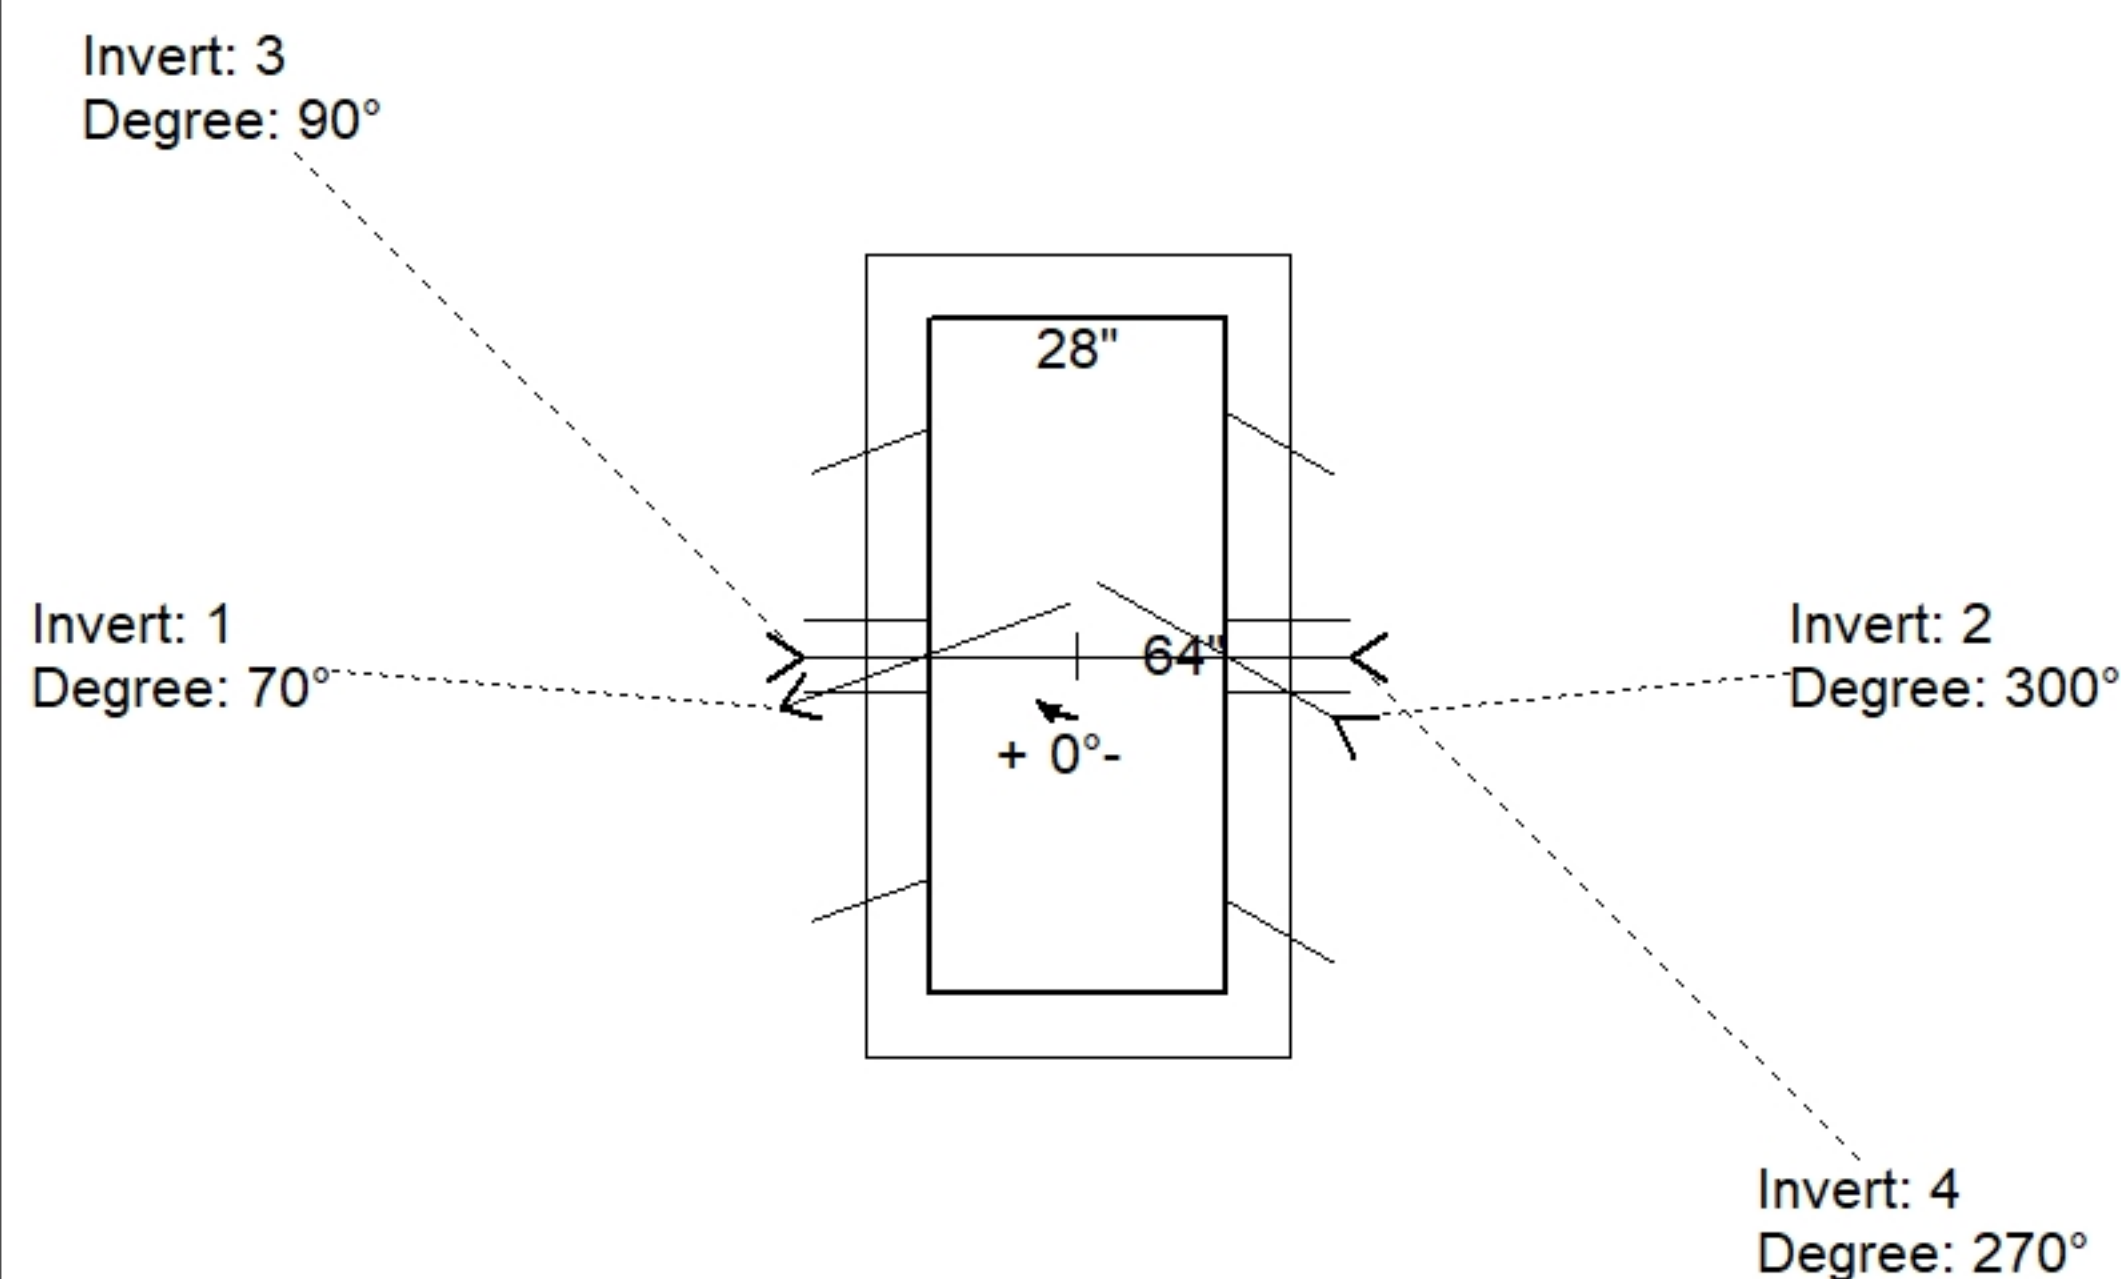

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌋)	Ref
Rim	422.35'							
Reducer								
Invert 1	418.38'	70°	30" x 19" ELL RCP	37.25" x 26.25"	40" x 28"	Hole 40 x 28	0"	P1
Invert 2	418.38'	300°	30" x 19" ELL RCP	37.25" x 26.25"	40" x 28"	Hole 40 x 28	0"	P1
Invert 3	421.58'	90°	7" x 1" LINTEL BAR SLOT	7" x 1"	7" x 1"	LINTEL BAR SLOT 7"x1"	42.025"	P1
Invert 4	421.58'	270°	7" x 1" LINTEL BAR SLOT	7" x 1"	7" x 1"	LINTEL BAR SLOT 7"x1"	42.025"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

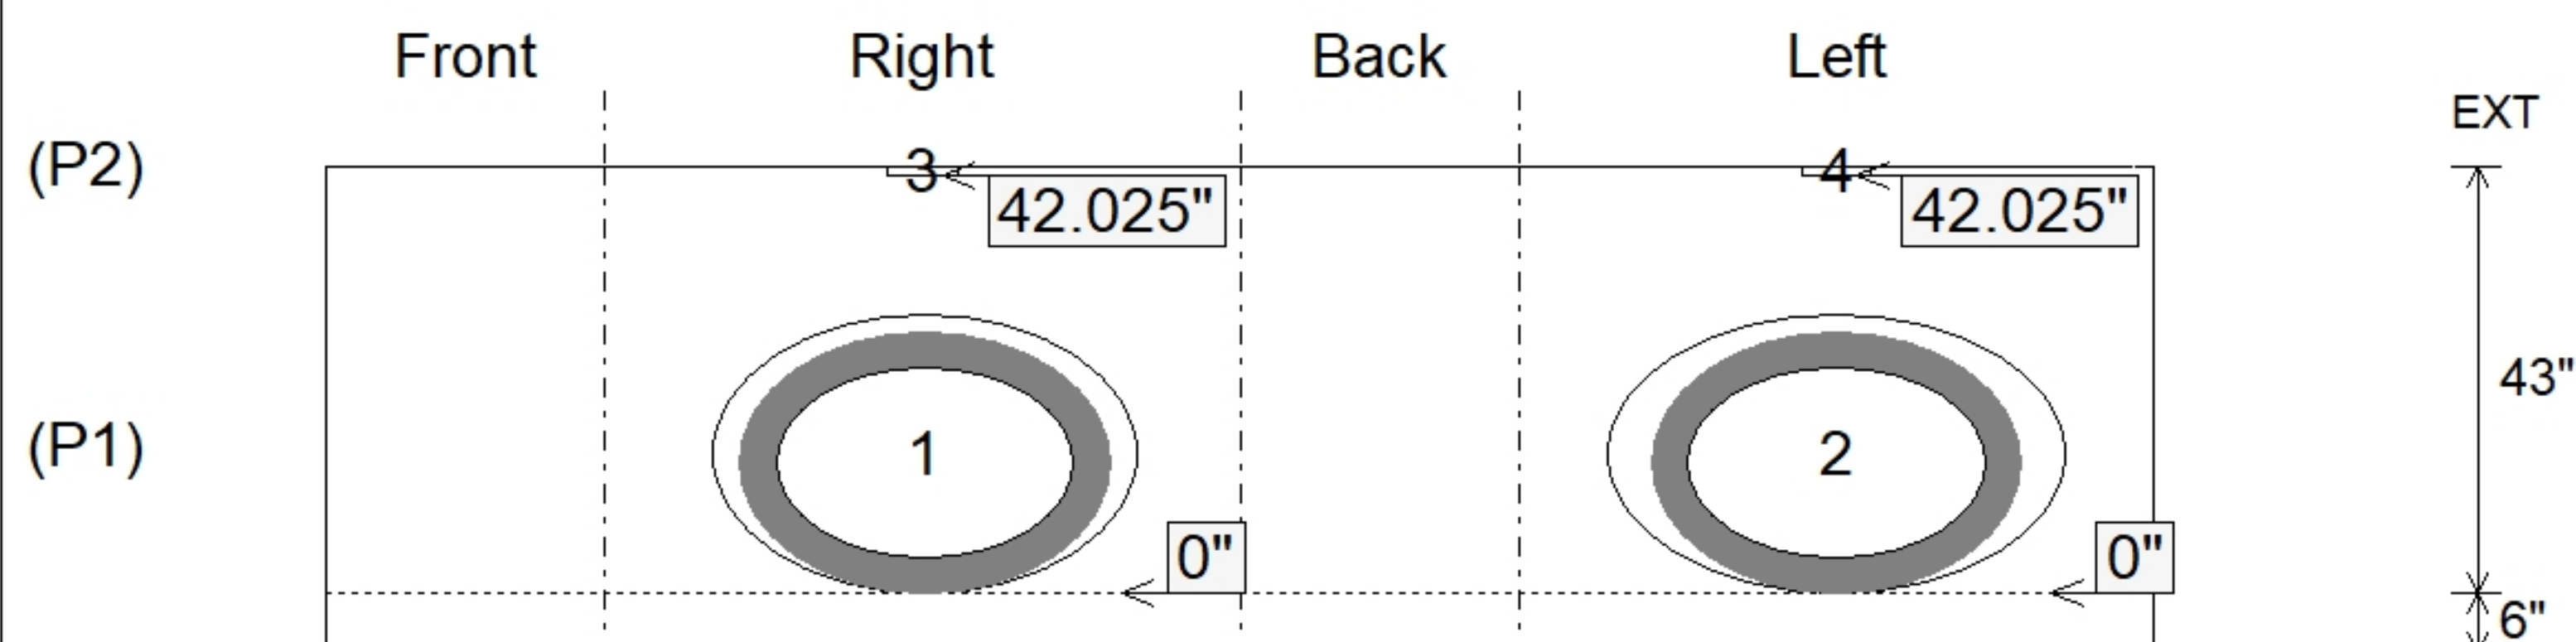

Submittal Drawing
6/16/2026 9:05:47 AM

SUBMITTAL
APPROVED BY:
