

Contractor: Hayes Pipe Supply

Plant: 100




Slack: 0.8"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 28" x 28" - CASTING HEIGHT - 7.50"
P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht - 35"
1) 28" x 28" - Conseal CS-102 1.00"
2) Hole - 26
1) Hole - 16



0 lb
2566 lb
0 lb
0 lb
0 lb

Structure Total: 2566 lb

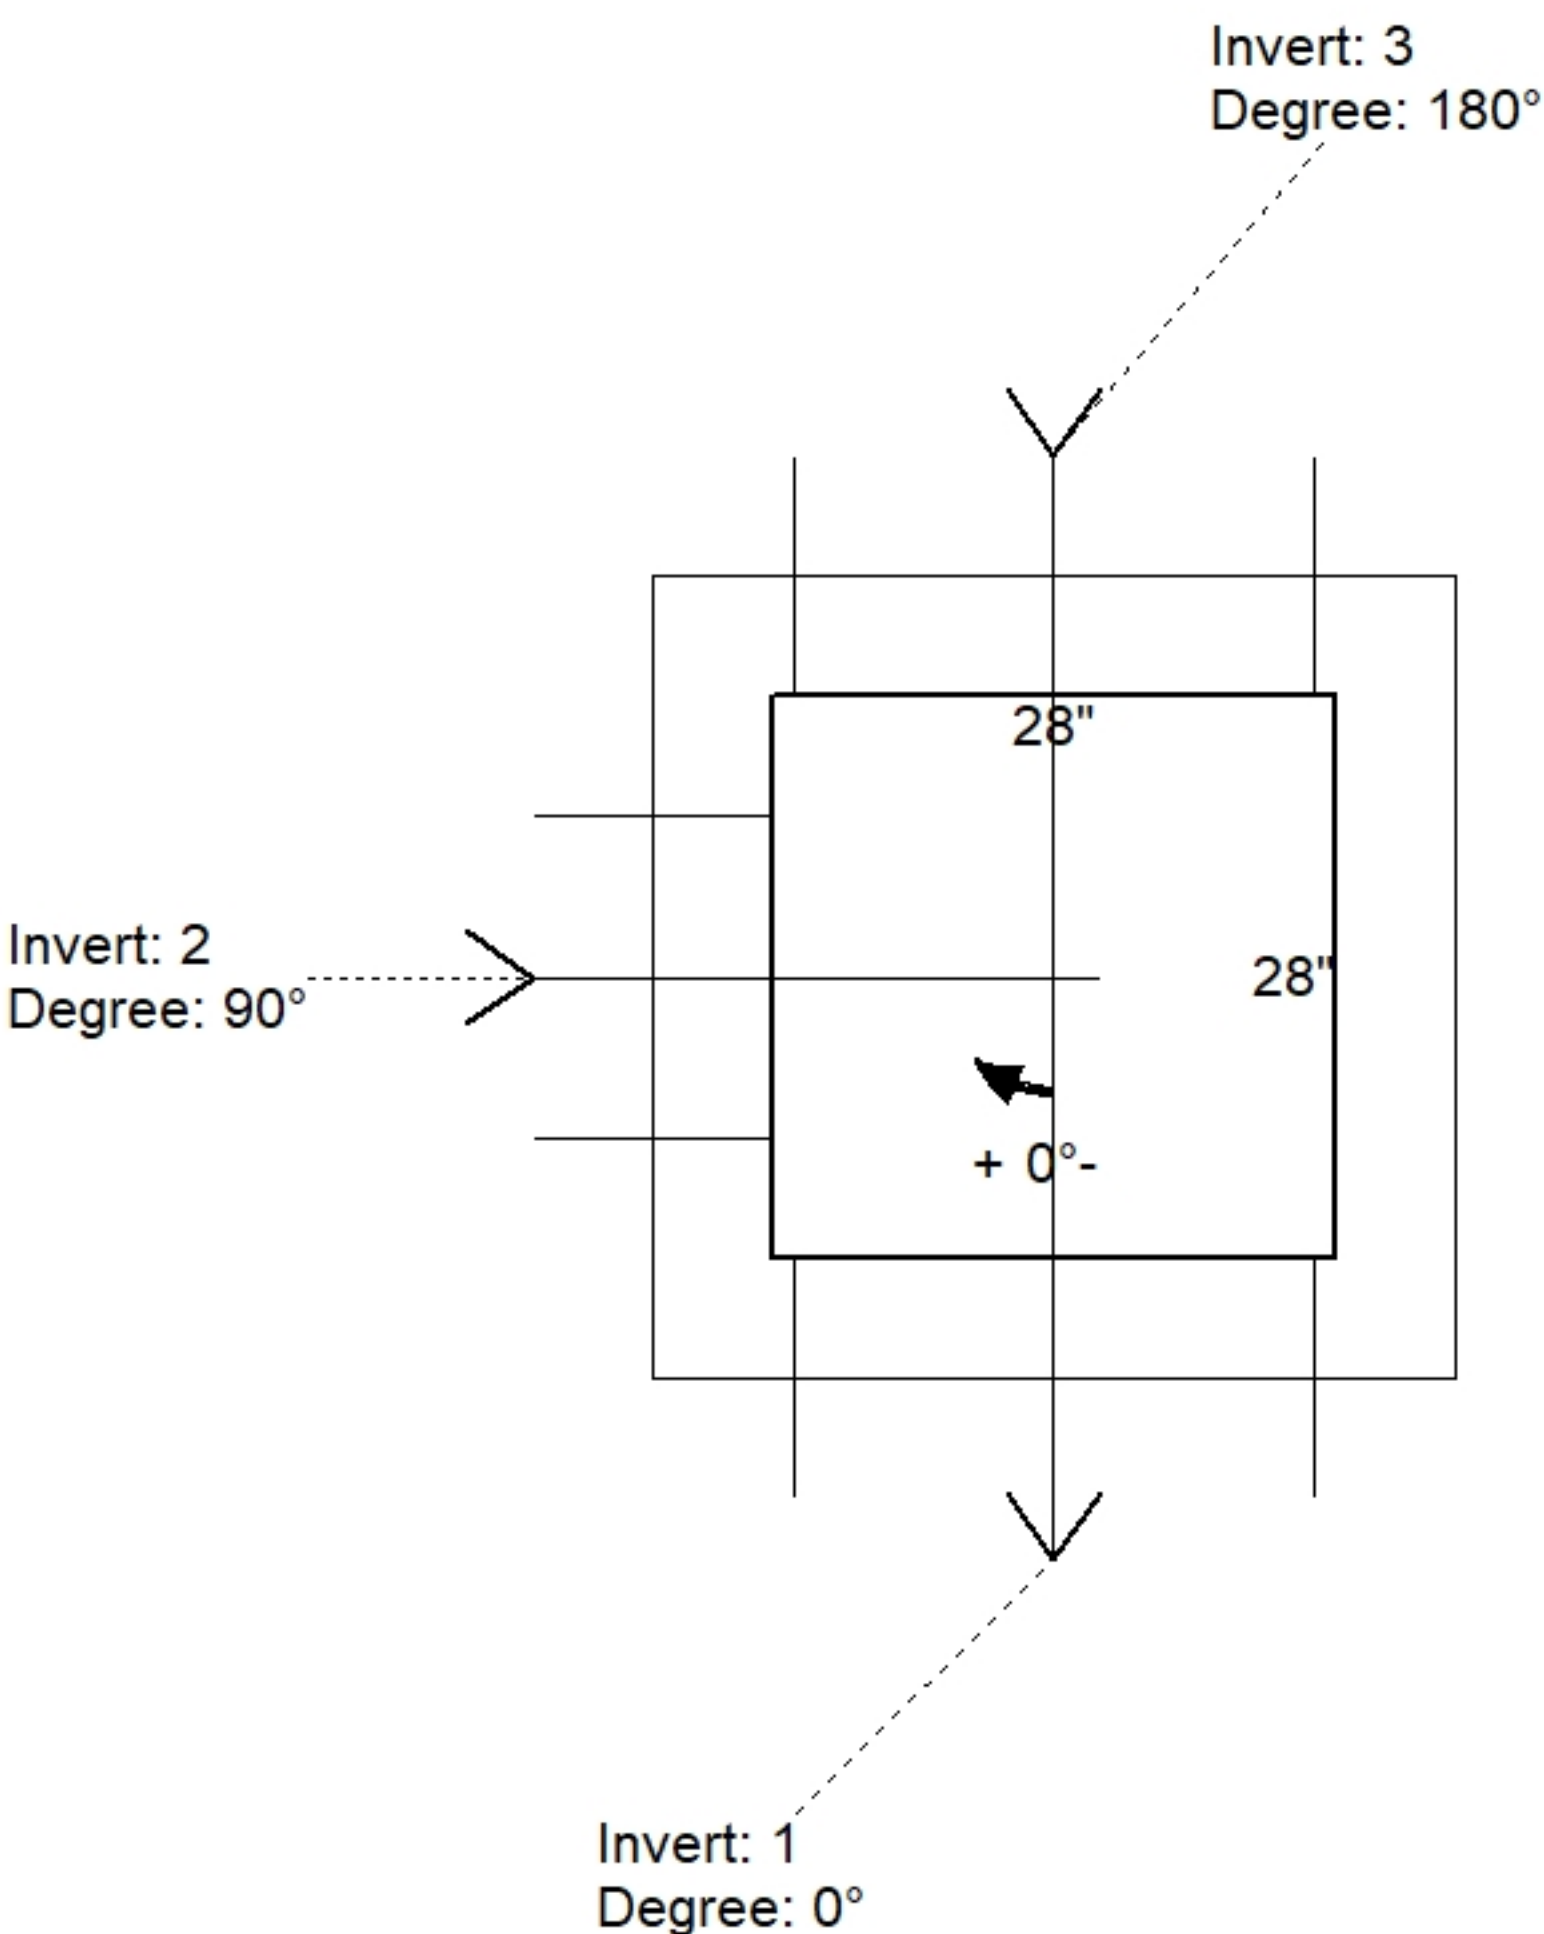

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	423.35'							
Reducer								
Invert 1	419.95'	0°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2	419.95'	90°	12" HDPE	14.5"	16"	Hole 16	1.25"	P1
Invert 3	419.95'	180°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

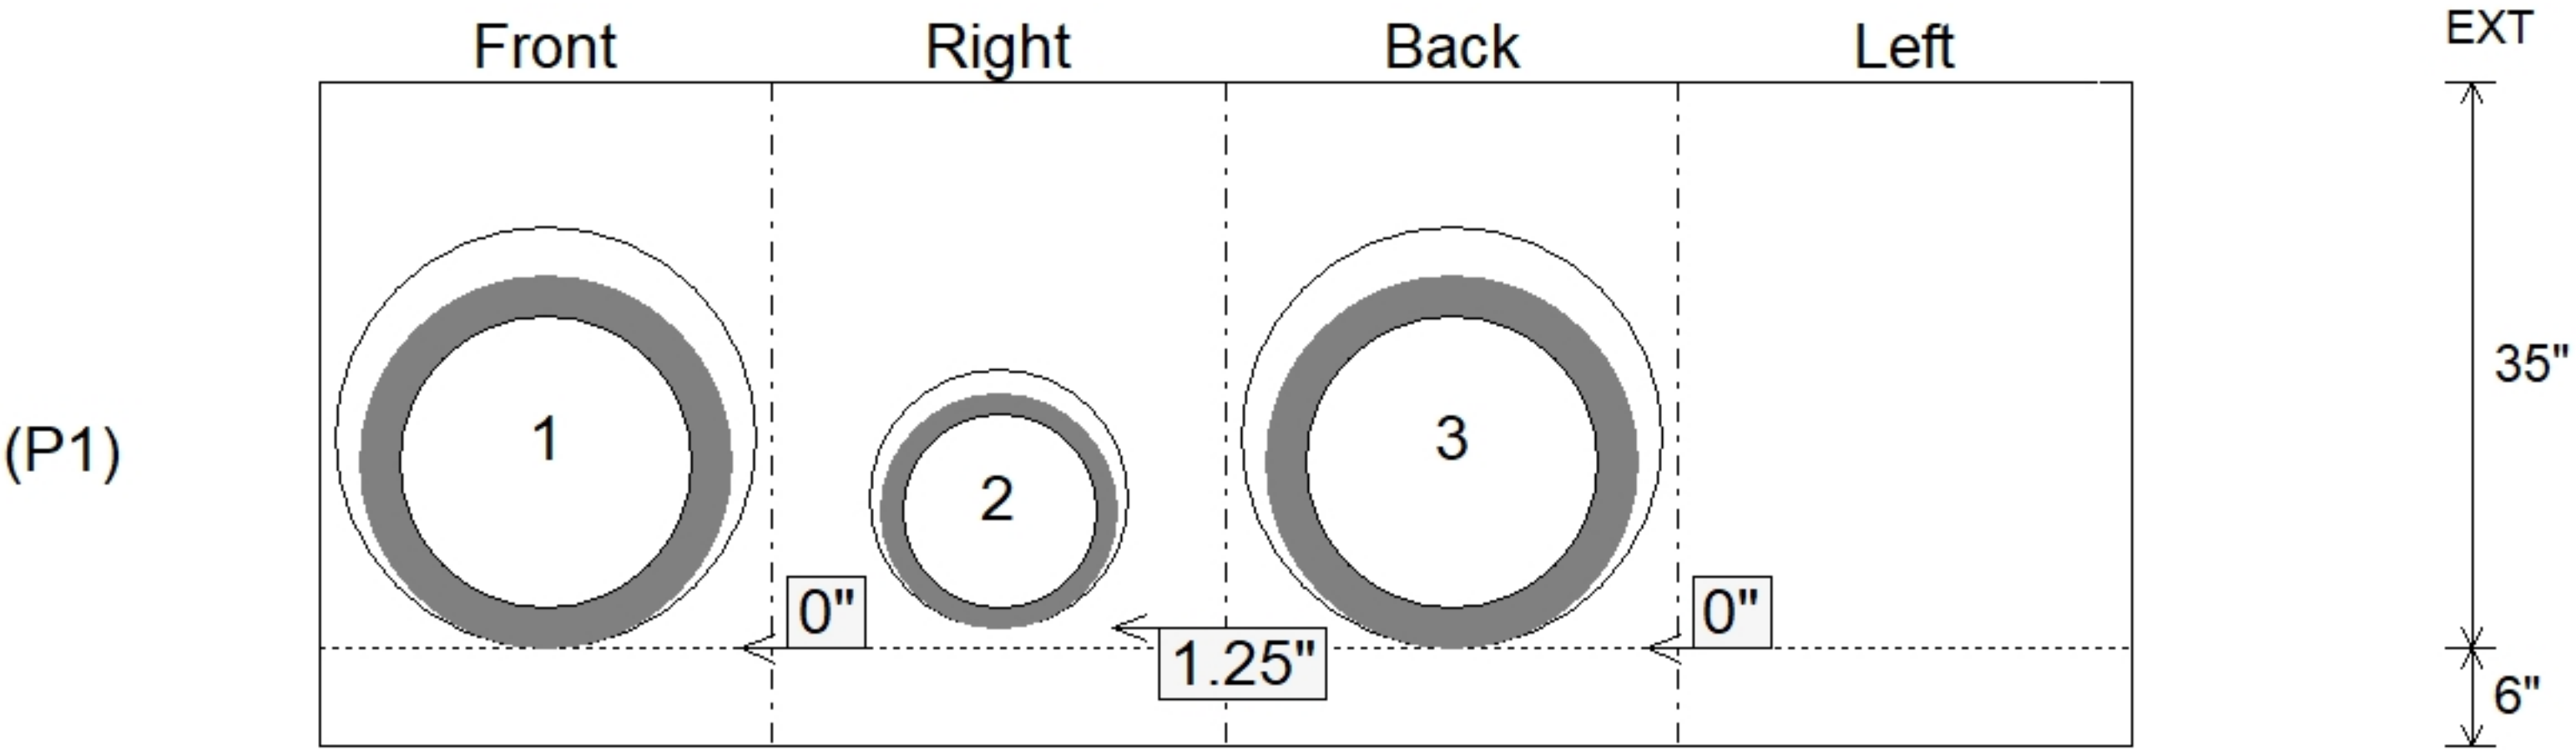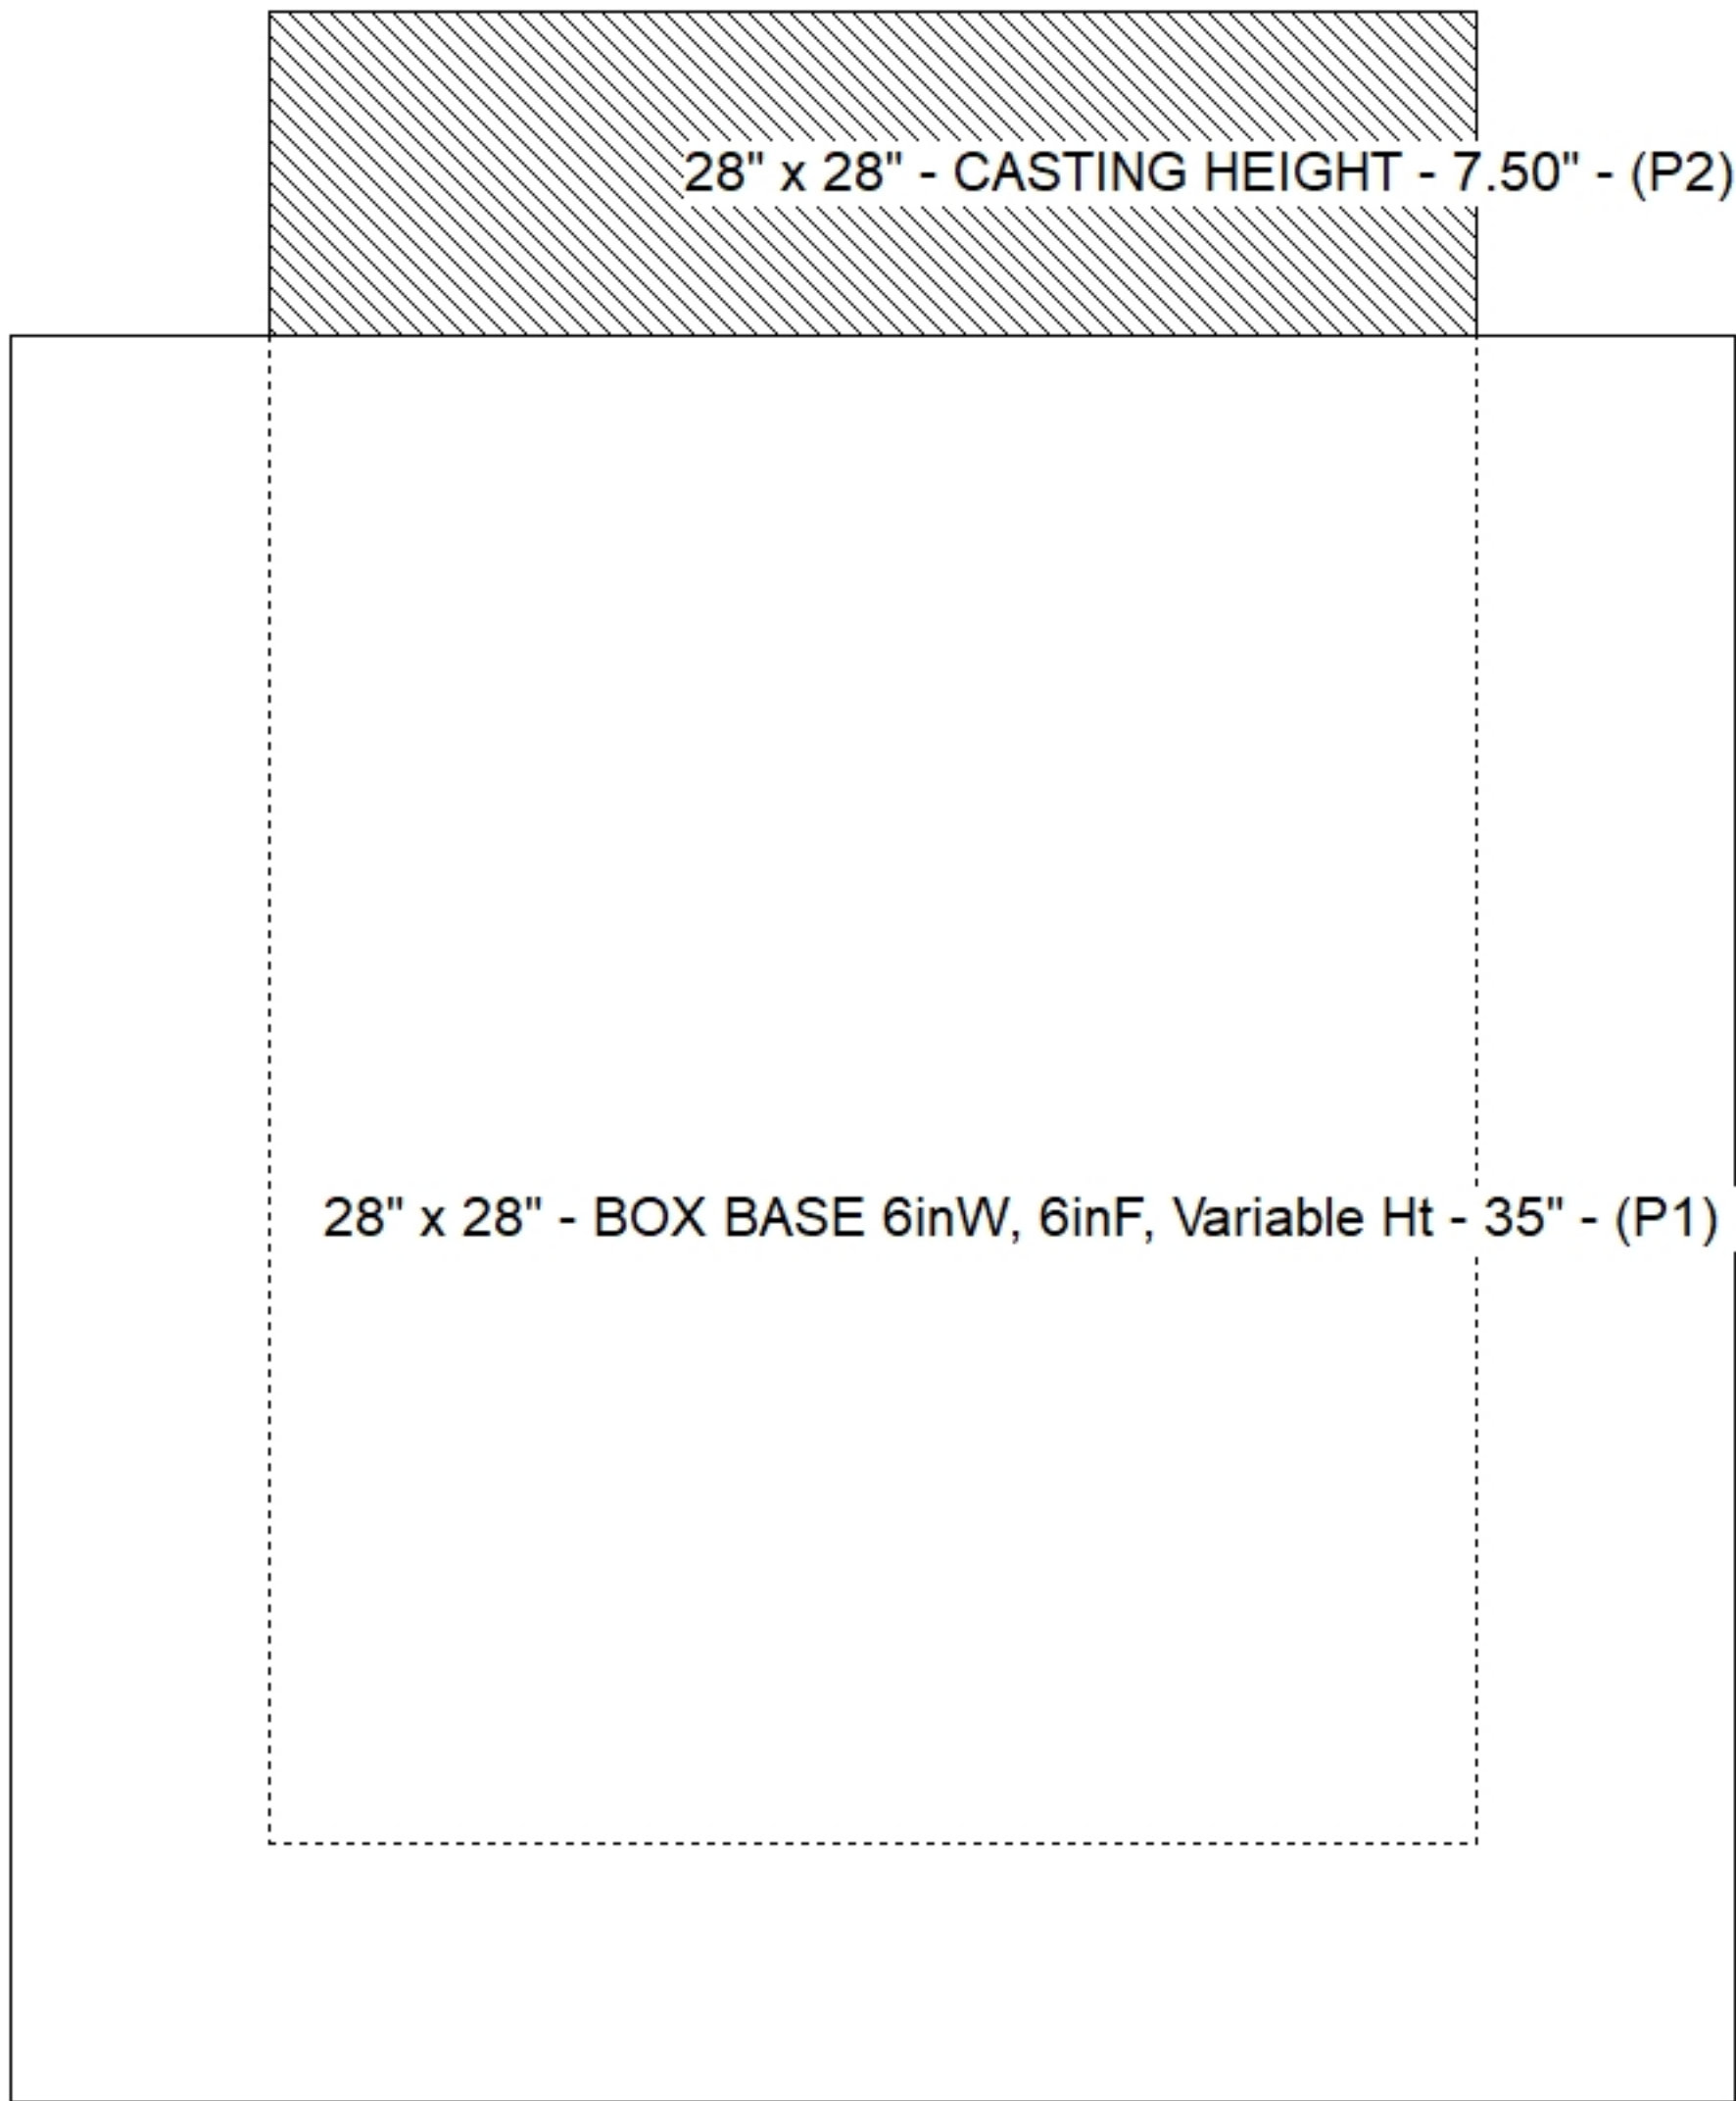

Submittal Drawing
6/16/2026 9:05:49 AM

SUBMITTAL
APPROVED BY:
