

Contractor: Hayes Pipe Supply

Plant: 100




Slack: 0.636"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 28" x 28" - CASTING HEIGHT - 7.50"
P2) 28" x 28" - BOX RISER 6inW, Variable Ht - 15"
P1) 28" x 28" - BOX BASE 6inW, 6inF - 48"
2) 28" x 28" - Conseal CS-102 1.00"
1) Hole - 26
1) Hole - 18

0 lb
1027 lb
3697 lb
0 lb
0 lb
0 lb


Structure Total: 4724 lb

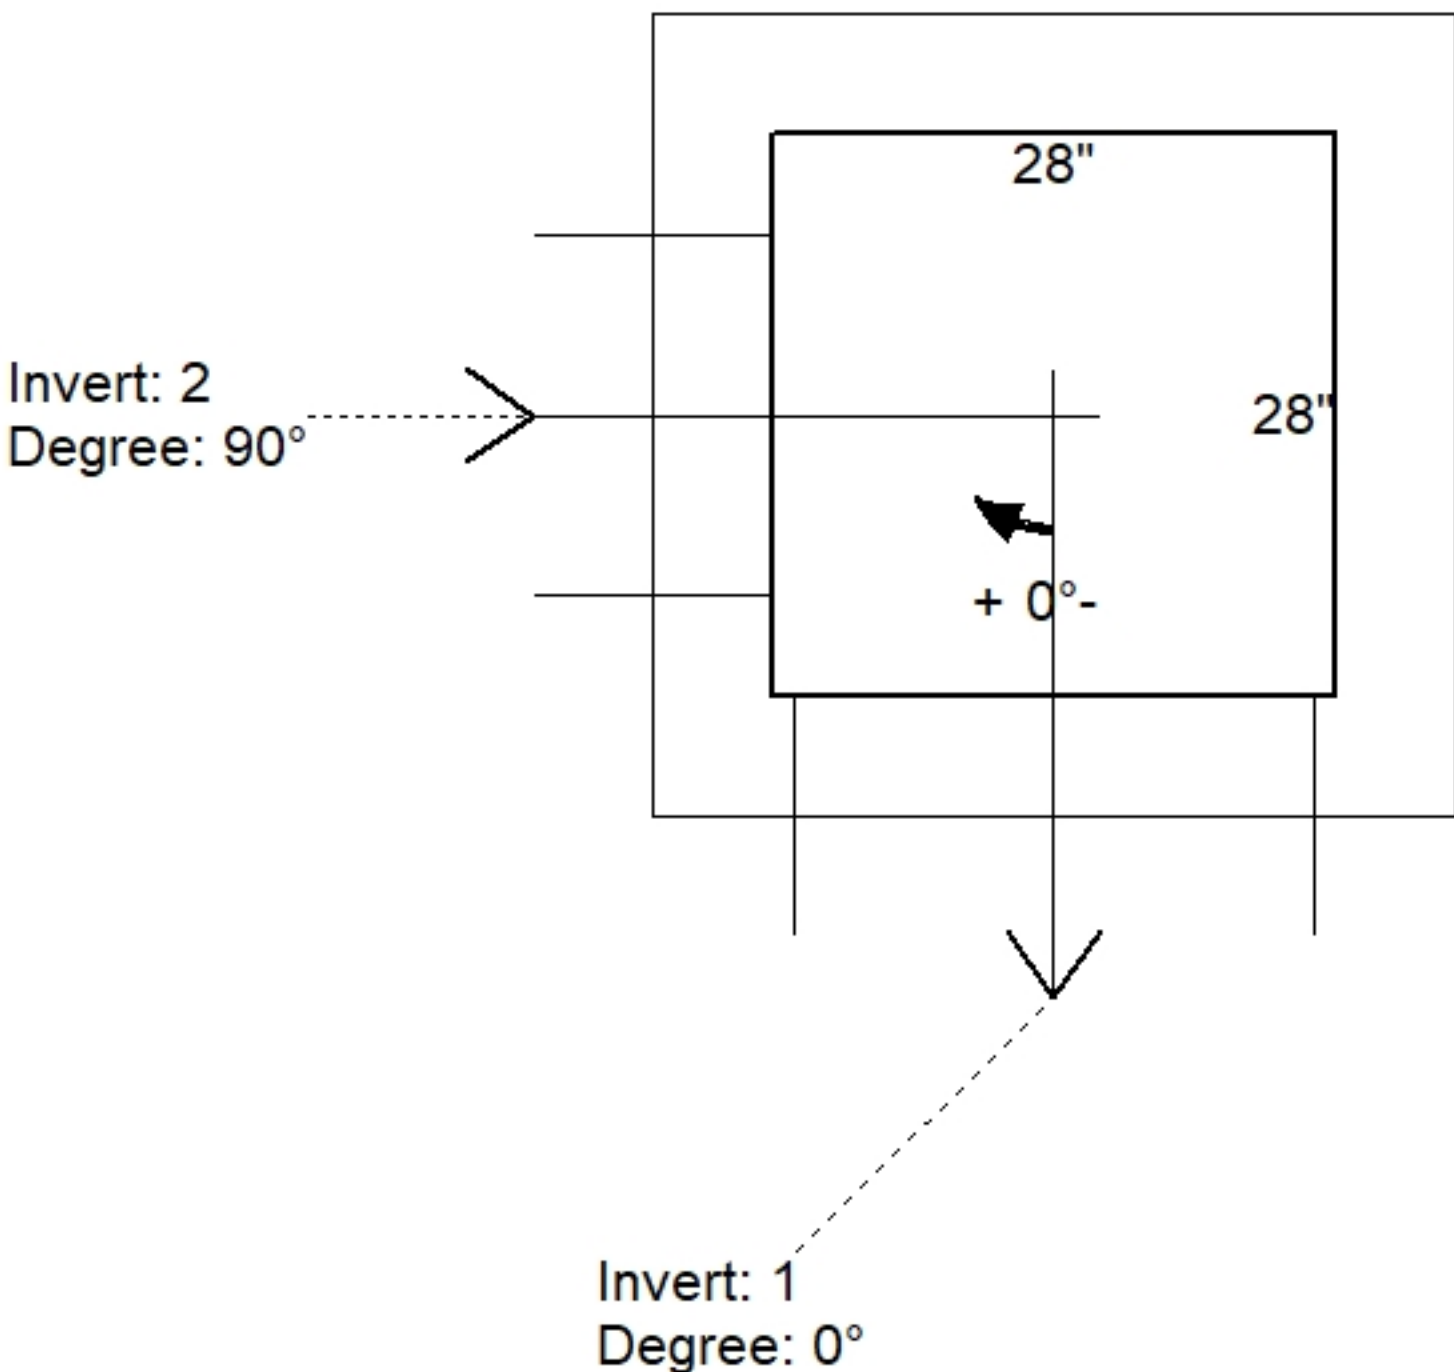

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	426.99'							
Reducer								
Invert 1	421.27'	0°	18" RCP B WALL	23"	26"	Hole 26	-0.004"	P1
Invert 2	421.37'	90°	12" HDPE	14.5"	18"	Hole 18	2.446"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

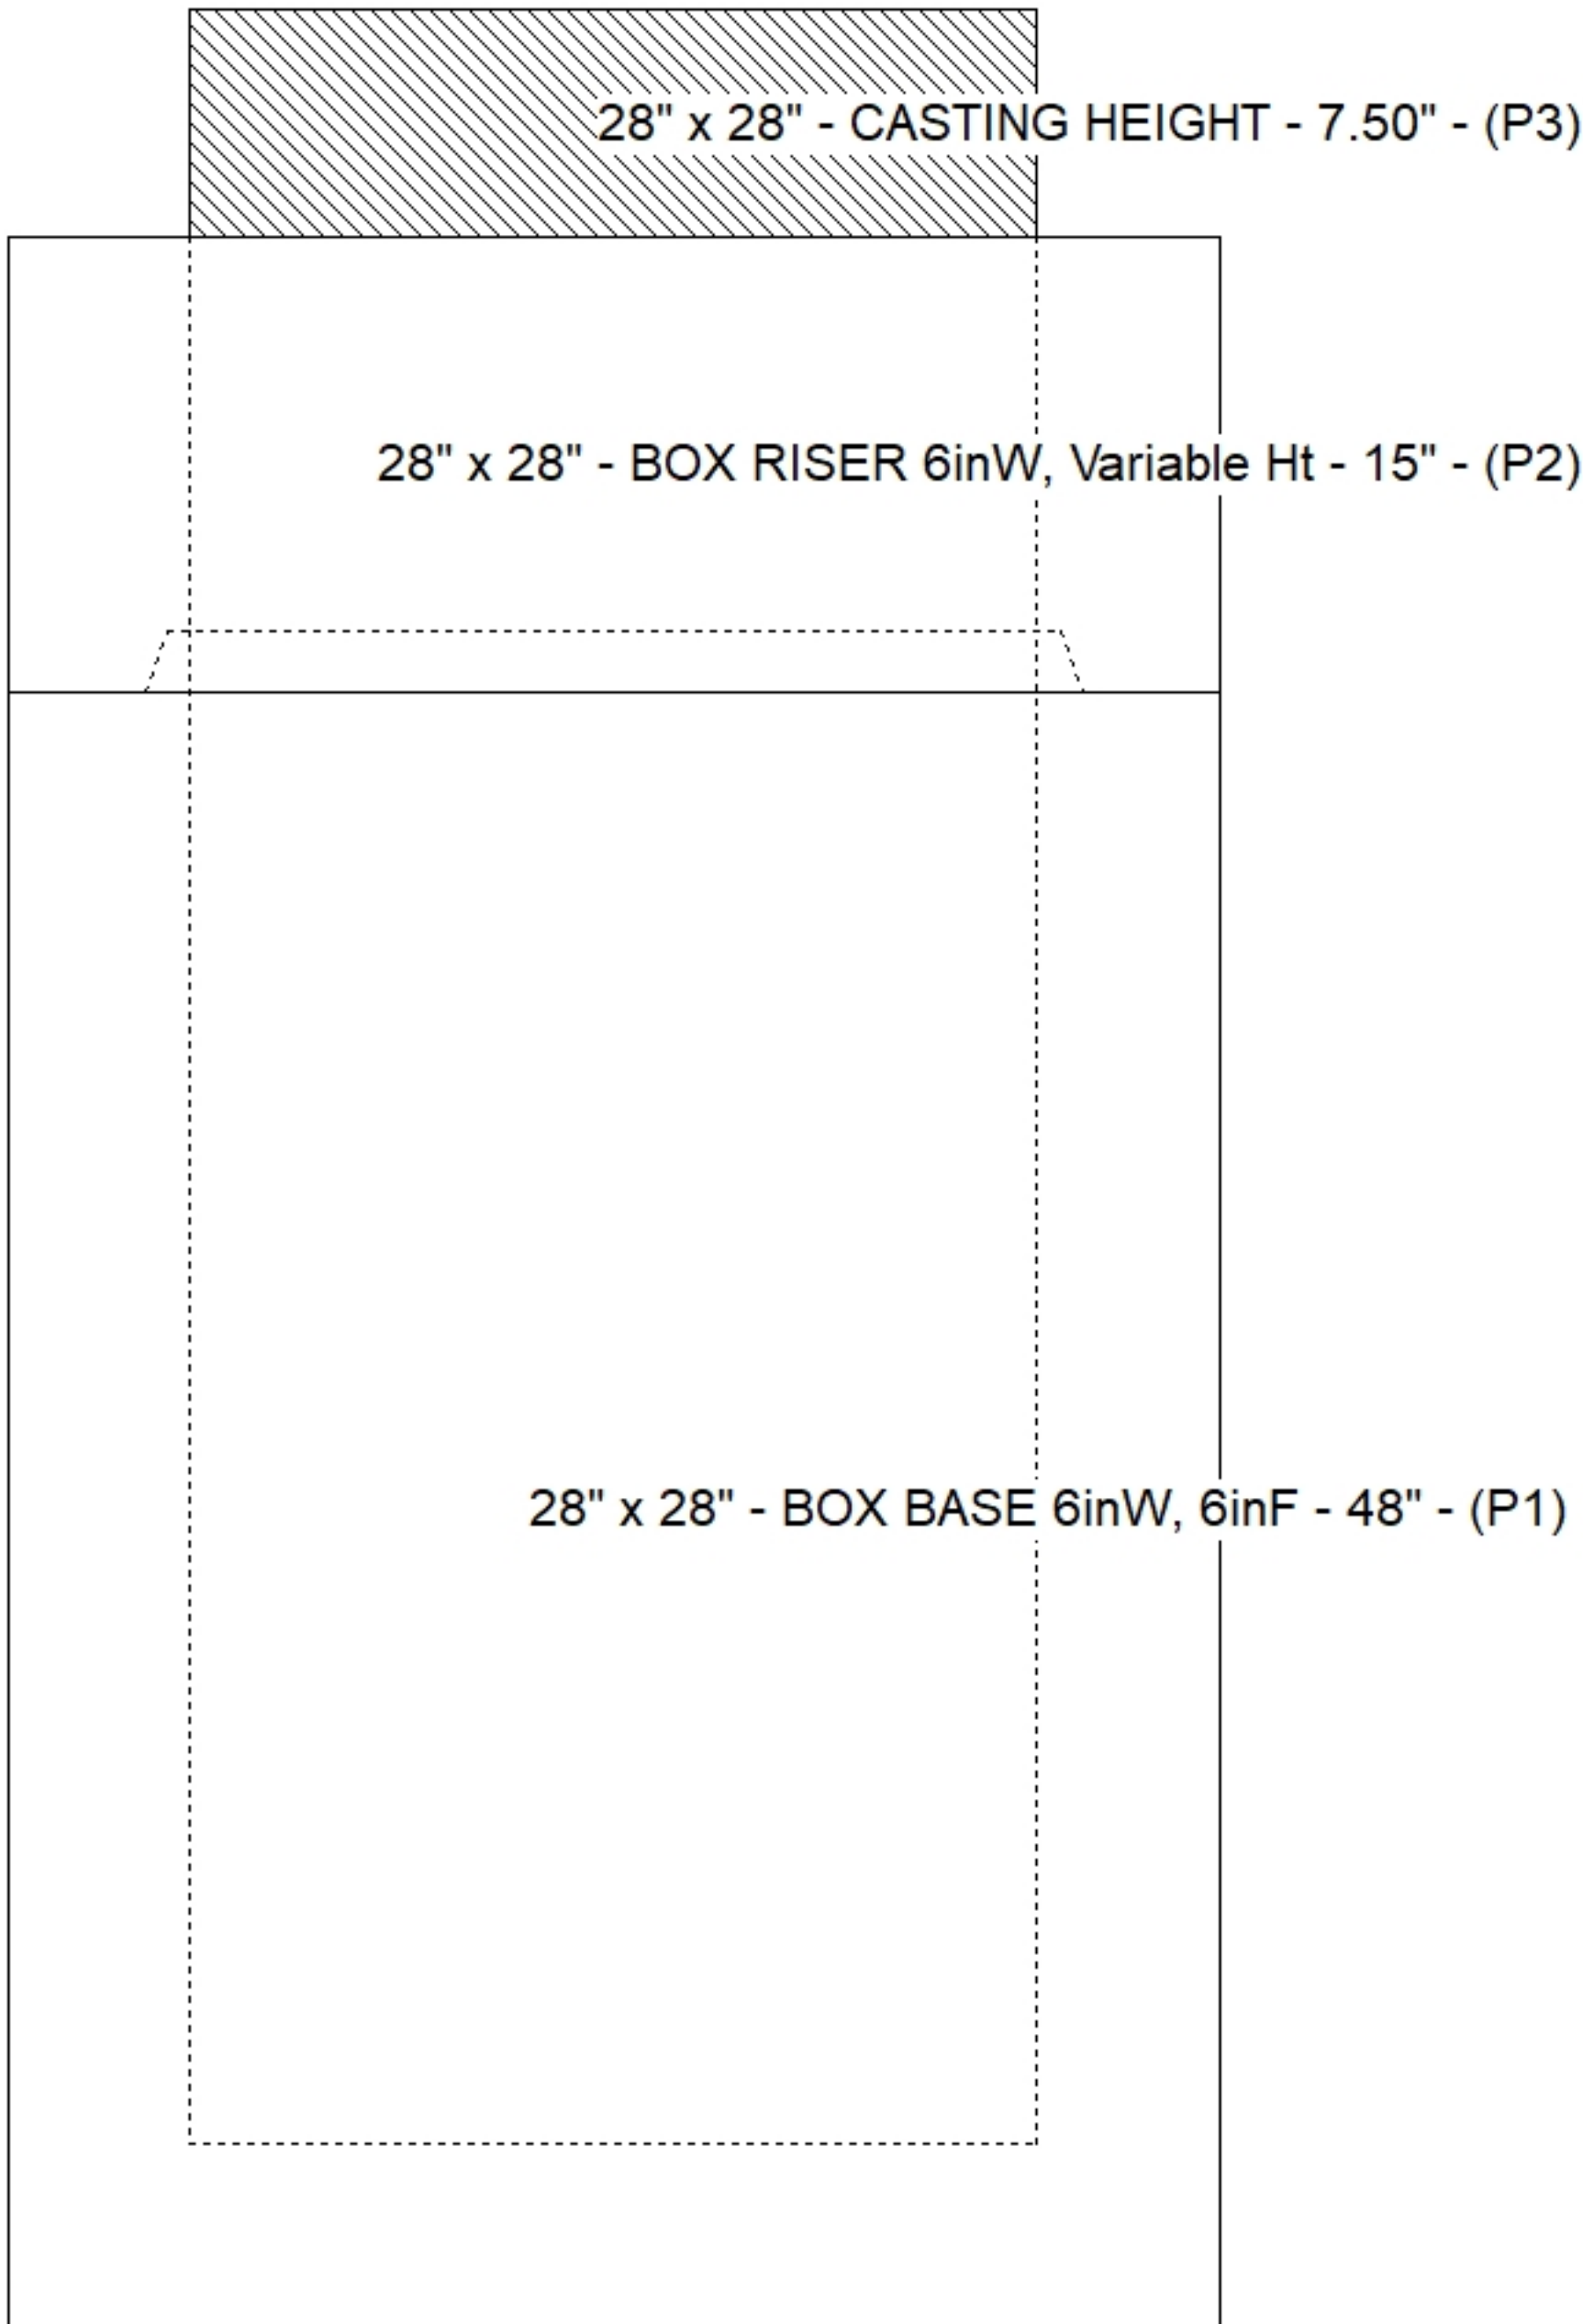

Default - Interior Dimensions

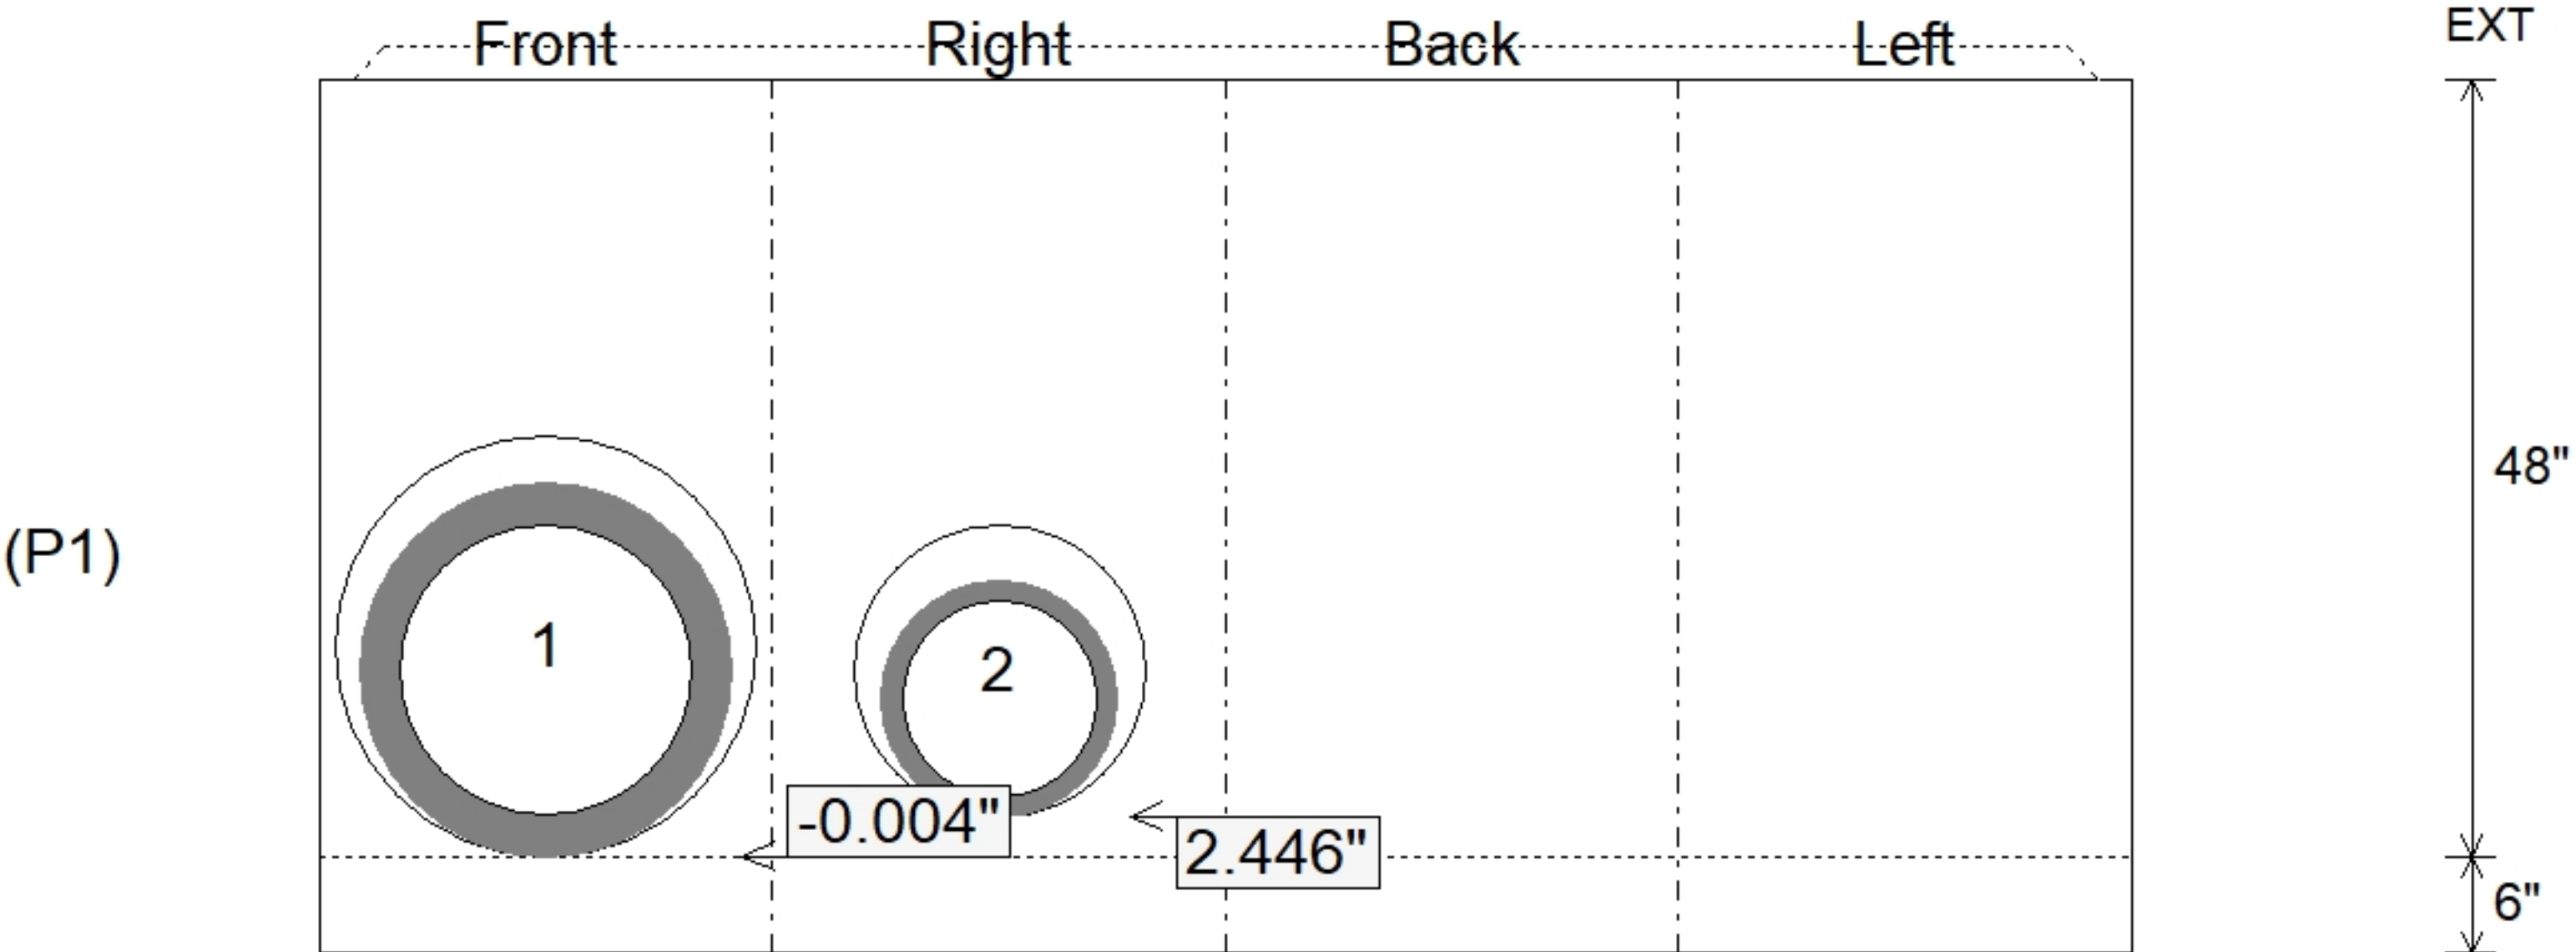

Submittal Drawing
6/16/2026 9:05:49 AM

SUBMITTAL
APPROVED BY:
