



Job Name: 26-2310 - 3rd & Madison Townhomes - Ph. 1 Job Location: Nashville, TN 37208 Contractor: Hayes Pipe Supply				Plant: 100 6/15/2026 10:58:57 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: B1 ST-CB										
P1 BX2828-06BA48				BOX BASE 6inW, 6inF T/n						
P3) 28" x 28" - CASTING HEIGHT - 6" P2) 28" x 28" - BOX RISER 6inW F/G - 12" P1) 28" x 28" - BOX BASE 6inW, 6inF T/n - 48" 2) 28" x 28" - Conseal CS-102 1.00" 1) Hole - 16 1) Hole - 14				0 lb 822 lb 3913 lb 0 lb 0 lb 0 lb ----- Structure Total: 4735 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING SUPPLIED BY OTHERS (JBS 4300 F/G). . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 427.47' Rim to Invert: 5.56' Slack: 1.97' Sump: 1.25' Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	421.91'	0°	20"	12" HDPE	14.5"	Hole 16	16"	16"	0"	0"
Invert 2	422'	180°	20"	10" HDPE	11.4"	Hole 14	14"	14"	1.625"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

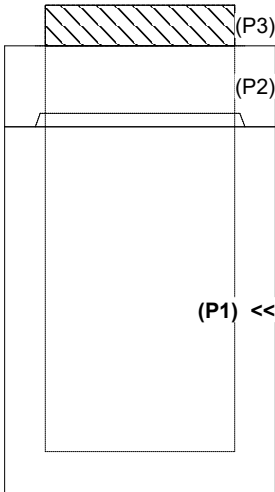


(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

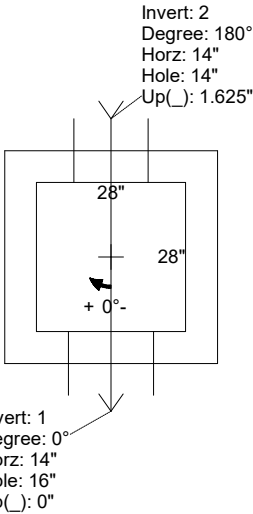

UPSIDE-DOWN VIEW (int. dimensions)

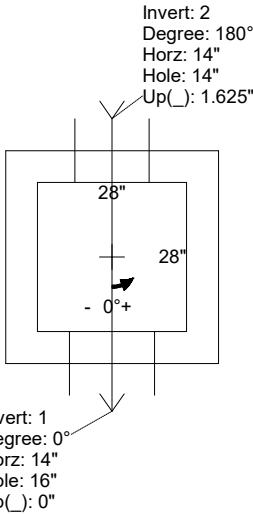

INSIDE WALL DIMENSIONS

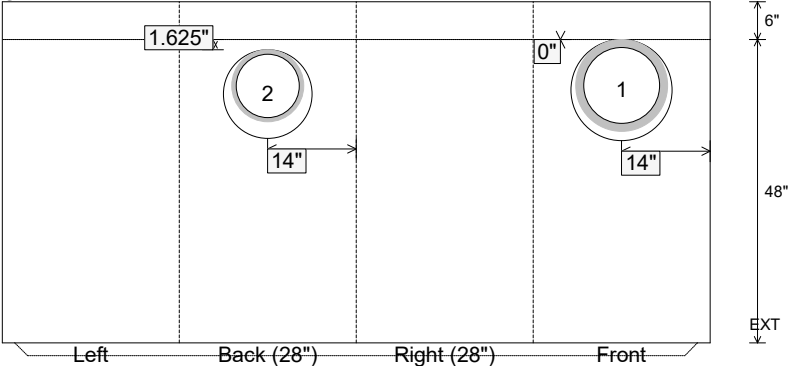

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 6"	Height (Int): 48" Height (Ext): 54"	Weight (Net): 3913 lb Volume (Net): 1cu.yd
----------------------------------	---------------------------------	--	--	---
