



Job Name: 26-2310 - 3rd & Madison Townhomes - Ph. 1 Job Location: Nashville, TN 37208 Contractor: Hayes Pipe Supply				Plant: 100 6/15/2026 10:58:59 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: B3 ST-CB										
P1 BX28280606VH				BOX BASE 6inW, 6inF, Variable Ht T/n						
P3) 28" x 28" - CASTING HEIGHT - 6" P2) 28" x 28" - BOX RISER 6inW F/G - 24" P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht T/n - 33" 2) 28" x 28" - Conseal CS-102 1.00" 1) Hole - 14"						0 lb 1643 lb 2988 lb 0 lb 0 lb ----- 0 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING SUPPLIED BY OTHERS (JBS 4300 F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 428.12' Rim to Invert: 5.26' Slack: 0.876" Sump: 0.756" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	422.86'	0°	20"	10" HDPE	11.4"	Hole 14	14"	14"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)




Invert: 1
Degree: 0°
Horz: 14"
Hole: 14"
Up(): 0"

UPSIDE-DOWN VIEW (int. dimensions)




Invert: 1
Degree: 0°
Horz: 14"
Hole: 14"
Up(): 0"

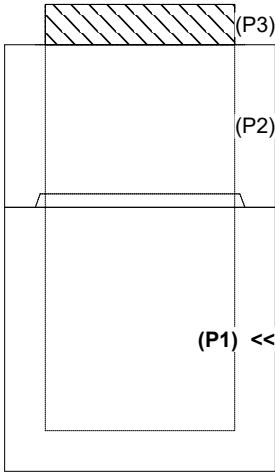

(P1) <<

INSIDE WALL DIMENSIONS

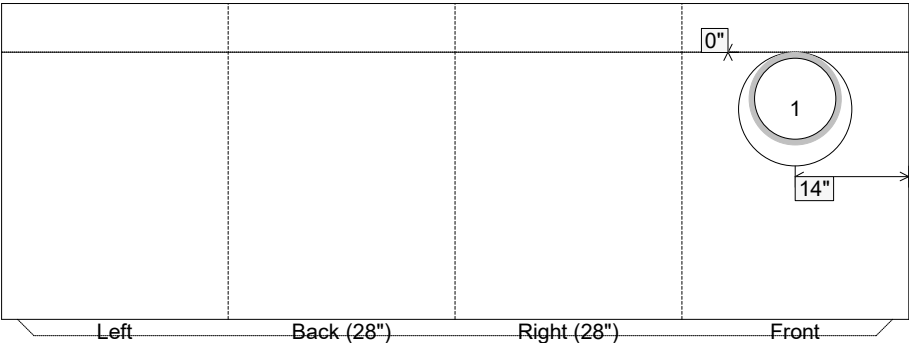

(P1)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 6"	Height (Int): 33" Height (Ext): 39"	Weight (Net): 2988 lb Volume (Net): 0.76cu.yd
----------------------------------	---------------------------------	--	--	--
